

Massachusetts School Building Authority

CAPITAL PLANNING PROJECT OVERVIEW REPORT

November 20, 2019

TABLE OF CONTENTS

Capital Pipeline Overview	2-3
Statements of Interest (SOIs)	4
Core Program	5-17
Eligibility Period	5
Consultant Selection	6-7
Feasibility Study	8
Schematic Design	9
Commissioning	10
Design Development	11
Summary of Bid Data	12-13
Construction	14-15
Closeout	16
Accelerated Repair Program	17-22
Project Variances	23-24

Appendices

(A) Project Status List

(B) 2018-21 Estimated Bid Dates

(C) School Construction Costs compared to Common Economic Indicators


(D) Construction Status Report

(E) FY19 Projects Substantially Complete

CAPITAL PIPELINE OVERVIEW

Status of Current Projects

A total of 312 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the Massachusetts School Building Authority (“MSBA”) are currently in the MSBA’s Eligibility Period and Capital Pipeline. The summary chart provides the number of projects in Eligibility Period and each phase of the Capital Pipeline. For a detailed look at the Capital Pipeline projects, please go to www.massschoolbuildings.org/building and select “Capital Pipeline Status Chart”.

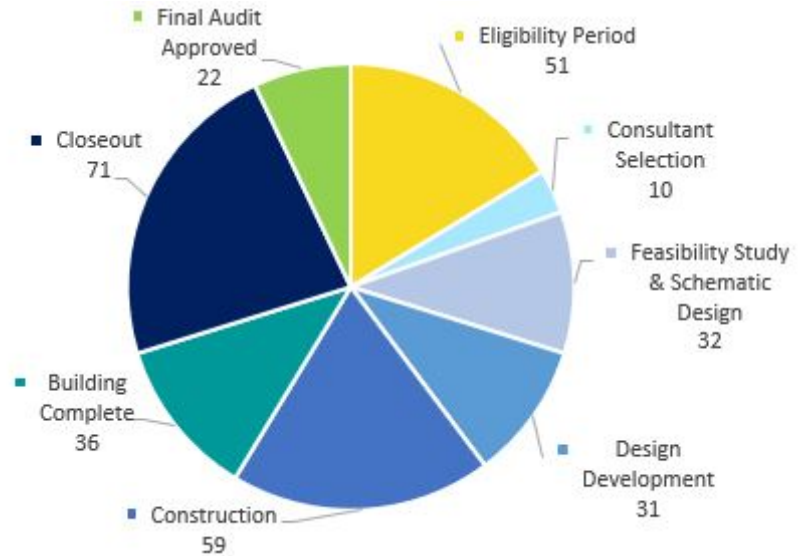

Capital Planning Updates:

The following activities are scheduled for FY 2020:

- Model School Program update – RFQ posted on July 31, 2019 with 5 responses received on October 31, 2019. MSBA review is currently underway.
- Procurements for commissioning services, technical review services, and school survey services are anticipated in the second half of FY 2020.
- 2019 Core Statements of Interest (“SOI”) recommendations anticipated for the December 2019 Board of Directors meeting.
- Consultants are currently reviewing costs, enrollment, and recommendations for a post-occupancy program anticipated at the February 2020 Board of Directors meeting.
- MSBA Roundtables – Recent/Upcoming dates for 2019 are listed below:
 - Commissioning Roundtable held on November 7, 2019
 - “Planning for Operation and Maintenance of New Schools”
 - Contractor Roundtable December 4, 2019
 - “Challenges and Solutions on Addition and Renovation Projects”
- MSBA Staff presentations to district officials and consultant teams regarding the requirements for the 2019 Accelerated Repair Program Invitees were held on November 6, 2019 and November 22, 2019.
- Please see Exhibit E for a summary of MSBA-funded projects that achieved substantial completion between June 30, 2018 and July 1, 2019 (FY 19). A total of 14 schools were completed including nine elementary schools, two middle schools, two high schools, and one vocational school. The project teams for these 14 schools included 12 OPM firms, 13 Designer firms, and 11 contractors. Please see Exhibit E for additional information.

2019 Progress Report

- * Statements of Interest (“SOI”) 2019
 - o The 2019 SOI submittal period opened on January 4, 2019. The deadline to file for consideration in the Accelerated Repair Program (“ARP”) was Friday, February 15, 2019. 83 ARP SOIs were reviewed and recommendations for invitations for 27 Districts and 42 schools were authorized at the June 26, 2019 Board meeting. The deadline to file for consideration in the Core Program was Friday, April 12, 2019. The MSBA has reviewed the 61 SOIs submitted for the Core Program and Further Review Recommendations that were presented at the May 31, 2019 Board meeting. Staff anticipates presenting recommendations for invitation into Eligibility Period at the December 11, 2019 Board meeting.
- * Statements of Interest (“SOI”) 2020
 - o The 2020 SOI submittal period is scheduled to open on Wednesday, January 8, 2020. The deadline to file for consideration in the ARP is Friday, February 14, 2020. The deadline to file for consideration in the Core Program is Wednesday, April 8, 2020.
- * Eligibility Period – Core Program
 - o There are nine districts currently in the Eligibility Period for the Core Program.
 - o For the 2018 SOIs, one SOI will be recommended for an Invitation to Feasibility Study at the December 2019 Board meeting.
 - o The eight remaining 2018 SOIs will be recommended for Invitations to Feasibility Study by the end of fiscal year 2020.
- * Feasibility Study/Schematic Design – Core Program
 - o Two districts completed their Owner’s Project Manager (“OPM”) Selections. Four districts are tentatively scheduled to receive MSBA approval for selection of their OPM.
 - o Four districts completed their Designer Selections and six districts are in the process of procuring a Designer.
 - o Three districts are anticipating submittals for their Preferred Schematic Solutions between February 2020 and April 2020.
 - o Three districts are anticipating submittals for their Project Funding Agreements between February 2020 and April 2020.
- * ARP
 - o 26 of the 27 districts from the 2019 ARP invitations have received consultant assignments. The remaining one district has requested to be removed from the Accelerated Repair Program at the December 2019 Board meeting.
- Construction Costs – Core Program
 - o In 2019, MSBA staff anticipates sub-bids for 22 projects with DBB bids or GMP executions for 20 of the 22 projects. The remaining 2 projects are anticipated to have DBB bids or GMP executions in 2020.
 - o In 2020, MSBA staff anticipates sub-bids for 15 projects with GMP executions and DBB bids for the 15 projects in 2020.
- * Substantial Completion – Core Program
 - o Of the thirteen projects scheduled to reach substantial completion in 2019, eleven have provided their substantial completion certificates.

STATEMENTS OF INTEREST (SOIs)

2019 SOI Process

The 2019 SOI submittal period opened on January 4, 2019. The deadline to file SOIs for consideration into the ARP, which is primarily for the replacement of roofs, windows/doors, and/or boilers in an otherwise structurally sound facility, was Friday, February 15, 2019. The MSBA reviewed the 83 SOIs submitted for the ARP and presented initial recommendations for invitation at the June 5th Facilities Assessment Subcommittee meeting. At the June 26, 2019 Board meeting, the Board of Directors approved the invitations for 27 districts representing 42 schools into the ARP.

The deadline to file SOIs for consideration into the Core Program, which is primarily for projects beyond the scope of ARP, including extensive repairs, renovations, additions/renovations, and new school construction, was Friday, April 12, 2019. The MSBA has reviewed the 61 SOIs that were submitted for the Core Program and the Further Review Recommendations that were presented at the May 31, 2019 Board meeting. Staff anticipates presenting recommendations for invitation into Eligibility Period at the December 11, 2019 Board meeting.

The table below lists the number of SOIs received and Invitations granted for the calendar years 2008 through 2019. Please note, the data for calendar year 2019 is under development.

Year	Total Number of SOIs Submitted	Number of CORE Program SOIs Submitted	Number of CORE Program Invitations	Number of Green Repair or Accelerated Repair Program SOIs Submitted	Number of Green Repair or Accelerated Program Repair Invitations	Number of SCILAB SOIs Submitted	Number of SCILAB Program Invitations
2008	431	425	104	6	6		
2009	237	206	41	31	31		
2010	224	202	19	22	22		
2011	371	184	18	187	149		
2012	280	198	11	69	36	13	11
2013	201	123	17	78	47		
2014	229	110	18	119	51		
2015	158	97	26	61	44		
2016	156	89	17	67	49		
2017	156	83	15	73	36		
2018	130	70	12	60	34		
2019	144	61	TBD	83	42		

2008: The MSBA launched the annual filing period.

2011: The MSBA opened the annual filing period twice, which included a dedicated opening for interest in the Green Repair Program and the annual opening.

2012: The MSBA’s annual filing period captures interest in the newly created Accelerated Repair Program, the 2012 Science Laboratory Initiative and the Core Program.

CORE PROGRAM

ELIGIBILITY PERIOD

There are nine districts in the Eligibility Period and four of those districts have secured their local funding.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA’s online enrollment projection tool. All districts in Eligibility Period have completed their online enrollment projection information.

District	School	Eligibility Period Commencement Date	30 days	60 days	90 days		180 days		270 days	Date of Invitation to Feasibility Study (Estimated)
			ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	
Fitchburg*	Crocker Elementary	6/26/19	X	X	X	X	X		X	February 2020
Westfield	Franklin Avenue ES	5/1/19	X	X	X	X	X	X	X	December 2019
Norwood	Dr. Philip O. Coakley MS	5/1/19	X	X	X	X	X		X	TBD
Brookline	John R. Pierce School	6/3/19	X	X	X	X			X	TBD
Haverhill	Dr. Albert B. Consentino School	6/3/19	X	X	X	X				TBD
Tyngsborough	Tyngsborough MS	6/3/19	X	X	X	X	X			TBD
Revere	Revere HS	7/1/19	X	X	X	X	X			TBD
Spencer East-Brookfield RSD	David Prouty HS	7/1/19	X	X	X	X				TBD
Webster	Bartlett HS	7/1/19	X	X	X	X	X			February 2020

*Fitchburg was re-categorized from the Invitation to Feasibility Study category to the Eligibility Period category at the June 26, 2019 Board meeting to re-evaluate the agreed-upon enrollment.

CONSULTANT SELECTION

Owner’s Project Manager (“OPM”) Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an OPM. Since the last report, two districts have completed their OPM selections (shaded in the table below). Currently, there are four districts in the Capital Pipeline that are in the process of procuring an OPM.

District	School	Anticipated Selection
Bristol Plymouth	Bristol Plymouth Voc Tech	November 2019
Greater Fall River	Diman RVTHS	November 2019
Walpole	Bird MS	February 2020
Hull	Memorial MS	March 2020
Peabody	Welch ES	March 2020
Stoneham	Stoneham HS	April 2020

Designer Selection

After a district has selected and executed a contract with an OPM, the district selects a Designer by utilizing either a local designer selection process for projects under \$5 million or the MSBA’s Designer Selection Panel (“DSP”) for projects over \$5 million. Since the last report, four districts have completed their Designer selection (shaded in the table below). There are currently six districts in the Capital Pipeline that are in the process of procuring a Designer.

District	School	Anticipated Selection
Andover	West ES	October 2019
Medfield	Dale Street ES	October 2019
Westwood	Hanlon ES	October 2019
Lawrence	Leahy ES	November 2019
Swampscott	Hadley ES	November 2019/December 2019
Northeast Metro	Northeast Metro	December 2019
Randolph	Lyons ES	December 2019/January 2020
Boston	William G. Carter School	January 2020
Bristol-Plymouth	Bristol Plymouth Voc Tech	January 2020/February 2020
Greater Fall River	Diman RVTHS	February 2020

For additional information on the selected consultant teams, see Appendix A.

FEASIBILITY STUDY

Once a district has procured an OPM and a Designer, the district and the district’s consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that three districts will appear before the Board for their Preferred Schematic Design authorizations at the February 2020 and April 2020 Board meetings.

District	School	Anticipated PS Board Date
Lawrence	Oliver Partnership	February 2020
Worcester	Doherty Memorial HS	February 2020
Boston	Josiah Quincy Upper School	April 2020

SCHEMATIC DESIGN

Prior to consideration by the Board for Project Scope and Budget Agreement authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that three districts will appear before the Board for Project Scope and Budget Agreement authorizations at the February 2020 and April 2020 Board meetings.

District	School	Anticipated PS&B Board Date
Nauset	Nauset RHS	February 2020
Waltham	Waltham HS	February 2020
Orange	Dexter Park	April 2020

COMMISSIONING

The MSBA assigns a Commissioning Consultant after a district has secured local funding for the Board approved project. Since the last report, the MSBA has assigned Commissioning Consultants for three additional projects which are presented in the table below.

District	School	Program	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Amesbury	Amesbury Elementary School	Core	\$48.98	BVH Integrated Services	\$95,248
Bridgewater-Raynham	Mitchell Elementary School	Core	\$64.68	Consulting Engineering Services	\$102,996
West Springfield	Coburn Elementary School	Core	\$54.73	Horizon Engineering Associates	\$98,236

To date, the MSBA has executed 496 Commissioning Consultant contracts, totaling \$37.2 million in commissioning fees for 588 schools. Construction budgets for projects being commissioned total \$11,107,773,621. To date, 349 work orders have been completed.

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced*	Percent Complete
FY10	31	\$4,231,376	\$4,273,277	100%
FY11	95	\$6,132,890	\$6,058,460	99%
FY12	52	\$4,373,944	\$4,386,520	100%
FY13	55	\$3,364,697	\$3,408,897	100%
FY14	47	\$2,604,062	\$2,541,165	98%
FY15	44	\$2,277,711	\$2,271,979	100%
FY16	44	\$3,385,137	\$3,108,854	92%
FY17	37	\$2,290,661	\$1,945,252	85%
FY 18	44	\$4,137,550	\$1,828,113	44%
FY 19	39	\$3,604,720	\$536,561	15%
FY 20	8	\$840,170	\$8,496	1%
Total	496	\$37,242,918	\$30,367,574	

*Includes approved additional services over value of Work Order

DESIGN DEVELOPMENT

After a district has secured local funding and has entered into a Project Funding Agreement (“PFA”) with the MSBA, the district enters into the Design Development Phase. Currently, there are 31 projects in the Design Development Phase with a total estimated construction cost of approximately \$1.63 billion. Of those 31 projects, 13 are ARP Projects and 18 are Core Program Projects. The 18 Core Program Projects in Design Development have a total estimated construction cost of approximately \$1.59 billion and are listed below.

Elementary School Districts	Middle School Districts	High School Districts	Other Grade Configurations
Bridgewater-Raynham (PK-2) Danvers (K-5) Foxborough (PK 4) Manchester-Essex (PK-5) Marblehead (PK-3) Northbridge (PK-5) Tewksbury (2-4) Wareham (PK-4) West Springfield (K-5) Westborough (K-3)	Dennis-Yarmouth (4-7)* Framingham (6-8) Weymouth (6-8)	Arlington (9-12) Central Berkshire (9-12)	Belmont (7-12) Easthampton (K-8) Pentucket (7-12)

* Pending litigation following local appropriation vote

District Design Submittals

During the Design Development phase, districts will submit three design submittals (Design Development, 60% Construction Documents, and 90% Construction Documents) for the MSBA to review. MSBA staff reviews the documents to ensure the project is still in compliance with the PFA. The chart below indicates the number of submittals received and reviewed by the MSBA in each fiscal year.

Fiscal Year	DD Reviews	60% Reviews	90% Reviews	Total Reviews
FY2010	5	0	0	5
FY2011	21	24	20	65
FY2012	12	24	28	64
FY2013	20	20	19	59
FY2014	15	13	14	42
FY2015	6	12	13	31
FY2016	10	10	8	28
FY2017	11	10	12	33
FY2018	10	11	9	30
FY2019	17	16	10	43
FY2020	4	6	12	22
Totals	131	146	145	422

SUMMARY OF BID DATA

Based on the most recent data and schedules provided by districts, 22 projects are scheduled to receive sub-bids in 2019, fifteen projects are scheduled to receive sub-bids in 2020, and five projects are scheduled to receive sub-bids in 2021.


Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2019	22	21,110	\$2.67 billion	\$2.16 billion
2020	15	14,250	\$1.82 billion	\$1.45 billion
2021	5	6,580	\$0.70 billion	\$0.56 billion
Grand Total	42	41,940	\$5.19 billion	\$4.17 billion

Note: These numbers are based on preliminary information received from the District and are subject to further review and calculation. Data is shown only for projects which have Project Scope and Budget Agreement approval by the Board. For additional information on the bid schedules of these projects, please see Appendix B.

The graph below plots Schematic Design Estimates, Construction Estimates, and Construction Bid Results from 2016 to present. The graph includes seven new construction projects that received bids in FY 2017, nine new construction projects that received bids in FY 2018, and nine new construction projects that received bids in FY 2019. The Orange Line is a trend line for Bid Costs and the Blue Line is a trend line for Schematic Design Estimates. Springfield's Brightwood Elementary School is the only new construction project that received bids since the last report prepared for the October 30, 2019 Board meeting.


A fully interactive version of this graph is available on the MSBA website, here:

<http://info.massschoolbuildings.org/TabPub/TableauCostData.aspx>

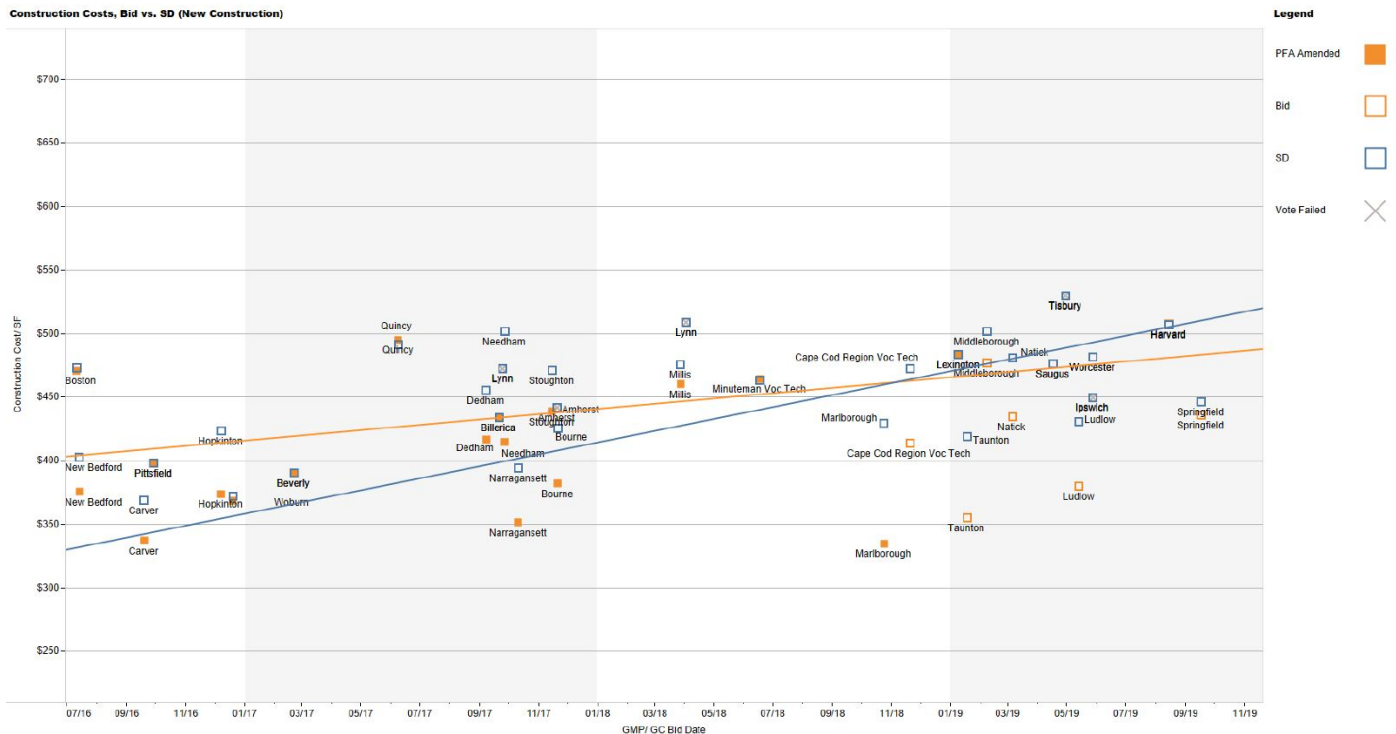

For additional information about these projects, please see Appendix C.

The graph below plots Schematic Design Estimates, Construction Estimates, and Construction Bid Results from 2016 to present for Addition/Renovation projects, including three addition/renovation construction projects that received bids in FY2017 and five addition/renovation construction projects that received bids in FY2018. The Orange Line is a trend line for Bid Costs and the Blue Line is a trend line for Schematic Design Estimates. *There have been no projects added since the last report prepared for the October 30, 2019 Board meeting.* A fully interactive version of this graph is available on the MSBA website, here: <http://info.massschoolbuildings.org/TabPub/TableauCostData.aspx>.

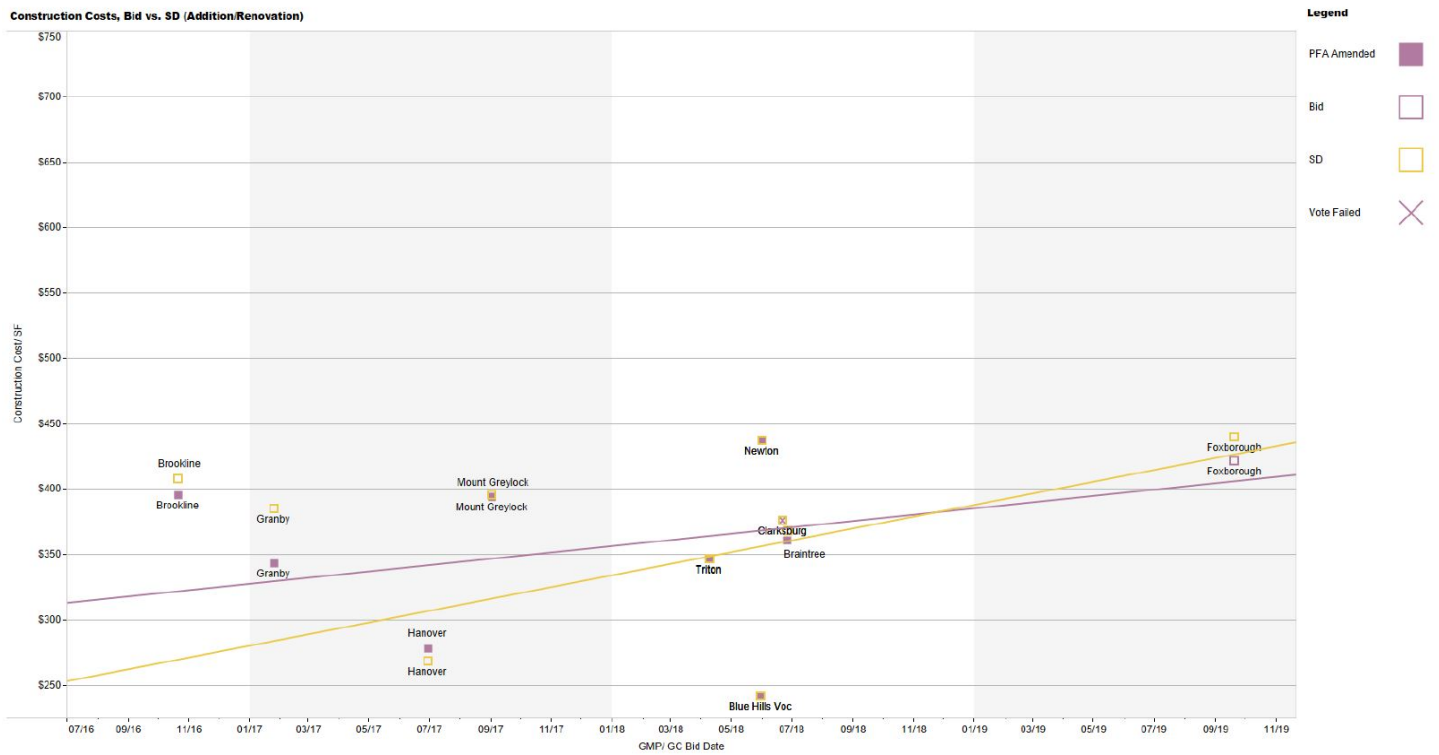

For additional information about these projects, please see Appendix C.

CONSTRUCTION

When a district with a Design-Bid-Build Construction project issues a Notice to Proceed, or when a Construction Manager At-Risk project has received sub-bids, the project is advanced to the Construction Phase. Currently, there are 59 projects in the Construction Phase with a total estimated construction cost of \$1.96 billion. Of those 59 projects, 39 are ARP Projects and 20 are Core Program Projects, however, this does not include the 36 projects that have reached substantial completion and are currently in the Building Complete Phase. The 20 Core Program Projects have a total estimated construction cost of \$1.88 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
Harvard (PK-5) Lexington (K-5) Ludlow (2-5) Marlborough (K-5) Shrewsbury (K-4) Springfield (PK-5) Taunton (PK-6)	Braintree (5-8) Natick (5-8)	Attleboro (9-12) Blue Hills Reg. Vo Tech (9-12) Boston (9-12) Bristol County Agr. (9-12) Cape Cod Reg. Vo Tech (9-12) Fall River (9-12) Middleborough (9-12) Somerville (9-12) Worcester (9-12)	Saugus (6-12) Westport (5-12)

Amendment to the Project Funding Agreement (PFA)

Upon receipt of construction bids or the execution of a GMP, a district submits the Contractor’s Schedule of Values to the MSBA. MSBA staff will collaborate with the district to reconcile the construction costs from the schedule of values against the estimated construction budget. Afterwards, an amendment to the PFA is executed to reflect the bids received for those projects. The chart, shown below, is the number of amendments to PFAs listed by fiscal year.

Fiscal Year	Total Amendments
FY2012	30
FY2013	31
FY2014	31
FY2015	17
FY2016	22
FY2017	8
FY2018	15
FY2019	13
FY2020	2

Substantial Completion

Thirteen projects are scheduled to reach Substantial Completion in 2019 and are listed in the table below.

Project	Enrollment	Contractor	OPM	Designer	Substantial Completion Date*	Building Construction Completion Date**	Variance (days)
Mt. Greylock	535	Turner	Dore & Whittier	Perkins Eastman/D PC	4/20/18	1/30/19	285 behind
Dedham Early Childhood Center	200	C.J. Marbardy H.V. Collins	Construction Monitoring Services	Knight, Bagge & Anderson	2/25/19	2/7/19	18 ahead
Quincy Sterling MS	430	Bond Brothers	PCA 360	Ai3 Architects	5/20/19	5/20/19	-
Billerica Memorial HS	1610	Shawmut	Leftfield	Perkins + Will	3/29/19	6/6/19	69 behind
Narragansett Templeton Center ES	580	Fontaine Brothers	Colliers	Symmes, Maini & McKee	5/15/19	6/18/19	34 behind
Bourne Peebles ES	460	Brait Builders	Symmes, Maini & McKee	Flansburgh	5/20/19	4/30/19	20 ahead
Millis Clyde F Brown ES	515	Bacon-Agostini	Compass	Tappe	5/25/19	6/7/19	13 behind
Needham Hillside ES	430	Bacon	Steven Popper	Dore & Whittier	6/14/19	7/5/19	21 behind
Newton Cabot ES	480	W.T. Rich	NV5	DiNisco Design	6/30/19	8/9/19	40 behind
Stoughton High School	1065	Consigli	Compass	Drummey Rosane Anderson	7/11/19	7/11/19	-
Triton Pine Grove ES	415	W.T.Rich	Pinck & Co.	Dore & Whittier	8/26/19	8/23/19	3 ahead
Minuteman Regional HS	628	Gilbane	Skanska	Kaestle Boos	9/25/19		
Blue Hills Reg. Voc. Tech. HS	900	Consigli	Dore & Whittier	Drummey Rosane Anderson	11/30/19		

*As defined in the executed Construction Contract, once provided to the MSBA

**Date on the Certificate of Substantial Completion, once provided to the MSBA

CLOSEOUT

After the district's contractor finishes all project work including, demolishing the old building, completing site work, and finalizing commissioning, the project proceeds to the Closeout Phase. Once all the project costs have been paid by the District, the District submits its Final Request for Payment Reimbursement via the MSBA's Pro-Pay system. After the District submits all the items identified on the MSBA's Index of Final Closeout, including the Final Request for Payment Reimbursement, the MSBA initiates the Draft Audit Report and sends it to the District for its consideration. The MSBA performs the final audit to determine final total grant amounts. Final payment to the District requires the MSBA Board's approval of the final Total Facilities Grant for the project.

Currently, there are 71 projects in the Closeout Phase including 51 ARP Projects and 20 Core Program Projects. The chart, shown below, lists the Core Program Projects by year of achieved Substantial Completion:

Year	All Project Phases	Final Audit Approved	Closeout	Building Complete
2012	22	22	0	0
2013	24	24	0	0
2014	19	19	0	0
2015	27	22	4	1
2016	12	8	4	0
2017	9	0	7	2
2018	11	0	6	5
2019	12	0	1	11
Total	135	96	20	19

ACCELERATED REPAIR PROGRAM



The photos above depict the before and after of the boiler room in the Carver Middle High School, serving 760 students. The project replaced the windows, doors, and boilers, thus, extending the useful life of the 63-year-old building. The project reached Substantial Completion in September 2017 and is being brought to the December 2019 Board of Directors meeting for Final Audit Approval.

Currently, there are 325 projects that are either active or completed in the ARP. The 325 projects are located in 129 districts, many of whom have been invited to the ARP multiple times. All the new information that has been updated since the last report is *italicized and bolded*.


Repair Program	Number of Districts	Number of Projects	Total Project Budgets	Maximum Facilities Grants	Number of Projects Final Audit Approved
2019 Accelerated	27	42			
2018 Accelerated	20	30	\$83,172,480	\$47,018,557	-
2017 Accelerated	19	34	\$117,020,597	\$73,280,673	1
2016 Accelerated	28	48	\$156,598,234	\$83,007,586	11
2015 Accelerated	24	43	\$136,680,652	\$91,974,052	27
2014 Accelerated	34	47	\$108,410,084	\$65,388,035	42
2013 Accelerated	25	45	\$94,650,790	\$54,662,711	45
2012 Accelerated	24	36	\$63,009,653	\$38,267,952	36

2019 Accelerated Repair Program

- Invitations – 27 districts, representing 42 projects
 - Scope includes 24 roofs and 21 boilers

2018 Accelerated Repair Program


- Invitations – 23 districts, representing 34 projects
 - Scope includes 17 roofs, 11 windows/doors, and 14 boilers
- SOI Removal – three districts; four projects (two roofs, two windows, one boiler)
- Approved for Project Funding Agreement – 20 districts, representing 30 projects
- Total Project Budgets - \$83,172,480
- MSBA Total Facilities Grant - \$47,018,557
- **13 of 15 projects reporting bids within estimated budget**

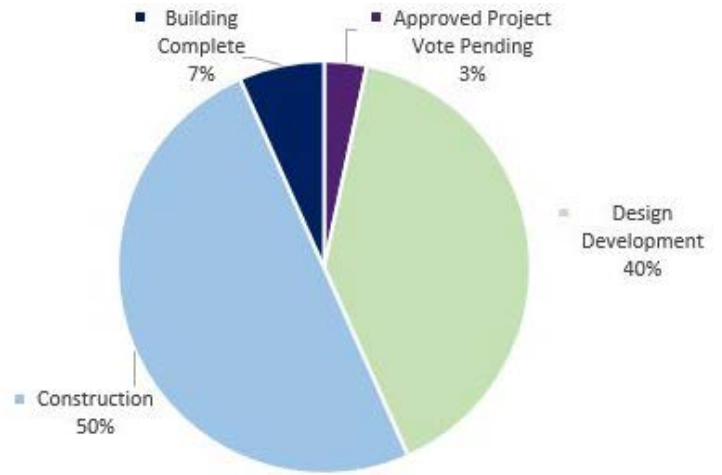

2018 ARP Status Chart

2017 Accelerated Repair Program


- Invitations – 20 districts, representing 36 projects
 - Scope includes nine roofs, 23 windows/doors, and 15 boilers
- SOI Removal - one district; two projects (one boiler; one windows/doors)
- Approved for Project Funding Agreement - 19 districts, representing 34 projects
- Total Project Budgets - \$117,020,597
- MSBA Total Facilities Grant - \$73,280,673
- Three districts, representing six projects, required a schedule extension following PFA approval
- 26 of 33 projects reporting bids within estimated budget
- **1 project has completed Final Audit**

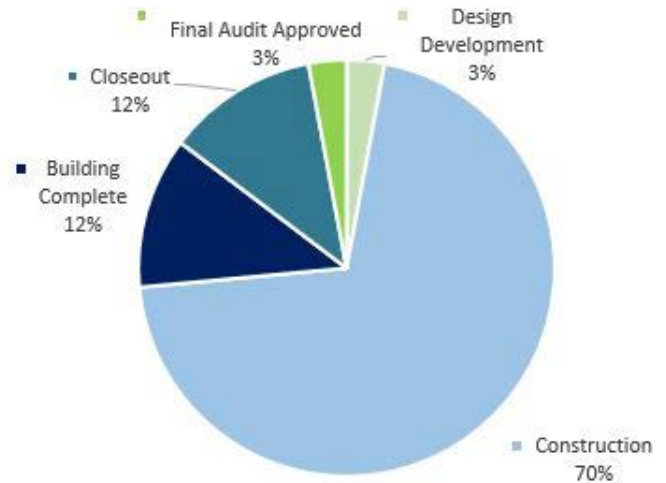

2017 ARP Status Chart

2016 Accelerated Repair Program


- Invitations – 28 districts, representing 49 projects
 - Scope includes 25 roofs, 19 windows/doors, and 13 boilers
- SOI Removal - one project (one boiler)
- Approved for Project Funding Agreements - 28 districts, representing 48 projects
- Total Project Budgets - \$156,598,234
- MSBA Total Facilities Grant - \$83,007,586
- Four districts, representing four projects, required a schedule extension following PFA approval
- 73% of projects bid within estimated budget
- **11 projects have completed Final Audit**

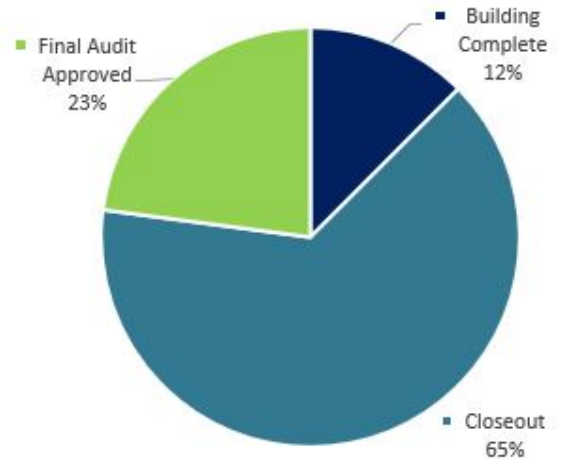

2016 ARP Status Chart

2015 Accelerated Repair Program


- Invitations – 24 districts, representing 44 projects
 - Scope includes 22 roofs, 26 windows/doors, and nine boilers
- SOI Removal – one project
- Approved for Project Funding Agreements – 24 districts, representing 43 projects
- Total Project Budgets - \$136,680,652
- MSBA Total Facilities Grants - \$91,974,052
- One district, representing one project, required two schedule extensions following PFA Approval
- 81% of projects bid within estimated budgets
- **27 projects have completed Final Audit**

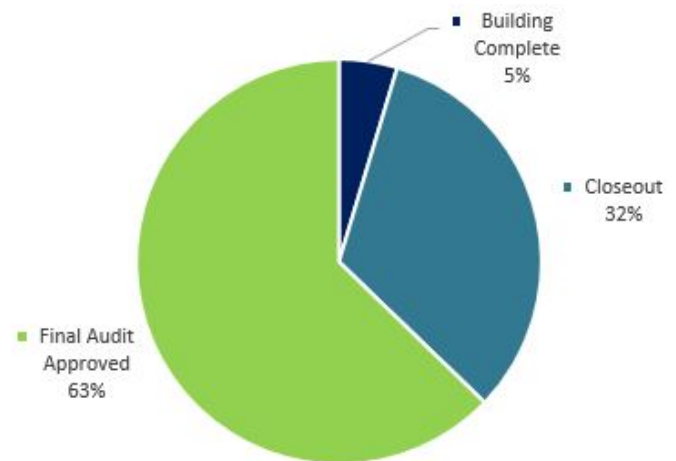

2015 ARP Status Chart

2014 Accelerated Repair Program

- Invitations – 36 districts, representing 51 projects
- SOI Removal – two districts, representing four projects
- Current 2014 ARP projects – 34 districts, representing 47 projects
 - Scope includes 20 roofs, 25 windows/doors, and 13 boilers
- Approved for Project Funding Agreements – 34 districts, representing 47 projects
- Total Project Budgets - \$108,410,084
- MSBA Total Facilities Grants - \$65,388,035
- Four districts, representing six projects, required schedule extensions following PFA approval
- 85% of projects bid within estimated budget
- 89% of projects have completed Final Audit

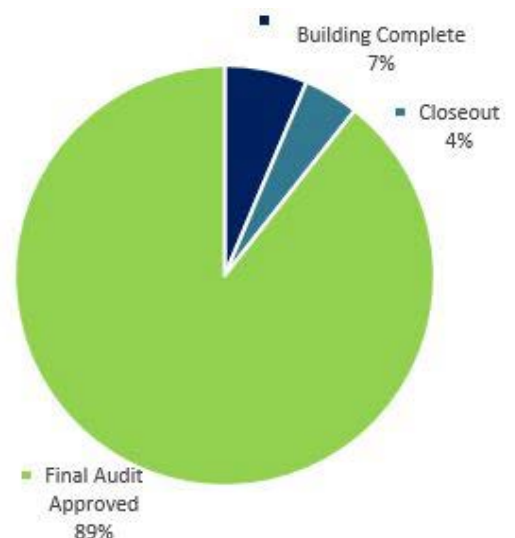

2014 ARP Status Chart

2013 Accelerated Repair Program

- Approved and completed Project Funding Agreements
 - 25 districts, representing 45 projects
- Scope included 30 roofs, 13 windows/doors, and seven boilers
- 100% of projects have completed Final Audit
 - Final Costs Submitted - \$70,489,512
 - Final MSBA Total Facilities Grants - \$37,769,94

2012 Accelerated Repair Program

- Approved and Completed Project Funding Agreements
 - 24 districts, representing 36 projects
- Scope included 21 roofs, 11 windows/doors, and seven boilers
- 100% of projects have completed Final Audit
 - Final Costs Submitted: \$47,748,996
 - Final MSBA Total Facilities Grant: \$28,518,764

Status of Green Repair Program

The Green Repair Program resulted in PFA authorizations totaling \$366,647,226 in Total Project Costs and \$222,889,218 in MSBA grants. All 189 projects from 93 districts have been approved for final grant payments.

2018 Accelerated Repair Projects – Construction Estimate vs. 2019-2020

- 13 of 15 projects reported bids within estimated budget.
- An additional 10 projects are anticipated to bid by the February Board of Directors meeting.

District	School	Scope	Project Type	Bid Date	Construction Estimate*	Bid Amount*	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance**
Norfolk	H Olive Day	Roof	DBB	Apr-19	\$2,471,557	\$3,043,000	-\$571,443	51.63%	\$0
Nashoba Valley Tech	Nashoba Valley Tech HS	Partial Roof, Partial Windows/Doors	DBB	Apr-19	\$2,545,929	\$2,870,100	-\$324,171	55.00%	\$0
New Bedford	Trinity Day Academy	Boiler	DBB	Apr-19	\$532,049	\$496,000	\$36,049	80.00%	\$28,839
Cambridge	Graham and Parks	Partial Roof	DBB	Apr-19	\$3,310,795	\$2,236,000	\$1,074,795	44.08%	\$473,770
Danvers	Highlands	Roof	DBB	May-19	\$2,774,225	\$2,216,100	\$558,125	50.58%	\$282,300
New Bedford	John Avery Parker	Roof	DBB	May-19	\$1,067,014	\$754,400	\$312,614	80.00%	\$250,091
Newton	Bigelow Middle	Boiler	DBB	May-19	\$1,009,826	\$850,830	\$158,996	32.47%	\$51,626
Ware	Stanley M Koziol Elem	Boiler	DBB	May-19	\$561,341	\$398,810	\$162,531	78.95%	\$128,318
Lynn	Lynn Vo Tech Institute	Partial Roof	DBB	Jun-19	\$3,526,624	\$2,003,000	\$1,523,624	79.58%	\$1,212,500
Springfield	Milton Bradley School	Partial Roof	DBB	Jun-19	\$2,785,783	\$1,548,500	\$1,237,283	80.00%	\$1,212,500
East Longmeadow	Meadow Brook	Roof	DBB	Jun-19	\$2,548,488	\$1,131,000	\$1,417,488	55.00%	\$779,618
West Bridgewater	Howard School	Partial Roof	DBB	Jun-19	\$311,438	\$248,000	\$63,438	52.69%	\$33,425
Tantasqua	Tantasqua Reg Jr High	Windows/Doors	DBB	Jun-19	\$1,542,752	\$1,306,000	\$236,752	55.63%	\$131,705
Springfield	High School/Science-Tech	Boiler	DBB	Oct-19	\$4,271,083	\$2,972,000	\$1,299,083	80.00%	\$1,039,266
Bourne	Bourne High	Roof	DBB	Nov-19	\$1,771,122	\$1,358,122	\$412,194	46.79%	\$192,866
				Total	\$31,030,026	\$23,431,862	\$7,597,358		\$5,816,824

2017 Accelerated Repair Projects – Construction Estimate vs. 2018-2019

- 26 of 33 projects reported bids within estimated budget.
- One project is anticipated to bid by the February 2020 Board of Directors meeting.

District	School	Scope	Project Type	Bid Date	Construction Estimate*	Bid mount*	Variance for Construction Estimate	Reimbursement Rate	Potential Grant Variance**
Westford	Abbot Elementary School	Partial Roof	DBB	Mar-18	\$2,399,102	\$1,987,000	\$412,102	44.48%	\$183,303
Weymouth	Wessagusset	Boiler	DBB	Apr-18	\$747,558	\$544,111	\$203,447	54.16%	\$29,059
Weymouth	Thomas W. Hamilton Primary School	Boiler	DBB	Apr-18	\$754,474	\$578,691	\$175,783	55.63%	\$97,788
East Longmeadow	Meadow Brook	Windows/Doors	DBB	Apr-18	\$2,228,280	\$1,770,877	\$457,403	55.00%	\$251,572
Quincy	North Quincy High	Partial Roof	DBB	May-18	\$1,266,623	\$1,346,000	-\$79,377	68.33%	\$0
Lawrence	Arlington Elementary School	Roof, Boiler	DBB	May-18	\$2,541,724	\$2,048,000	\$493,724	80.00%	\$394,979
Boston	William E. Russell	Roof	DBB	May-18	\$1,598,728	\$1,576,700	\$22,028	65.47%	\$14,422
Worcester	Thorndyke Road	Partial Windows/Doors	DBB	Jun-18	\$2,010,580	\$2,468,151	-\$457,571	78.95%	\$0
Worcester	Lincoln Street	Partial Roof, Windows/Doors	DBB	Jun-18	\$3,082,067	\$2,540,513	\$541,554	78.95%	\$427,557
Worcester	Elm Park Community	Windows/Doors	DBB	Jun-18	\$2,623,542	\$2,623,336	\$206	78.95%	\$163
Athol-Royalston	Athol High	Roof, Windows/Doors, Boiler	DBB	Oct-18	\$8,103,411	\$6,277,000	\$1,826,411	79.58%	\$1,453,458
Norton	J C Solmonese	Windows/Doors	DBB	Oct-18	\$1,876,411	\$2,005,257	-\$126,846	55.63%	\$0
Norton	Henri A. Yelle	Windows/Doors	DBB	Oct-18	\$3,116,095	\$3,182,481	-\$66,386	55.63%	\$0
Norton	L G Nourse Elementary	Windows/Doors	DBB	Oct-18	\$1,709,260	\$1,747,262	-\$38,002	55.63%	\$0
Holyoke	Morgan Elem	Windows/Doors	DBB	Nov-18	\$1,960,881	\$1,962,810	-\$1,929	80.00%	\$0
Holyoke	Lt Clayre Sullivan Elem	Windows/Doors	DBB	Nov-18	\$4,167,411	\$3,973,625	\$193,786	80.00%	\$155,029
Seekonk	Mildred Aitken School	Partial Windows/Doors	DBB	Dec-18	\$926,745	\$965,500	-\$38,755	52.69%	\$0
Mansfield	Mansfield High	Partial Windows/Doors	DBB	Dec-18	\$1,562,260	\$1,347,000	\$215,260	50.79%	\$109,331
Randolph	Martin E Young Elem	Windows/Doors	DBB	Jan-19	\$1,828,630	\$1,393,298	\$435,332	76.84%	\$334,509
Springfield	South End Middle School	Windows/Doors	DBB	Oct-18	\$1,934,908	\$1,198,000	\$736,908	80.00%	\$589,526
Lynn	Hood	Roof, Windows/Doors	DBB	Dec-18	\$4,439,681	\$3,546,000	\$893,681	79.58%	\$711,191
Holyoke	Kelly Elem	Windows/Doors, Boiler	DBB	Apr-18/Nov-18	\$5,286,531	\$4,391,000	\$895,531	80.00%	\$716,425
Randolph	Margaret L Donovan	Windows/Doors, Boiler	DBB	Aug-18/Dec-18	\$3,843,498	\$3,225,498	\$618,254	76.84%	\$475,066
Boston	John Marshall	Windows/Doors	DBB	Jan-19	\$4,458,029	\$3,969,000	\$489,029	65.47%	\$320,167
Boston	Hugh Roe O'Donnell	Boiler	DBB	Dec-18	\$911,516	\$892,621	\$18,895	65.47%	\$12,371

District	School	Scope	Project Type	Bid Date	Construction Estimate*	Bid mount*	Variance for Construction Estimate	Reimbursement Rate	Potential Grant Variance**
Boston	Charles Sumner	Boiler	DBB	Dec-18	\$1,013,960	\$910,700	\$103,260	65.47%	\$67,604
Boston	Maurice J Tobin	Boiler	DBB	Dec-18	\$1,463,372	\$1,032,808	\$430,564	65.47%	\$281,890
East Bridgewater	Central	Boiler	DBB	Feb-19	\$1,223,611	\$759,619	\$463,992	56.26%	\$261,042
Blackstone-Millville	John F Kennedy Elem	Windows/Doors, Boiler	DBB	Mar-19	\$3,828,470	\$2,105,900	\$1,722,570	57.74%	\$994,612
Lawrence	School for Exceptional Studies	Roof	DBB	Mar-19	\$3,782,209	\$3,161,000	\$621,209	80.00%	\$496,967
				Total	\$84,563,400	\$73,093,108	\$11,472,546		\$8,827,745

Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their PFAs pending compliance with the following stipulations:

- The district must submit a detailed, revised, construction timeline that explains how the work will be completed at each school; and
- Any costs that are related to a district requesting an extension to the construction schedule will be the sole responsibility of the district, and those costs are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for windows, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant, as authorized by the Board.

Six of the 34 2017 ARP Projects revised their construction schedules to reflect substantial completion in 2019 or beyond. Staff has reported previously on the shaded projects listed below, which remain in Construction or Design Development.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Lynn	Hood	Roof, Windows/Doors	30-Apr-19	22-Oct-19	The District and its consultants have determined that bidding for construction in 2019 would better serve the existing facilities.
Fall River	Samuel Watson	Roof, Windows/Doors, Boiler	31-Dec-19	31-Aug-21	The District and its consultants sought and received a MAAB variance prior to proceeding with its appropriation vote, which delayed the development of construction documents.

PROJECT VARIANCES

Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement, which establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Staff has reported on budget increases for the 23 projects shaded below at previous Board Meetings. No shading appears where project information is new or updated since the previous Board Meeting. In no event has the increase in a budget resulted in an increase to the Estimated Maximum Total Facilities Grant, as authorized by the Board.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Andover	Bancroft ES	New	\$44,659,837	\$16,773,753	\$50,299,859	\$16,575,965	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Berlin-Boylston	Tahanto Regional HS	New	\$43,954,901	\$21,148,751	\$43,519,302	\$18,972,041	District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Burlington	Marshall Simonds MS	Add/Reno	\$32,865,272	\$17,143,365	\$34,221,929	\$15,362,127	The District appropriated at its May 2012 annual town meeting through Articles 18: 19, additional funds for the costs associated with the construction of the new field complex and field lighting replacement.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical HS	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
			\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Greater New Bedford	Greater New Bedford Vocational and Technical High School	Add/Reno	\$17,099,808	\$13,543,920	\$16,396,429	\$12,258,642	District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Lexington	Joseph Estabrook ES	New	\$40,792,248	\$12,250,739	\$43,392,248	\$12,148,491	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
Newburyport	Nock/Molin MS	Add/Reno	\$26,997,326	\$13,697,934	\$28,170,749	\$12,520,326	The District has received additional funding to cover additional construction change order costs.
North Reading	North Reading MS/HS	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Norfolk County Agricultural	Norfolk County Agricultural HS	Add/Reno	\$28,552,385	\$15,369,712	\$30,589,078	\$13,867,050	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Northborough	Lincoln Street ES	Add/Reno	\$25,530,553	\$10,407,408	\$25,530,553	\$10,407,408	The MSBA Board Approved Total Project Budget increased by \$60,400 from \$25,470,153 to \$25,530,553 due to the addition of an alternate, for a new ball field added at the District’s request.
Plymouth	South HS	New	\$107,800,000	\$46,867,514	\$111,063,271	\$46,328,160	The District appropriated \$3,263,371 of additional funding to fund change order work to incorporate scope previously identified in the construction bid documents as Alternate 4 (synthetic turf field) and a portion of Alternate 5 (electrical infrastructure to support future lights at synthetic turf field). Note that the increased Total Project Budget will not increase the Maximum Facilities Grant.
Revere	Staff Sergeant James J. Hill ES	New	\$45,402,396	\$29,551,048	\$45,402,396	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Salem	Saltonstall ES	Repair	\$15,503,406	\$11,794,492	\$15,752,033	\$10,709,091	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Sutton	Sutton MS	Add/Reno	\$59,945,474	\$29,843,511	\$60,130,536	\$27,002,506	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Hopkinton	Center ES	New	\$45,629,373	\$14,058,455	\$47,129,373	\$14,058,455	The District has appropriated \$1,500,000 of additional funds to cover the costs associated with the construction of a building addition due to an unanticipated increase in enrollment.
Uxbridge	Uxbridge HS	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.
Weston	Field ES	New	\$31,504,146	\$8,310,510	\$32,654,146	\$8,105,549	District-approved Construction Change Orders exceeded available contingency amount.
Winchester	Winchester HS	Add/Reno	\$129,923,146	\$44,493,270	\$131,513,741	\$43,100,458	The MSBA Board Approved total Project Budget increased due to a construction change order for additional soil abatements at Skillings Field. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Winthrop	Winthrop MS/HS	New	\$81,818,740	\$42,582,841	\$81,432,986	\$41,249,005	The MSBA Board Approved Total Project Budget increased due to revised FEMA flood plain requirements which necessitated the elevation of the new building to be raised. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Woburn	Wyman-Hurld ES	New	\$33,705,396	\$14,387,427	\$39,647,723	\$14,387,427	The District had completed a project review with its Conservation Commission and an Order of Conditions was issued on June 12, 2015. A neighborhood group appealed this Order and was reviewed by The DEP. The District experienced delays in completing its City Council vote for its appropriation and incurred additional costs.
Oxford	Oxford MS	Add/Reno	\$6,128,870	\$3,483,589	\$7,340,000	\$3,359,171	The District received additional funding to cover additional construction costs including accessibility upgrades. District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Tewksbury	Tewksbury HS	New	\$84,173,174	\$44,194,627	\$67,710,158	\$36,219,487	District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.

APPENDIX A PROJECT STATUS LIST

Date of Report: 11/8/2019

Total Projects: 312

SOI	MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CM/GC	Commissioning Consultant
2008	200800010405	Abington	Frolio Middle School	Closeout	Core Program	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Horizon Engineering Associates, LLP
2016	201606000020	Acton-Boxborough	C.T. Douglas Elementary School	Approved Project Vote Pending	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Arrowstreet Inc.	-	-
2019	201900030025	Acushnet	Acushnet Elementary Sch	Eligibility Period	Accelerated Repair	Roof	-	-	-	-	-
2019	201900050405	Agawam	Agawam Junior High	Eligibility Period	Accelerated Repair	Boiler	-	-	-	-	-
2015	201500070005	Amesbury	Amesbury Elementary	Approved Project Vote Pending	Core Program			NV5 (fka Joslin, Lesser + Associates Inc.)	DiNisco Design, Inc.	-	-
2017	201700090025	Andover	West Elementary School	Feasibility Study	Core Program			PMA Consultants, LLC	-	-	-
2015	201500100505	Arlington	Arlington High School	Design Development	Core Program	New Construction		Skanska USA Building, Inc	HMFH Architects, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
2017	201700140015	Ashland	David Mindess School	Feasibility Study	Core Program			Compass Project Management, Inc.	Flansburgh Associates, Inc.	-	-
2017	201706150505	Athol-Royalston	Athol High	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	NETCO Construction Project Managers, Inc.	CSS Architects Incorporated	J.D. Rivet & Co., Inc.	Colliers Project Leaders NE, LLC
2014	201400160505	Attleboro	Attleboro High	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	Cadmus Group LLC
2015	201500260505	Belmont	Belmont High	Design Development	Core Program	Addition / Renovation	CM@R	Daedalus Projects Inc	Perkins+Will	Skanska USA Building, Inc.	BVH Integrated Services, P.C.
2013	201300300305	Beverly	Briscoe Middle	Building Complete	Core Program	New Construction	CM@R	CBRE/HEERY	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Bard, Rao + Athanas Consulting Engineers, LLC
2013	201300310505	Billerica	Billerica Memorial High School	Building Complete	Core Program	New Construction	CM@R	Leftfield, LLC	Perkins+Will	Shawmut Design and Construction	NV5
2019	201908050605	Blackstone Valley Reg	Blackstone Valley	Eligibility Period	Accelerated Repair	Roof		Hill International Company	Mount Vernon Group Architects, Inc.	-	-
2017	201706220008	Blackstone-Millville	John F Kennedy Elementary	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	Skanska USA Building, Inc	TSKP Studio, LLC	Homer Contracting	Colliers Project Leaders NE, LLC
2018	201806220010	Blackstone-Millville	Millville Elem	Approved Project Vote Pending	Accelerated Repair	Boiler	DBB	PCA 360	NV5	-	Colliers Project Leaders NE, LLC
2015	201508060605	Blue Hills Voc	Blue Hills Reg Voc Tech	Construction	Core Program	Addition / Renovation	CM@R	Dore & Whittier Management Partners, Inc.	Drumme Rosane Anderson, Inc.	Consigli Construction Company, Inc.	Rist-Frost-Shumway Engineering, P.C.
2013	201300350546	Boston	Boston Arts Academy	Construction	Core Program	New Construction	CM@R	PMA Consultants, LLC	Perkins Eastman/DPC	Lee Kennedy Co., Inc.	Symmes, Maini & McKee Associates
2016	201600350560	Boston	Boston Latin School	Building Complete	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	-	Rist-Frost-Shumway Engineering, P.C.
2017	201700350036	Boston	Carter School	Designer Selection	Core Program			Hill International Company	-	-	-
2015	201500350052	Boston	Charles Sumner Elementary School	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Lambrian Construction Corp.	Simpson Gumpertz & Heger Inc.
2017	201700350052	Boston	Charles Sumner Elementary School	Construction	Accelerated Repair	Boiler	DBB	Vertex Construction Services	The S/L/A/M Collaborative	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
2015	201500350020	Boston	Curley K-8 School	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	GVW, Inc.	Simpson Gumpertz & Heger Inc.
2019	201900350020	Boston	Curley K-8 School	Eligibility Period	Accelerated Repair	Roof	-	-	-	-	-
2015	201500350072	Boston	David A. Ellis Elementary School	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	GVW, Inc.	Simpson Gumpertz & Heger Inc.
2015	201500350080	Boston	Donald Mckay	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Paul J. Rogan Co., Inc.	Simpson Gumpertz & Heger Inc.
2018	201800350080	Boston	Donald Mckay	Construction	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	Fitzmeyer & Tocci Associates, Inc.
2015	201500350651	Boston	Dorchester Academy	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Lambrian Construction Corp.	Simpson Gumpertz & Heger Inc.
2017	201700350530	Boston	East Boston High School	Construction	Accelerated Repair	Boiler	DBB	Vertex Construction Services	The S/L/A/M Collaborative	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
2015	201500350415	Boston	Grover Cleveland	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Paul J. Rogan Co., Inc.	Simpson Gumpertz & Heger Inc.



2010	201000350074	Boston	Henry Dearborn Middle School	Closeout	Core Program	New Construction	CM@R	Daedalus Projects Inc	Jonathan Levi Architects LLC	Gilbane Building Company	Symmes, Maini & McKee Associates
2017	201700350141	Boston	Hugh R. O'Donnell Elementary School	Construction	Accelerated Repair	Boiler	DBB	Vertex Construction Services	The S/L/A/M Collaborative	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
2016	201600350146	Boston	James Condon Elementary	Building Complete	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	-	Rist-Frost-Shumway Engineering, P.C.
2018	201800350156	Boston	James Otis	Construction	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	Simpson Gumpertz & Heger Inc.
2017	201700350178	Boston	John Marshall	Construction	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	The S/L/A/M Collaborative	WCI Corp.	Simpson Gumpertz & Heger Inc.
2016	201600350179	Boston	John W. McCormack Middle School	Closeout	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	Gibson Roofs, Inc.	Simpson Gumpertz & Heger Inc.
2018	201800350286	Boston	Josiah Quincy	Construction	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	Fitzemeyer & Tocci Associates, Inc.
2018	201800350262	Boston	Lyndon	Construction	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	Fitzemeyer & Tocci Associates, Inc.
2019	201900350655	Boston	Lyon Upper 9-12	Eligibility Period	Accelerated Repair	Boiler	-	-	-	-	-
2017	201700350229	Boston	Maurice J. Tobin K-8 School	Construction	Accelerated Repair	Boiler	DBB	Vertex Construction Services	The S/L/A/M Collaborative	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
2018	201800350575	Boston	O'Bryant Sch Math/Science	Construction	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	Simpson Gumpertz & Heger Inc.
2016	201600350268	Boston	Paul A. Dever Elementary School	Closeout	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	Gibson Roofs, Inc.	Simpson Gumpertz & Heger Inc.
2010	201000350565	Boston	Quincy Upper School	Feasibility Study	Core Program	-	-	Skanska USA Building, Inc	HMFH Architects, Inc.	-	-
2018	201800350691	Boston	Rafael Hernandez	Construction	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	Fitzemeyer & Tocci Associates, Inc.
2016	201600350360	Boston	William E. Channing Elementary School	Building Complete	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	-	Rist-Frost-Shumway Engineering, P.C.
2017	201700350366	Boston	William E. Russell Elementary School	Building Complete	Accelerated Repair	Roof	DBB	Vertex Construction Services	The S/L/A/M Collaborative	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
2019	201900350363	Boston	William McKinley	Eligibility Period	Accelerated Repair	Roof	-	-	-	-	-
2015	201500350380	Boston	Young Achievers Science and Math Pilot K-8 School	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
2018	201800360505	Bourne	Bourne High	Design Development	Accelerated Repair	Roof	DBB	P3 Inc.	CIVITECTS PC	-	Russo Barr Associates, Inc.
2014	201400360010	Bourne	Peebles Elementary School	Building Complete	Core Program	New Construction	DBB	Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	Brait Builders Corp.	BVH Integrated Services, P.C.
2016	201600380013	Boxford	Spofford Pond	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	NETCO Construction Project Managers, Inc.	Russo Barr Associates, Inc.	Homer Contracting	CBI Consulting LLC
2013	201300400305	Braintree	East Middle School	Construction	Core Program	Addition / Renovation	CM@R	Hill International Company	Miller Dyer Spears Inc.	Shawmut Design and Construction	Fitzemeyer & Tocci Associates, Inc.
2016	201600400310	Braintree	South Middle School	Approved Project Vote Pending	Core Program	-	-	Hill International Company	Miller Dyer Spears Inc.	-	-
2016	201606250002	Bridgewater-Raynham	Mitchell Elementary School	Design Development	Core Program	New Construction	-	Daedalus Projects Inc	Raymond Design Associates, Inc.	-	-
2014	201409100705	Bristol County Agr	Bristol County Agr High	Construction	Core Program	Addition / Renovation	CM@R	Colliers Project Leaders NE, LLC	HMFH Architects, Inc.	-	NV5
2017	201708100605	Bristol-Plymouth Voc Tech	Bristol-Plymouth Vocational Technical	Designer Selection	Core Program	-	-	-	-	-	-
2014	201400440421	Brockton	Ashfield Middle School	Building Complete	Accelerated Repair	Roof, Boiler	DBB	Architectural Consulting Group, LLC	Tighe & Bond, Inc.	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
2014	201400440010	Brockton	Brookfield	Building Complete	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	Tighe & Bond, Inc.	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
2014	201400440035	Brockton	Gilmore	Building Complete	Accelerated Repair	Roof, Boiler	DBB	Architectural Consulting Group, LLC	Tighe & Bond, Inc.	Reliable Roofing and Sheet Metal, LLC	Rist-Frost-Shumway Engineering, P.C. Simpson Gumpertz & Heger Inc.
2019	201900440055	Brockton	Huntington	Eligibility Period	Accelerated Repair	Roof	-	-	-	-	-
2011	201100460015	Brookline	Edward Devotion	Building Complete	Core Program	Addition / Renovation	CM@R	-	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC



2018	201800460040	Brookline	Pierce	Eligibility Period	Core Program	-	-	-	-	-	-
2016	201600490090	Cambridge	Fletcher Maynard Academy	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Atane Engineers, P.C.	John F. Shea Company, Inc.	Gale Associates, Inc.
2018	201800490080	Cambridge	Graham and Parks	Construction	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	The S/L/A/M Collaborative	-	Thompson & Lichtner Co., Inc.
2014	201408150605	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Construction	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Drumme Rosane Anderson, Inc.	Brait Builders Corp.	NV5
2013	201300520015	Carver	Carver Elementary School	Closeout	Core Program	New Construction	DBB	PMA Consultants, LLC	HMFH Architects, Inc.	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
2016	201600520405	Carver	Carver Middle/High School	Closeout	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Leftfield, LLC	Johnson Roberts Associates, Inc.	J.J. Cardosi, Inc.	Symmes, Maini & McKee Associates
2015	201506350505	Central Berkshire	Wahconah Regional High	Design Development	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Drumme Rosane Anderson, Inc.	Barr & Barr Inc.	Horizon Engineering Associates, LLP
2019	201900560015	Chelmsford	South Row	Eligibility Period	Accelerated Repair	Roof	JACOBS Project Management Co.	Russo Barr Associates, Inc.	-	-	-
2008	200800570050	Chelsea	Clark Avenue School	Closeout	Core Program	New Construction	CM@R	Pinck & Co., Inc.	HMFH Architects, Inc.	W. T. Rich Company Inc.	Cannon Design
2015	201500610010	Chicopee	Belcher Elementary School	Final Audit Approved	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Kaestle Boos Associates, Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
2016	201600610050	Chicopee	Chicopee Academy	Closeout	Accelerated Repair	Roof	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	W.J. Mountford Company	Thompson & Lichtner Co., Inc.
2009	200900610021	Chicopee	Dupont Middle	Closeout	Core Program	Renovation	DBB	Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Symmes, Maini & McKee Associates
2015	201500610310	Chicopee	Fairview Elementary	Final Audit Approved	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Kaestle Boos Associates, Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
2016	201600610015	Chicopee	Patrick E. Bowe Elementary School	Closeout	Accelerated Repair	Windows / Doors	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	W.J. Mountford Company	Thompson & Lichtner Co., Inc.
2018	201800710010	Danvers	Highlands	Building Complete	Accelerated Repair	Roof	DBB	JACOBS Project Management Co.	ICON architecture, inc.	Northern Contracting	R. J. Kenney Associates, Inc.
2015	201500710032	Danvers	Ivan G Smith	Design Development	Core Program	New Construction	CM@R	PMA Consultants, LLC	Tappe Architects, Inc.	W. T. Rich Company Inc.	Colliers Project Leaders NE, LLC
2016	201600720050	Dartmouth	Dartmouth Middle School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Greenwood Industries, Inc.	CBI Consulting LLC
2012	201200730005	Dedham	Early Childhood Center	Building Complete	Core Program	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	H.V. Collins Co., Inc.	Symmes, Maini & McKee Associates
2015	201506450305	Dennis-Yarmouth	Mattacheese Middle Sch	Design Development	Core Program	New Construction	DBB	PMA Consultants, LLC	Perkins Eastman/DPC	-	Consulting Engineering Services, LLC
2019	201900790035	Dracut	Brookside Elementary	Eligibility Period	Accelerated Repair	Roof	-	-	-	-	-
2019	201900790045	Dracut	George H. Englesby Elementary School	Eligibility Period	Accelerated Repair	Roof	-	-	-	-	-
2017	201700830005	East Bridgewater	Central	Construction	Accelerated Repair	Boiler	DBB	PMA Consultants, LLC	Architectural Engineers, Inc.	George T. Wilkinson, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2019	201900830005	East Bridgewater	Central	Eligibility Period	Accelerated Repair	Roof	PMA Consultants, LLC	Kaestle Boos Associates, Inc.	-	-	-
2017	201700870013	East Longmeadow	Meadow Brook	Closeout	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	Kaestle Boos Associates, Inc.	Lizotte Glass	Building Enclosure Associates, LLC
2018	201800870013	East Longmeadow	Meadow Brook	Construction	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	Turowski2 Architecture, Inc.	Titan Roofing, Inc.	CBI Consulting LLC
2014	201400860010	Easthampton	Maple Elementary School	Design Development	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Caolo & Bieniek Associates, Inc.	-	Horizon Engineering Associates, LLP
2016	201600880003	Easton	Center School	Approved Project Vote Pending	Core Program	-	-	PMA Consultants, LLC	Perkins Eastman/DPC	-	-
2019	201908170505	Essex North Shore Agricultural and Technical School	Essex Technical High School	Eligibility Period	Accelerated Repair	Roof	Atlantic Construction and Management, Inc.	-	-	-	-
2014	201400950505	Fall River	B. M. C. Durfee High School	Construction	Core Program	Addition / Renovation	CM@R	Leftfield, LLC	Ai3 Architects LLC	Suffolk Construction Company	Jacobs Engineering Group Inc.
2017	201700950140	Fall River	James Tansey Elementary School	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	-	-	-	Fitzemeyer & Tocci Associates, Inc. Thompson & Lichtner Co., Inc.
2018	201800950325	Fall River	Resiliency Preparatory School	Design Development	Accelerated Repair	Roof, Boiler	DBB	P3 Inc.	edm Services, Inc.	-	Symmes, Maini & McKee Associates



2017	201700950145	Fall River	Samuel Watson Elementary School	Design Development	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	-	-	-	Fitzmeyer & Tocchi Associates, Inc. Thompson & Lichtner Co., Inc.
2018	201800950150	Fall River	Westall	Design Development	Accelerated Repair	Roof, Boiler	DBB	P3 Inc.	edm Services, Inc.	-	Symmes, Maini & McKee Associates
2016	201600970016	Fitchburg	Crocker Elementary	Eligibility Period	Core Program			Colliers Project Leaders NE, LLC	saam architecture	-	-
2019	201900970060	Fitchburg	South Street Elementary	Eligibility Period	Accelerated Repair	Roof, Boiler		-	-	-	-
2015	201500990015	Foxborough	Mabelle M. Burrell Elementary School	Design Development	Core Program	Addition / Renovation		Colliers Project Leaders NE, LLC	Kaestle Boos Associates, Inc.	-	Cadmus Group LLC
2015	201501000305	Framingham	Fuller Middle	Design Development	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Jonathan Levi Architects LLC	Consigli Construction Company, Inc.	Jacobs Engineering Group Inc.
2016	201601030020	Gardner	Waterford Street	Approved Project Vote Pending	Core Program			Colliers Project Leaders NE, LLC	Jones Whitsett Architects, Inc.	-	-
2016	201601070020	Gloucester	East Gloucester Elementary	Feasibility Study	Core Program			CBRE/HEERY	Dore & Whittier Architects, Inc.	-	-
2016	201601070505	Gloucester	Gloucester High School	Final Audit Approved	Accelerated Repair	Roof	DBB	P3 Inc.	Baker/Wohl Architects, Inc.	Stanley Roofing Company, Inc.	CBI Consulting LLC
2012	201201110010	Granby	West Street	Closeout	Core Program	Addition / Renovation	DBB	Colliers Project Leaders NE, LLC	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
2017	201708210605	Greater Fall River	Diman Regional Vocational Technical High	Designer Selection	Core Program			-	-	-	-
2009	200908280605	Greater Lowell Voc Tec	Gr Lowell Regional Vocational Technical	Closeout	Core Program	Addition / Renovation	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
2017	201706730010	Groton-Dunstable	Florence Roche School	Feasibility Study	Core Program			Leftfield, LLC	-	-	-
2016	201601180005	Halifax	Halifax Elementary School	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Vertex Construction Services	Habeeb & Associates Architects, Inc.	Lambrian Construction Corp.	Russo Barr Associates, Inc.
2019	201906800310	Hampden-Wilbraham	Wilbraham Middle	Eligibility Period	Accelerated Repair	Roof		Leftfield, LLC	Dietz & Company Architects, Inc.	-	-
2019	201901220004	Hanover	Cedar Elementary	Eligibility Period	Accelerated Repair	Roof		-	-	-	-
2013	201301220015	Hanover	Sylvester Elementary School	Building Complete	Core Program	Addition / Renovation	DBB	P3 Inc.	Mount Vernon Group Architects, Inc.	Brait Builders Corp.	Horizon Engineering Associates, LLP
2015	201501250005	Harvard	Hildreth Elementary School	Construction	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Arrowstreet Inc.	Shawmut Design and Construction	Bard, Rao + Athanas Consulting Engineers, LLC
2012	201201280035	Haverhill	Caleb Dustin Hunking	Closeout	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	JCJ Architecture, PC	Shawmut Design and Construction	Colliers Project Leaders NE, LLC
2018	201801280100	Haverhill	Consentino	Eligibility Period	Core Program			-	-	-	-
2008	200801330505	Holbrook	Holbrook Junior-Senior High School	Closeout	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
2014	201401370045	Holyoke	E N White Elementary	Final Audit Approved	Accelerated Repair	Boiler	DBB	STV DPM (fka STV Inc.)	Richard D. Kimball Co., Inc. (d/b/a NV5)	Adams Plumbing and Heating, Inc.	BVH Integrated Services, P.C.
2017	201701370010	Holyoke	H.B. Lawrence School	Approved Project Vote Pending	Core Program	New Construction		Pinck & Co., Inc.	Jones Whitsett Architects, Inc.	-	-
2017	201701370040	Holyoke	Kelly Elementary	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	Hill International Company	ICON architecture, inc.	Lambrian Construction Corp.	R.J. Kenney Associates, Inc.
2017	201701370055	Holyoke	Lt Clayre Sullivan Elementary	Construction	Accelerated Repair	Windows / Doors	DBB	Hill International Company	ICON architecture, inc.	GVW, Inc.	Consulting Engineering Services, LLC R.J. Kenney Associates, Inc.
2014	201401370025	Holyoke	William G. Morgan	Final Audit Approved	Accelerated Repair	Boiler	DBB	STV DPM (fka STV Inc.)	Richard D. Kimball Co., Inc. (d/b/a NV5)	Adams Plumbing and Heating, Inc.	BVH Integrated Services, P.C.
2017	201701370025	Holyoke	William G. Morgan	Construction	Accelerated Repair	Windows / Doors	DBB	Hill International Company	ICON architecture, inc.	GVW, Inc.	R.J. Kenney Associates, Inc.
2013	201301390005	Hopkinton	Center	Closeout	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Drumney Rosane Anderson, Inc.	Colantonio, Inc.	NV5
2018	201801420305	Hull	Memorial Middle	OPM Selection	Core Program			-	-	-	-
2014	201401440015	Ipswich	Winthrop Elementary School	Final Audit Approved	Core Program	New Construction		PMA Consultants, LLC	Perkins Eastman/DPC	-	-
2019	201901450005	Kingston	Kingston Elementary	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-



2017	201701490008	Lawrence	Community Day Arlington	Building Complete	Accelerated Repair	Roof, Boiler	DBB	Pinck & Co., Inc.	Johnson Roberts Associates, Inc.	Greenwood Industries, Inc.	Symmes, Maini & McKee Associates
2017	201701490040	Lawrence	Francis M. Leahy Elementary School	Feasibility Study	Core Program			Atlantic Construction and Management, Inc.	-	-	-
2016	201601490050	Lawrence	Henry K Oliver School for Exceptional Studies	Feasibility Study	Core Program			Pinck & Co., Inc.	Symmes Maini & McKee Associates, Inc.	-	-
2017	201701490537	Lawrence	Henry K Oliver School for Exceptional Studies	Construction	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	Johnson Roberts Associates, Inc.	Greenwood Industries, Inc.	Symmes, Maini & McKee Associates
2016	201601510015	Leicester	Leicester Middle	Schematic Design	Core Program			NV5 (fka Joslin, Lesser + Associates Inc.)	Finegold Alexander Architects	-	-
2015	201501550035	Lexington	Maria Hastings Elementary School	Construction	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	DiNisco Design, Inc.	Walsh Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2019	201901600002	Lowell	Dr Gertrude Bailey	Eligibility Period	Accelerated Repair	Roof, Boiler		Leftfield, LLC	-	-	-
2019	201901600015	Lowell	Greenhalge	Eligibility Period	Accelerated Repair	Boiler		Leftfield, LLC	-	-	-
2019	201901600315	Lowell	James S Daley Middle Sch	Eligibility Period	Accelerated Repair	Boiler		Leftfield, LLC	-	-	-
2019	201901600340	Lowell	James Sullivan Middle Sch	Eligibility Period	Accelerated Repair	Roof, Boiler		Leftfield, LLC	-	-	-
2014	201401600505	Lowell	Lowell High	Approved Project Vote Pending	Core Program	Addition / Renovation		Skanska USA Building, Inc	Perkins Eastman/DPC	-	Bard, Rao + Athanas Consulting Engineers, LLC
2019	201901600005	Lowell	Rogers Early Learning Center	Eligibility Period	Accelerated Repair	Boiler		Leftfield, LLC	-	-	-
2019	201901600075	Lowell	S Christa McAuliffe Elementary	Eligibility Period	Accelerated Repair	Boiler		Leftfield, LLC	-	-	-
2015	201501610020	Ludlow	Chapin Street Elementary School	Construction	Core Program	New Construction	DBB	STV DPM (fka STV Inc.)	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2010	201001620505	Lunenburg	Lunenburg High School	Closeout	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Tappe Architects, Inc.	Shawmut Design and Construction	Cannon Design
2017	201701630055	Lynn	Hood Elementary School	Construction	Accelerated Repair	Roof, Windows / Doors	DBB	PCA 360	Russo Barr Associates, Inc.	Lockheed Window Corporations	CBI Consulting LLC
2018	201801630605	Lynn	Lynn Voc Tech Institute	Design Development	Accelerated Repair	Roof	DBB	-	-	Stanley Roofing Company, Inc.	CBI Consulting LLC
2015	201506980010	Manchester Essex Regional	Memorial Elementary School	Design Development	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	Symmes, Maini & McKee Associates
2017	201701670505	Mansfield	Mansfield High School	Construction	Accelerated Repair	Windows / Doors	DBB	Watermark Environmental, Inc.	Baker/Wohl Architects, Inc.	J.J. Cardosi, Inc.	CBI Consulting LLC
2015	201501680015	Marblehead	Elbridge Gerry	Design Development	Core Program	New Construction		Leftfield, LLC	Raymond Design Associates, Inc.	-	NV5
2015	201501700025	Marlborough	Richer	Construction	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	WSP USA
2016	201601710310	Marshfield	Furnace Brook Middle School	Closeout	Accelerated Repair	Roof	DBB	PCA 360	CIVITECTS PC	Colantonio, Inc.	Russo Barr Associates, Inc.
2016	201601720035	Mashpee	Quashnet School	Closeout	Accelerated Repair	Windows / Doors	DBB	exPERTcon, Inc.	Raymond Design Associates, Inc.	J.J. Cardosi, Inc.	CBI Consulting LLC
2017	201701750005	Medfield	Dale Street	Feasibility Study	Core Program			-	-	-	-
2014	201401820505	Middleborough	Middleborough High	Construction	Core Program	New Construction	DBB	Compass Project Management, Inc.	Drumme Rosane Anderson, Inc.	Fontaine Brothers, Inc.	Colliers Project Leaders NE, LLC
2011	201101850090	Milford	Woodland	Final Audit Approved	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
2016	201601860025	Millbury	Raymond E. Shaw School	Approved Project Vote Pending	Core Program			Hill International Company	Turowski2 Architecture, Inc.	-	-
2014	201401870005	Millis	Clyde F Brown	Building Complete	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Tappe Architects, Inc.	Bacon-Agostini Construction Joint Venture	Colliers Project Leaders NE, LLC
2009	200908300605	Minuteman Voc Tech	Minuteman Regional High School	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	Gilbane Building Company	Bard, Rao + Athanas Consulting Engineers, LLC
2019	201907170020	Mohawk Trail	Sanderson Academy	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-
2019	201901910025	Monson	Quarry Hill Comm	Eligibility Period	Accelerated Repair	Roof		-	-	-	-



2013	201307150505	Mount Greylock	Mt Greylock Reg High	Closeout	Core Program	Addition / Renovation	CM@R	Dore & Whittier Management Partners, Inc.	Perkins Eastman/DPC	Turner Construction Company	BVH Integrated Services, P.C.
2008	200807200020	Narragansett	Templeton Center School	Building Complete	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Symmes Maini & McKee Associates, Inc.	Fontaine Brothers, Inc.	Fitzmeyer & Tocci Associates, Inc.
2018	201808520605	Nashoba Valley Tech	Nashoba Valley Tech H S	Construction	Accelerated Repair	Roof, Windows / Doors	DBB	Leftfield, LLC	Robinson Green Beretta (RGB) Architects	Capeway Roofing Systems, Inc.	Simpson Gumpertz & Heger Inc.
2015	201501980305	Natick	John. F. Kennedy Middle School	Construction	Core Program	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
2016	201606600505	Nauset	Nauset Regional High	Schematic Design	Core Program			Daedalus Projects Inc	Flansburgh Associates, Inc.	-	-
2013	201301990035	Needham	Hillside Elementary School	Building Complete	Core Program	New Construction	DBB	-	Dore & Whittier Architects, Inc.	Bacon Construction Co, Inc.	Rist-Frost-Shumway Engineering, P.C.
2017	201702010015	New Bedford	Elizabeth Carter Brooks Elementary School	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Johnson Roberts Associates, Inc.	-	WSP USA
2016	201602010115	New Bedford	John Avery Parker	Closeout	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	CBI Consulting LLC	-	WSP USA
2018	201802010115	New Bedford	John Avery Parker	Construction	Accelerated Repair	Roof	DBB	Vertex Construction Services	Habeeb & Associates Architects, Inc.	Capeway Roofing Systems, Inc.	Thompson & Lichtner Co., Inc.
2009	200902010070	New Bedford	John Hannigan	Closeout	Core Program	New Construction	DBB	Daedalus Projects Inc	Turowski2 Architecture, Inc.	H.V. Collins Co., Inc.	WSP USA
2018	201802010510	New Bedford	Trinity Day Academy	Construction	Accelerated Repair	Boiler	DBB	Vertex Construction Services	Habeeb & Associates Architects, Inc.	Araujo Brothers Plumbing & Heating	WSP USA
2018	201807280015	New Salem-Wendell	Swift River	Design Development	Accelerated Repair	Windows / Doors	DBB	Colliers Project Leaders NE, LLC	TSKP Studio, LLC	-	Russo Barr Associates, Inc.
2018	201802070305	Newton	Bigelow Middle	Construction	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Tighe & Bond, Inc.	Veterans Development Corporation, Inc.	NV5
2013	201302070025	Newton	Cabot	Building Complete	Core Program	Addition / Renovation	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	DiNisco Design, Inc.	W. T. Rich Company Inc.	Colliers Project Leaders NE, LLC
2018	201802070315	Newton	F A Day Middle	Design Development	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Tighe & Bond, Inc.	-	NV5
2018	201802080015	Norfolk	H Olive Day	Construction	Accelerated Repair	Roof	DBB	PMA Consultants, LLC	Gale Associates, Inc.	Greenwood Industries, Inc.	R.J. Kenney Associates, Inc.
2018	201809150705	Norfolk County Agriculture	Norfolk County Agr	Design Development	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	-	-	Gale Associates, Inc.
2016	201602150015	North Brookfield	North Brookfield Elementary	Closeout	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	Dietz & Company Architects, Inc.	MDM Engineering	Simpson Gumpertz & Heger Inc.
2016	201607350030	North Middlesex	Hawthorne Brook	Building Complete	Accelerated Repair	Windows / Doors	DBB	Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	Gale Associates, Inc.
2011	201107350505	North Middlesex	North Middlesex Reg	Building Complete	Core Program	New Construction	DBB	CBRE/HEERY	Symmes Maini & McKee Associates, Inc.	CTA Construction Co., Inc.	Horizon Engineering Associates, LLP
2016	201607350020	North Middlesex	Squannacook	Building Complete	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	Vanguard Construction Company, Inc.	Gale Associates, Inc.
2016	201607350035	North Middlesex	Varnum Brook Elementary School	Building Complete	Accelerated Repair	Roof, Windows / Doors	DBB	Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	Gale Associates, Inc.
2010	201002170505	North Reading	North Reading High School	Closeout	Core Program	Addition / Renovation	CM@R	PMA Consultants, LLC	Dore & Whittier Architects, Inc.	Gilbane Building Company	Cannon Design
2016	201602100005	Northampton	Bridge Street School	Final Audit Approved	Accelerated Repair	Roof	DBB	Colliers Project Leaders NE, LLC	The S/L/A/M Collaborative	D.A. Sullivan & Sons, Inc.	CBI Consulting LLC
2016	201602100025	Northampton	Leeds Elementary School	Final Audit Approved	Accelerated Repair	Roof	DBB	Colliers Project Leaders NE, LLC	The S/L/A/M Collaborative	D.A. Sullivan & Sons, Inc.	CBI Consulting LLC
2019	201902140305	Northbridge	Northbridge Middle	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-
2015	201502140001	Northbridge	W Edward Balmer	Design Development	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Dore & Whittier Architects, Inc.	Fontaine Brothers, Inc.	Fitzmeyer & Tocci Associates, Inc.
2017	201708530605	Northeast Metro Voc	Northeast Metro Regional Vocational	Designer Selection	Core Program			PMA Consultants, LLC	-	-	-
2017	201702180060	Norton	Henri A. Yelle Elementary School	Construction	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	Turowski2 Architecture, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
2017	201702180015	Norton	J C Solmonese	Construction	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	Turowski2 Architecture, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
2017	201702180010	Norton	L. G. Nourse Elementary School	Construction	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	Turowski2 Architecture, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
2018	201802200305	Norwood	Dr. Philip O. Coakley Middle School	Eligibility Period	Core Program			-	-	-	-



2016	201602230010	Orange	Dexter Park School	Feasibility Study	Core Program			Hill International Company	Raymond Design Associates, Inc.	-	-	
2008	200802290305	Peabody	Higgins Middle School	Closeout	Core Program	New Construction	DBB	Daedalus Projects Inc	DiNisco Design, Inc.	Bacon-Agostini Construction Joint Venture	BVH Integrated Services, P.C.	
2018	201802290027	Peabody	William A Welch Sr	OPM Selection	Core Program			-	-	-	-	
2015	201507450505	Pentucket	Pentucket Reg Sr High	Design Development	Core Program	New Construction		Vertex Construction Services	Dore & Whittier Architects, Inc.	-	Jacobs Engineering Group Inc.	
2010	201002360510	Pittsfield	Taconic High School	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Drumrey Rosane Anderson, Inc.	Gilbane Building Company	Colliers Project Leaders NE, LLC	
2012	201202390515	Plymouth	Plymouth South High	Closeout	Core Program	New Construction	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Rist-Frost-Shumway Engineering, P.C.	
2013	201302420505	Provincetown	Provincetown High	Closeout	Core Program	Repair	DBB	Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	E. Amanti & Sons, Inc.	BVH Integrated Services, P.C.	
2019	201907530010	Quabbin	Hubbardston Center	Eligibility Period	Accelerated Repair	Roof		Pinck & Co., Inc.	CSS Architects Incorporated	-	-	
2016	201607780005	Quaboag Regional	Warren Elementary	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	NETCO Construction Project Managers, Inc.	TSKP Studio, LLC	Lockheed Window Corporations	Colliers Project Leaders NE, LLC	
2018	201807780010	Quaboag Regional	West Brookfield Elem	Schematic Design	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Baker/Wohl Architects, Inc.	-	-	
2016	201602430040	Quincy	Atherton Hough Elementary School	Closeout	Accelerated Repair	Boiler	DBB	Hill International Company	Architectural Engineers, Inc.	E. Amanti & Sons, Inc.	Consulting Engineering Services, LLC	
2015	201502430020	Quincy	Beechwood Knoll Elementary	Building Complete	Accelerated Repair	Roof, Windows / Doors	DBB	Atlantic Construction and Management, Inc.	Baker/Wohl Architects, Inc.	Alpha Contracting Associates, Inc.	CBI Consulting LLC	
2016	201602430020	Quincy	Beechwood Knoll Elementary	Closeout	Accelerated Repair	Boiler	DBB	Hill International Company	Architectural Engineers, Inc.	E. Amanti & Sons, Inc.	Consulting Engineering Services, LLC	
2015	201502430060	Quincy	Merrymount Elementary School	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	Baker/Wohl Architects, Inc.	Gibson Roofs, Inc.	CBI Consulting LLC	
2016	201602430060	Quincy	Merrymount Elementary School	Closeout	Accelerated Repair	Boiler	DBB	Hill International Company	Architectural Engineers, Inc.	E. Amanti & Sons, Inc.	Consulting Engineering Services, LLC	
2017	201702430510	Quincy	North Quincy High School	Closeout	Accelerated Repair	Roof	DBB	STV DPM (fka STV Inc.)	CBI Consulting LLC	Greenwood Industries, Inc.	Gale Associates, Inc.	
2013	201302430320	Quincy	Reay E. Sterling Middle School	Building Complete	Core Program	New Construction	CM@R	PCA 360	Ai3 Architects LLC	Bond Brothers, Inc.	Symmes, Maini & McKee Associates	
2016	201602430110	Quincy	Wollaston Elementary School	Closeout	Accelerated Repair	Boiler	DBB	Hill International Company	Architectural Engineers, Inc.	E. Amanti & Sons, Inc.	Consulting Engineering Services, LLC	
2017	201702440020	Randolph	Elizabeth G Lyons Elementary	Designer Selection	Core Program			Daedalus Projects Inc	-	-	-	
2017	201702440015	Randolph	Margaret L. Donovan Elementary School	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	TSKP Studio, LLC	A&A Window Products, Inc.	Consulting Engineering Services, LLC Gale Associates, Inc.	
2017	201702440040	Randolph	Martin E Young Elementary	Construction	Accelerated Repair	Windows / Doors	DBB	Atlantic Construction and Management, Inc.	TSKP Studio, LLC	Modern Glass & Aluminum, Inc.	Gale Associates, Inc.	
2015	201502480056	Revere	Garfield Elementary School	Final Audit Approved	Accelerated Repair	Roof	DBB	Leftfield, LLC	Turowski2 Architecture, Inc.	Greenwood Industries, Inc.	Thompson & Lichtner Co., Inc.	
2016	201602480057	Revere	Garfield Middle School	Final Audit Approved	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	BLW Engineers, Inc.	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.	
2018	201802480505	Revere	Revere High	Eligibility Period	Core Program			-	-	-	-	
2010	201002480035	Revere	Staff Sargent James J. Hill Elementary School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Drumrey Rosane Anderson, Inc.	CTA Construction Co., Inc.	Rist-Frost-Shumway Engineering, P.C.	
2016	201602510060	Rockland	Jefferson Elementary School	Approved Project Vote Pending	Core Program	New Construction		PMA Consultants, LLC	Symmes Maini & McKee Associates, Inc.	-	-	
2019	201902580005	Salem	Bentley	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-	
2019	201902610002	Sandwich	Forestdale School	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-	
2019	201902610025	Sandwich	Oak Ridge	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-	
2014	201402620505	Saugus	Saugus High	Construction	Core Program	New Construction	CM@R	PMA Consultants, LLC	HMFH Architects, Inc.	Suffolk Construction Company	Consulting Engineering Services, LLC	



2012	201202640305	Scituate	Gates Intermediate School	Building Complete	Core Program	New Construction	DBB	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP USA
2017	201702650015	Seekonk	Midred Aitken Elementary School	Building Complete	Accelerated Repair	Windows / Doors	DBB	Colliers Project Leaders NE, LLC	Gale Associates, Inc.	Lizotte Glass	Thompson & Lichtner Co., Inc.
2016	201602660505	Sharon	Sharon High	Approved Project Vote Pending	Core Program	New Construction		PMA Consultants, LLC	Tappe Architects, Inc.	-	-
2015	201502710005	Shrewsbury	Beal School	Construction	Core Program	New Construction	CM@R	PMA Consultants, LLC	Lamoureux Pagano Associates Architects, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2017	201702730305	Somerset	Somerset Middle School	Feasibility Study	Core Program			CGA Project Management	Ai3 Architects LLC	-	-
2013	201302740505	Somerville	Somerville High	Construction	Core Program	Addition / Renovation	CM@R	PMA Consultants, LLC	Symmes Maini & McKee Associates, Inc.	Suffolk Construction Company	WSP USA
2016	201602740120	Somerville	Winter Hill Community	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Municipal Building Consultants, Inc.	TSKP Studio, LLC	Lockheed Window Corporations	Thompson & Lichtner Co., Inc.
2019	201902760008	Southborough	Mary E Finn School	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-
2018	201807670505	Spencer-E Brookfield	David Prouty High	Eligibility Period	Core Program			-	-	-	-
2016	201602810095	Springfield	Alfred G. Zanetti Montessori Magnet School	Closeout	Accelerated Repair	Windows / Doors	DBB	Leftfield, LLC	Gale Associates, Inc.	D.A. Sullivan & Sons, Inc.	Building Enclosure Associates, LLC
2016	201602810360	Springfield	Balliet Middle School	Closeout	Accelerated Repair	Windows / Doors	DBB	Leftfield, LLC	Gale Associates, Inc.	W.J. Mountford Company	Building Enclosure Associates, LLC
2015	201502810025	Springfield	Brightwood School	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	DiNisco Design, Inc.	-	WSP USA
2015	201502810035	Springfield	Daniel B Brunton	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	CBI Consulting LLC	Five Star Building Corp.	Building Enclosure Associates, LLC
2019	201902810080	Springfield	Frederick Harris	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-
2018	201802810530	Springfield	High School/Science-Tech	Design Development	Accelerated Repair	Boiler	DBB	Architectural Consulting Group, LLC	Shekar & Associates, Inc.	-	Colliers Project Leaders NE, LLC
2019	201902810100	Springfield	Indian Orchard Elem	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-
2016	201602810110	Springfield	Kensington Avenue School	Closeout	Accelerated Repair	Roof	DBB	Leftfield, LLC	Gale Associates, Inc.	Greenwood Industries, Inc.	Building Enclosure Associates, LLC
2016	201602810330	Springfield	M Marcus Kiley Middle	Closeout	Accelerated Repair	Windows / Doors	DBB	Leftfield, LLC	Gale Associates, Inc.	D.A. Sullivan & Sons, Inc.	Building Enclosure Associates, LLC
2016	201602810140	Springfield	Mary M Lynch	Closeout	Accelerated Repair	Roof	DBB	Leftfield, LLC	Gale Associates, Inc.	Greenwood Industries, Inc.	Building Enclosure Associates, LLC
2015	201502810155	Springfield	Mary M Walsh	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	CBI Consulting LLC	PDS Engineering and Construction, Inc.	Building Enclosure Associates, LLC
2018	201802810023	Springfield	Milton Bradley School	Construction	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	Kaestle Boos Associates, Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
2017	201702810355	Springfield	South End Middle School	Building Complete	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	CGKV Architects, Inc.	W.J. Mountford Company	Building Enclosure Associates, LLC
2015	201502810550	Springfield	Springfield Public Day High School	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	CBI Consulting LLC	Westfield Construction Co., Inc.	Building Enclosure Associates, LLC
2015	201502810350	Springfield	STEM Middle Academy	Final Audit Approved	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	CBI Consulting LLC	Westfield Construction Co., Inc.	Building Enclosure Associates, LLC
2019	201902810160	Springfield	Sumner Avenue	Eligibility Period	Accelerated Repair	Boiler		-	-	-	-
2016	201602810015	Springfield	Thomas M Balliet	Closeout	Accelerated Repair	Roof	DBB	Leftfield, LLC	Gale Associates, Inc.	W.J. Mountford Company	Building Enclosure Associates, LLC
2016	201602810045	Springfield	William N. DeBerry	Feasibility Study	Core Program			Skanska USA Building, Inc	DiNisco Design, Inc.	-	-
2018	201802840505	Stoneham	Stoneham High	OPM Selection	Core Program			-	-	-	-
2014	201402850025	Stoughton	Joseph H. Gibbons Elementary School	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Atlantic Construction and Management, Inc.	CGKV Architects, Inc.	A&A Window Products, Inc.	Building Enclosure Associates, LLC
2013	201302850505	Stoughton	Stoughton High	Building Complete	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Drumme Rosane Anderson, Inc.	Consigli Construction Company, Inc.	Fitzemeyer & Tocci Associates, Inc.
2015	201502850020	Stoughton	West Elementary School	Building Complete	Accelerated Repair	Windows / Doors	DBB	Compass Project Management, Inc.	CBI Consulting LLC	Alpha Contracting Associates, Inc.	Building Enclosure Associates, LLC
2017	201702910010	Swampscott	Hadley	Designer Selection	Core Program			-	-	-	-
2018	201802920505	Swansea	Joseph Case High	Schematic Design	Accelerated Repair	Boiler		Vertex Construction Services	Architectural Engineers, Inc.	-	-



2018	201807700405	Tantasqua	Tantasqua Reg Jr High	Design Development	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	Next Phase Studios, Inc.	-	R.J. Kenney Associates, Inc.
2015	201502930007	Taunton	Edmund Hatch Bennett	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	TRAC Builders, Inc.	Gale Associates, Inc.
2015	201502930042	Taunton	Joseph H Martin	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	TRAC Builders, Inc.	Gale Associates, Inc.
2014	201402930015	Taunton	Mulcahey Elementary School	Construction	Core Program	New Construction	DBB	CGA Project Management	Dore & Whittier Architects, Inc.	Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
2018	2018029300525	Taunton	Taunton Alternative High School	Design Development	Accelerated Repair	Roof, Windows / Doors	DBB	NETCO Construction Project Managers, Inc.	Simpson Gumpertz & Heger Inc.	-	Building Enclosure Associates, LLC
2015	201502950025	Tewksbury	Louise Davy Trahan Elementary School	Design Development	Core Program	New Construction		CBRE/HEERY	Flansburgh Associates, Inc.	-	Consulting Engineering Services, LLC
2016	201602980005	Topsfield	Proctor Elementary School	Closeout	Accelerated Repair	Roof	DBB	Compass Project Management, Inc.	The S/L/A/M Collaborative	Northern Contracting	Gale Associates, Inc.
2016	201602980010	Topsfield	Steward Elementary School	Closeout	Accelerated Repair	Roof	DBB	Compass Project Management, Inc.	The S/L/A/M Collaborative	Northern Contracting	Gale Associates, Inc.
2015	201507730025	Triton	Pine Grove	Building Complete	Core Program	Addition / Renovation	CM@R	Pinck & Co., Inc.	Dore & Whittier Architects, Inc.	W. T. Rich Company Inc.	BVH Integrated Services, P.C.
2018	201803010305	Tyngsborough	Tyngsborough Middle	Eligibility Period	Core Program			-	-	-	-
2009	200907750305	Wachusett	Mountview Middle School	Final Audit Approved	Core Program	New Construction	DBB	-	Lamoureux Pagano Associates Architects, Inc.	CTA Construction Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2019	201903050020	Wakefield	Greenwood	Eligibility Period	Accelerated Repair	Roof		-	-	-	-
2018	201803070305	Walpole	Bird Middle	OPM Selection	Core Program			-	-	-	-
2014	201403080505	Waltham	Waltham Sr High	Schematic Design	Core Program	New Construction		NV5 (fka Joslin, Lesser + Associates Inc.)	Symmes Maini & McKee Associates, Inc.	-	-
2018	201803090020	Ware	Stanley M Koziol Elem Sch	Building Complete	Accelerated Repair	Boiler	DBB	Hill International Company	CGKV Architects, Inc.	-	NV5
2018	201803090305	Ware	Ware Middle School	Design Development	Accelerated Repair	Windows / Doors	DBB	-	CGKV Architects, Inc.	-	CBI Consulting LLC
2015	201503100003	Wareham	John William Decas	Closeout	Accelerated Repair	Roof, Boiler	DBB	Colliers Project Leaders NE, LLC	ICON architecture, inc.	Nadeau Corporation	Bard, Rao + Athanas Consulting Engineers, LLC Gale Associates, Inc.
2015	201503100017	Wareham	Minot Forest	Design Development	Core Program	New Construction		PMA Consultants, LLC	Mount Vernon Group Architects, Inc.	Sumco Eco-Contracting, LLC	Symmes, Maini & McKee Associates
2017	201703140505	Watertown	Watertown High School	Feasibility Study	Core Program			Compass Project Management, Inc.	-	-	-
2015	201503140305	Watertown	Watertown Middle School	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	exPERTcon, Inc.	Gale Associates, Inc.	Homer Contracting	Thompson & Lichtner Co., Inc.
2014	201403150005	Wayland	Claypit Hill School	Closeout	Accelerated Repair	Windows / Doors	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	Lockheed Window Corporations	Russo Barr Associates, Inc.
2016	201603150020	Wayland	Loker School	Closeout	Accelerated Repair	Windows / Doors	DBB	Colliers Project Leaders NE, LLC	CBI Consulting LLC	GVW, Inc.	Thompson & Lichtner Co., Inc.
2019	201903150020	Wayland	Loker School	Eligibility Period	Accelerated Repair	Roof		Architectural Consulting Group, LLC	-	-	-
2018	201803160505	Webster	Bartlett Jr Sr High Sch	Eligibility Period	Core Program			-	-	-	-
2017	201703170050	Wellesley	Upham Elementary School	Feasibility Study	Core Program			Compass Project Management, Inc.	Symmes Maini & McKee Associates, Inc.	-	-
2018	201803230305	West Bridgewater	Howard School	Construction	Accelerated Repair	Roof	DBB	JACOBS Project Management Co.	Mount Vernon Group Architects, Inc.	MDM Engineering	Russo Barr Associates, Inc.
2010	201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Final Audit Approved	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Flansburgh Associates, Inc.	CTA Construction Co., Inc.	Cannon Design
2015	201503320007	West Springfield	Phillip G. Coburn Elementary School	Design Development	Core Program	New Construction		NV5 (fka Joslin, Lesser + Associates Inc.)	TSKP Studio, LLC	-	-
2018	201803210025	Westborough	Elsie A Hastings Elem	Schematic Design	Accelerated Repair	Roof, Windows / Doors, Boiler		Leftfield, LLC	Dietz & Company Architects, Inc.	-	-
2016	201603210010	Westborough	Fales Elementary School	Design Development	Core Program	New Construction	CM@R	Vertex Construction Services	HMFH Architects, Inc.	Gilbane Building Company	Fitzmeyer & Tocci Associates, Inc.
2009	200903210305	Westborough	Gibbons Middle School	Closeout	Core Program	Repair	CM@R	CBRE/HEERY	Habeeb & Associates Architects, Inc.	Gilbane Building Company	BVH Integrated Services, P.C.
2018	201803250015	Westfield	Franklin Ave	Eligibility Period	Core Program			-	-	-	-



2017	201703260004	Westford	Abbot Elementary	Final Audit Approved	Accelerated Repair	Roof	DBB	Leftfield, LLC	Raymond Design Associates, Inc.	Titan Roofing, Inc.	CBI Consulting LLC
2019	201903310030	Westport	Westport Elementary	Eligibility Period	Accelerated Repair	Roof	-	-	-	-	-
2014	201403310305	Westport	Westport Junior/Senior High School	Construction	Core Program	New Construction	CM@R	Daedalus Projects Inc	Jonathan Levi Architects LLC	-	BVH Integrated Services, P.C.
2017	201703350015	Westwood	Hanlon Elementary School	Feasibility Study	Core Program	-	-	Compass Project Management, Inc.	-	-	-
2015	201503360020	Weymouth	Maria Weston Chapman Middle School	Design Development	Core Program	Addition / Renovation	-	Hill International Company	HMFH Architects, Inc.	-	WSP USA
2019	201903360085	Weymouth	Ralph Talbot	Eligibility Period	Accelerated Repair	Boiler	-	-	-	-	-
2017	201703360105	Weymouth	Thomas W. Hamilton Primary School	Closeout	Accelerated Repair	Boiler	DBB	Atlantic Construction and Management, Inc.	BLW Engineers, Inc.	AAlanco Service Corporation	Fitzemeyer & Tocci Associates, Inc.
2017	201703360110	Weymouth	Wessagusset Primary School	Closeout	Accelerated Repair	Boiler	DBB	Atlantic Construction and Management, Inc.	BLW Engineers, Inc.	AAlanco Service Corporation	Fitzemeyer & Tocci Associates, Inc.
2009	200903420505	Wilmington	Wilmington High School	Closeout	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
2010	201003440505	Winchester	Winchester High School	Closeout	Core Program	Addition / Renovation	CM@R	Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	NV5
2012	201203470060	Woburn	Wyman	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	DiNisco Design, Inc.	CTA Construction Co., Inc.	Fitzemeyer & Tocci Associates, Inc.
2016	201603480020	Worcester	Belmont Street Community	Closeout	Accelerated Repair	Windows / Doors	DBB	Watermark Environmental, Inc.	Tighe & Bond, Inc.	Stutman Contracting, Inc.	Russo Barr Associates, Inc.
2019	201903480035	Worcester	Burncoat Street	Eligibility Period	Accelerated Repair	Roof	-	exPERTcon, Inc.	-	-	-
2018	201803481008	Worcester	Challenge and Reach Academy	Design Development	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Arcadis U.S., Inc.	Johnson Roberts Associates, Inc.	-	Colliers Project Leaders NE, LLC
2016	201603480050	Worcester	Chandler Elementary Community	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Watermark Environmental, Inc.	Tighe & Bond, Inc.	Stutman Contracting, Inc.	BVH Integrated Services, P.C. Russo Barr Associates, Inc.
2016	201603480512	Worcester	Doherty Memorial High	Feasibility Study	Core Program	-	-	Tishman Construction Corporation of MA	Lamoureux Pagano Associates Architects, Inc.	-	-
2017	201703480095	Worcester	Elm Park Community	Construction	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Atane Engineers, P.C.	Fontaine Brothers, Inc.	Russo Barr Associates, Inc.
2015	201503480090	Worcester	Flagg Street	Closeout	Accelerated Repair	Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
2015	201503480177	Worcester	Francis J McGrath Elementary	Closeout	Accelerated Repair	Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
2016	201603481004	Worcester	Gerald Creamer Center	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Watermark Environmental, Inc.	Tighe & Bond, Inc.	Stutman Contracting, Inc.	BVH Integrated Services, P.C. Russo Barr Associates, Inc.
2015	201503480115	Worcester	Grafton Street	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
2015	201503480140	Worcester	Jacob Hiatt Magnet	Closeout	Accelerated Repair	Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
2017	201703480160	Worcester	Lincoln Street	Construction	Accelerated Repair	Roof, Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Atane Engineers, P.C.	Fontaine Brothers, Inc.	Russo Barr Associates, Inc.
2019	201903480160	Worcester	Lincoln Street	Eligibility Period	Accelerated Repair	Boiler	-	exPERTcon, Inc.	-	-	-
2012	201203480200	Worcester	Nelson Place	Final Audit Approved	Core Program	New Construction	CM@R	Tishman Construction Corporation of MA	Lamoureux Pagano Associates Architects, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2014	201403480520	Worcester	South High Community	Construction	Core Program	New Construction	CM@R	CBRE/HEERY	Lamoureux Pagano Associates Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2019	201903480230	Worcester	Tatnuck	Eligibility Period	Accelerated Repair	Roof	-	exPERTcon, Inc.	-	-	-
2017	201703480235	Worcester	Thorndyke Road	Construction	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Atane Engineers, P.C.	Fontaine Brothers, Inc.	Russo Barr Associates, Inc.
2019	201903480280	Worcester	Vernon Hill School	Eligibility Period	Accelerated Repair	Roof	-	exPERTcon, Inc.	-	-	-
2016	201603480026	Worcester	Wawecus Road School	Closeout	Accelerated Repair	Windows / Doors	DBB	Watermark Environmental, Inc.	Tighe & Bond, Inc.	Stutman Contracting, Inc.	Russo Barr Associates, Inc.



2019	201903480420	Worcester	Worcester East Middle	Eligibility Period	Accelerated Repair	Roof	exPERTcon, Inc.	-	-	-
------	--------------	-----------	-----------------------	--------------------	--------------------	------	-----------------	---	---	---

APPENDIX B
2019-21 ESTIMATED BID DATES

2019 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 20, 2019

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes	2019											
									November	December	January	February	March	April	May	June	July	August	September	October
Taunton	ES	735	New	\$ 65.0	Wed 11/28/18	Fri 1/25/19	\$ 50.1	NTP targeted: January 2019												
Middleborough	HS	720	New	\$ 103.5	Fri 12/14/18	Fri 2/8/19	\$ 83.6	NTP targeted: February 2019												
Worcester	HS	1420	New	\$ 210.0	Wed 1/16/19	Tue 5/28/19	\$ 173.1	GMP targeted: May 2019												
Natick	MS	1000	New	\$ 109.6	Tue 1/22/19	Wed 3/6/19	\$ 87.6	NTP targeted: March 2019												
Ludlow	ES	630	New	\$ 57.5	Fri 3/1/19	Tue 5/14/19	\$ 45.8	NTP targeted: May 2019												
Harvard	ES	445	New	\$ 53.6	Mon 4/8/19	Thu 8/15/19	\$ 43.2	GMP targeted: August 2019												
Boston	HS	500	New	\$ 124.8	Thu 5/2/19	Tue 12/31/19	\$ 96.5	GMP targeted: October 2019												
Springfield	ES	800	New	\$ 82.2	Thu 7/18/19	Thu 10/31/19	\$ 67.1	GMP targeted: October 2019												
Foxborough	ES	270	Add / Reno	\$ 34.7	Tue 8/6/19	Fri 9/20/19	\$ 27.1	NTP targeted: September 2019												
Fall River	HS	2570	New	\$ 263.5	Mon 8/12/19	Mon 12/16/19	\$ 218.1	GMP targeted: December 2019												
Bristol County	HS	640	Add / Reno	\$ 103.8	Mon 9/2/19	Wed 11/27/19	\$ 84.1	GMP targeted: November 2019												
Manchester - Essex	ES	335	New	\$ 52.2	Fri 9/6/19	Tue 11/12/19	\$ 41.3	GMP targeted: November 2019												

Construction Manager at Risk Project CMR Project Pending Local Approval Filed Sub Bids

 Design Bid Build Project DBB Project Pending Local Approval GC Bids/GMP Execution

The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

Projects represented by a single black diamond have not completed a Schematic Design Submission.

Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval. Note: Budget values are in millions.

2019 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 20, 2019

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes	2019																	
									November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	
Attleboro	HS	1725	New	\$ 259.9	Mon 9/30/19	Fri 3/6/20	\$ 223.4	GMP targeted: March 2020										9/30	Attleboro High School							3/6
Easthampton	ES	1010	New	\$ 109.2	Thu 10/3/19	Tue 11/26/19	\$ 90.1	NTP targeted: November 2019										10/3	Easthampton - Maple Elementary School							11/26
Shrewsbury	ES	790	New	\$ 92.8	Mon 10/7/19	Tue 11/26/19	\$ 74.4	GMP targeted: November 2019										10/7	Shrewsbury - Beal Elementary School							11/26
Westport	MSHS	860	New	\$ 96.9	Wed 10/9/19	Sat 11/30/19	\$ 79.9	GMP targeted: October 2019										10/9	Westport MSHS							11/30
Northbridge	ES	1030	New	\$ 101.0	Wed 10/9/19	Mon 12/9/19	\$ 79.7	GMP targeted: December 2019										10/9	Northbridge - Balmer Elementary School							12/9
Danvers	ES	465	New	\$ 52.0	Fri 11/1/19	Fri 12/27/19	\$ 42.2	GMP targeted: December 2019										11/1	Danvers - Ivan G. Smith Elementary School							12/27
Framingham	MS	630	New	\$ 98.3	Fri 11/15/19	Fri 1/3/20	\$ 78.3	GMP targeted: February 2020										11/15	Framingham - Fuller Middle School							1/3
Total		16575		\$ 2,070.1			\$ 1,685.5																			

Construction Manager at Risk Project		CMR Project Pending Local Approval		Filed Sub Bids	
Design Bid Build Project		DBB Project Pending Local Approval		GC Bids/GMP Execution	

The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

Projects represented by a single black diamond have not completed a Schematic Design Submission.

Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval. Note: Budget values are in millions.

2020 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 20, 2019

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes	Dec '19	Jan '20	Feb '20	Mar '20	Apr '20	May '20	Jun '20	Jul '20	Aug '20	Sep '20	Oct '20	Nov '20	Dec '20	Jan '21	Feb '21								
Belmont	HS	2215	New	\$ 295.2	Mon 12/16/19	Fri 2/28/20	\$ 237.1	GMP targeted: February 2020	Belmont High School 12/16 2/28 1/29																						
Wareham	ES	1020	New	\$ 90.5	Tue 12/31/19	Mon 2/10/20	\$ 72.1	NTP targeted: February 2020	Wareham - Minot Forest Elementary School 12/31 2/10 1/27																						
Westborough	ES	400	New	\$ 56.9	Mon 2/24/20	Fri 5/15/20	\$ 45.8	GMP targeted: May 2020	Westborough - Annie E. Fales Elementary School 2/24 5/15 3/25																						
Tewksbury	ES	790	New	\$ 98.5	Mon 4/20/20	Fri 6/26/20	\$ 77.7	GMP targeted: June 2020	Tewksbury - Louise Davy Trahan Elementary School 4/20 6/26 6/12																						
Central Berkshire	HS	460	New	\$ 72.7	Thu 5/14/20	Mon 6/29/20	\$ 59.8	GMP targeted: June 2020	Central Berkshire - Wahconah Regional High School 5/14 6/29 6/15																						
Pentucket	HS	965	New	\$ 146.3	Tue 5/19/20	Tue 7/14/20	\$ 118.8	GMP targeted: July 2020	Pentucket Regional High School 5/19 7/14 6/30																						
Marblehead	ES	450	New	\$ 55.6	Tue 5/26/20	Tue 10/27/20	\$ 44.0	GMP targeted: October 2020	Marblehead - Elbridge Gerry Elementary School 5/26 10/27 9/28																						
West Springfield	ES	585	New	\$ 69.0	Thu 7/30/20	Thu 9/10/20	\$ 54.7	NTP targeted: September 2020	West Springfield - Coburn Elementary School 7/30 9/10 8/26																						
Weymouth	MS	1470	Add / Reno	\$ 164.2	Wed 8/12/20	Fri 9/25/20	\$ 128.6	GMP targeted: September 2020	Weymouth - Maria Weston Chapman Middle School 8/12 9/25 9/11																						
Gardner	ES	925	New	\$ 89.6	Wed 8/19/20	Thu 10/1/20	\$ 70.9	NTP targeted: October 2020	Gardner - Waterford Street Elementary School 8/19 10/1 9/17																						
Braintree	MS	800	New	\$ 86.6	Mon 9/7/20	Wed 11/11/20	\$ 69.2	NTP targeted: November 2020	Braintree South Middle School 9/7 11/11 10/21																						
Arlington	HS	1755	New	\$ 290.9	Mon 9/7/20	Thu 12/10/20	\$ 235.8	GMP targeted: December 2020	Arlington High School 9/7 12/10 11/18																						

Construction Manager at Risk Project CMR Project Pending Local Approval Filed Sub Bids
 Design Bid Build Project DBB Project Pending Local Approval GC Bids/GMP Execution

The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

Projects represented by a single black diamond have not completed a Schematic Design Submission.




Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval. Note: Budget values are in millions.




2020 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 20, 2019

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes																	
									Dec '19	Jan '20	Feb '20	Mar '20	Apr '20	May '20	Jun '20	Jul '20	Aug '20	Sep '20	Oct '20	Nov '20	Dec '20	Jan '21	Feb '21		
Bridgewater - Raynham	ES	740	New	\$ 80.6	Thu 9/10/20	Wed 9/30/20	\$ 64.7	NTP targeted: September 2020									Bridgewater-Raynham - Mitchell Elementary School								
																	9/10	9/25	9/30						
Sharon	HS	1250	New	\$ 163.0	Mon 10/26/20	Sun 12/20/20	\$ 126.2	GMP targeted: December 2021...											10/26	11/16	12/20				
Amesbury	ES	425	New	\$ 60.5	Wed 11/4/20	Wed 12/30/20	\$ 49.0	NTP targeted: December 2020										11/4	12/11	12/30					
Total		14250		\$ 1,820.0			\$ 1,454.3																		

Construction Manager at Risk Project  CMR Project Pending Local Approval  Filed Sub Bids 

Design Bid Build Project  DBB Project Pending Local Approval  GC Bids/GMP Execution 

The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

Projects represented by a single black diamond have not completed a Schematic Design Submission.

Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval. Note: Budget values are in millions.

2021 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 20, 2019

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes	Nov '20	Dec '20	Jan '21	Feb '21	Mar '21	Apr '21	May '21	Jun '21	Jul '21	Aug '21	Sep '21	Oct '21	Nov '21	Dec '21	Jan '22
									Millbury	ES	550	New	\$ 60.9	Wed 12/9/20	Tue 2/9/21	\$ 49.3	NTP targeted: February 2021...	Millbury - Shaw Elementary School 12/9 2/9 1/9					
Acton - Boxborough	ES	650	New	\$ 117.3	Tue 12/15/20	Mon 2/15/21	\$ 95.4	GMP targeted: February 2021...	Acton-Boxborough - CT Douglas Elementary School 12/15 2/15 1/15														
Easton	ES	760	New	\$ 94.8	Wed 12/23/20	Tue 2/9/21	\$ 74.9	NTP targeted: February 2021...	Easton - Center Elementary School 12/23 2/9 1/26														
Rockland	ES	760	New	\$ 86.6	Wed 1/6/21	Tue 2/16/21	\$ 68.2	NTP targeted: February 2021...	Rockland - Jefferson Elementary School 1/6 2/16 2/2														
Lowell	HS	3520	Add / Reno	\$ 343.4	Mon 2/1/21	Fri 5/7/21	\$ 271.2	GMP targeted: May 2021	Lowell High School 2/1 5/7 3/5														
Waltham	HS	1830	New		Mon 2/1/21	Wed 4/21/21		GMP targeted: April 2021...	Waltham Senior High School 2/1 4/21 3/1														
Nauset	HS	905	Add / Reno		Tue 5/25/21	Tue 5/25/21		GMP targeted: May 2021	Nauset Regional High School 5/25														
Leicester	MS	930	New		Mon 7/26/21	Mon 7/26/21		NTP targeted: July 2021	Leicester Middle School 7/26														
Total		9905		\$ 703.1			\$ 559.1																

Construction Manager at Risk Project CMR Project Pending Local Approval Filed Sub Bids
 Design Bid Build Project DBB Project Pending Local Approval GC Bids/GMP Execution

The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

Projects represented by a single black diamond have not completed a Schematic Design Submission.


Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval. Note: Budget values are in millions.

APPENDIX C
SCHOOL CONSTRUCTION COSTS COMPARED
TO COMMON ECONOMIC INDICATORS

New Construction Costs Compared to Common Economic Indicators | November 20, 2019

Legend


- New Construction PSR - Board Vote +
- New Construction SD
- New Construction Vote Failed ×
- New Construction Bid
- New Construction PFA Amended ■
- New Construction PSR +
- 3% Escalation
- Average- New Construction Projects —
- BLS PPI- New School Construction —
- MSBA Construction Funding Limit —
- RLB Comparative Cost- Boston —
- Average \$/SF for Add/Reno —

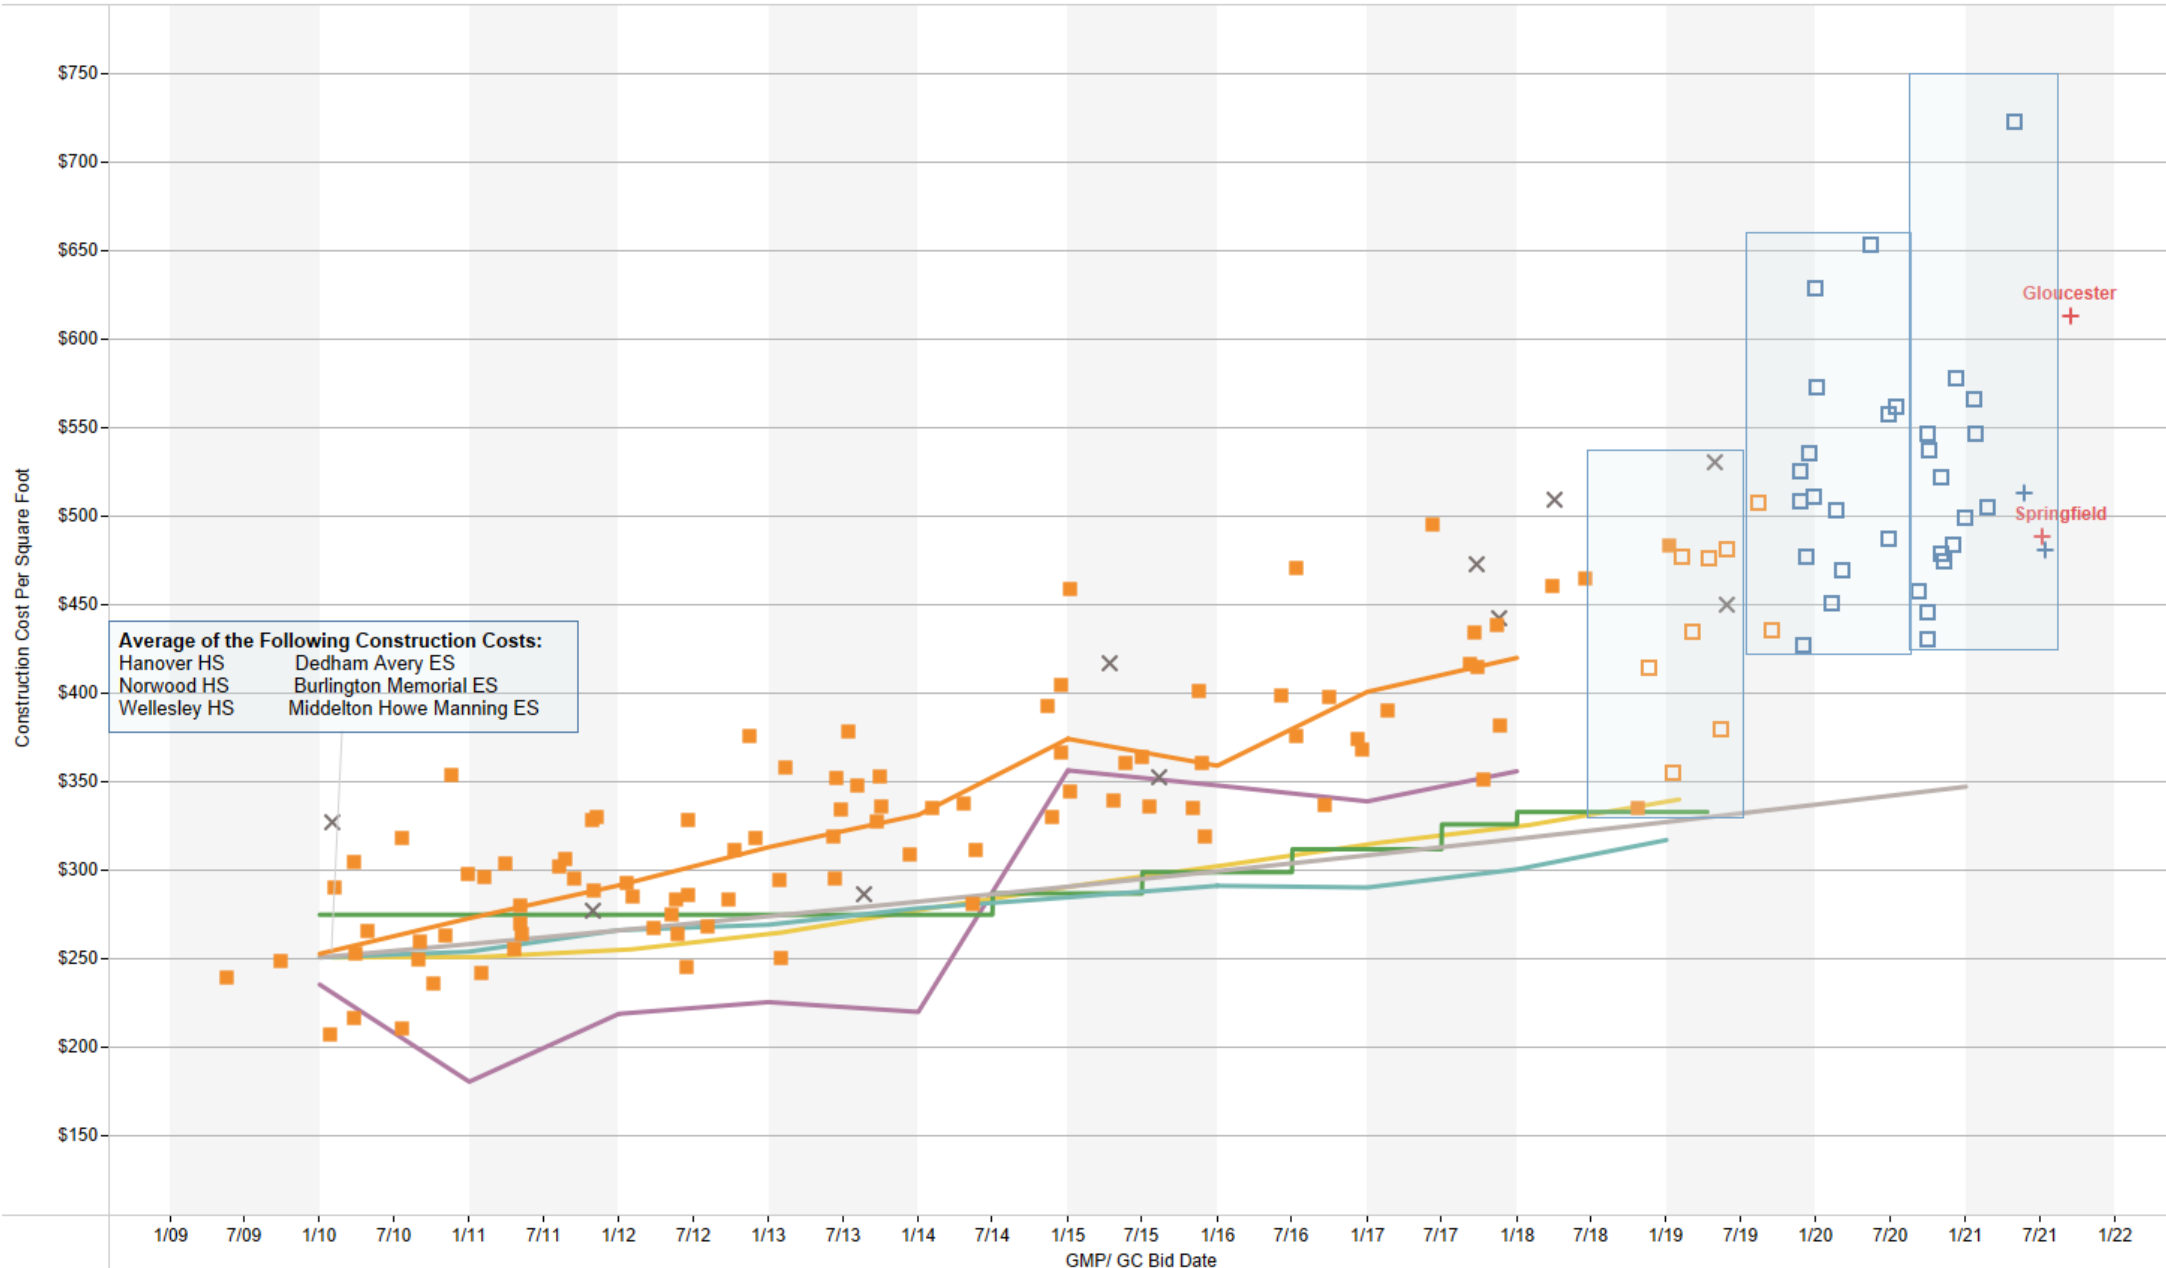

Average of the Following Construction Costs:
 Hanover HS Dedham Avery ES
 Norwood HS Burlington Memorial ES
 Wellesley HS Middleton Howe Manning ES

The information and data contained in this chart is based on the MSBA's review of construction cost estimates, contracts and other documentation provided by cities, towns, and regional school districts. This information and data is intended for informational purposes only. The data may have changed based on actual construction bids or contract amendments, for example, and the MSBA shall have no responsibility or duty to update any of the information. Please contact the Districts for the most current information. The MSBA hereby disclaims any and all liability and responsibility that may arise in connection with the information contained in this chart. (Updated November 2019)

Addition/Renovation Costs Compared to Common Economic Indicators | November 20, 2019

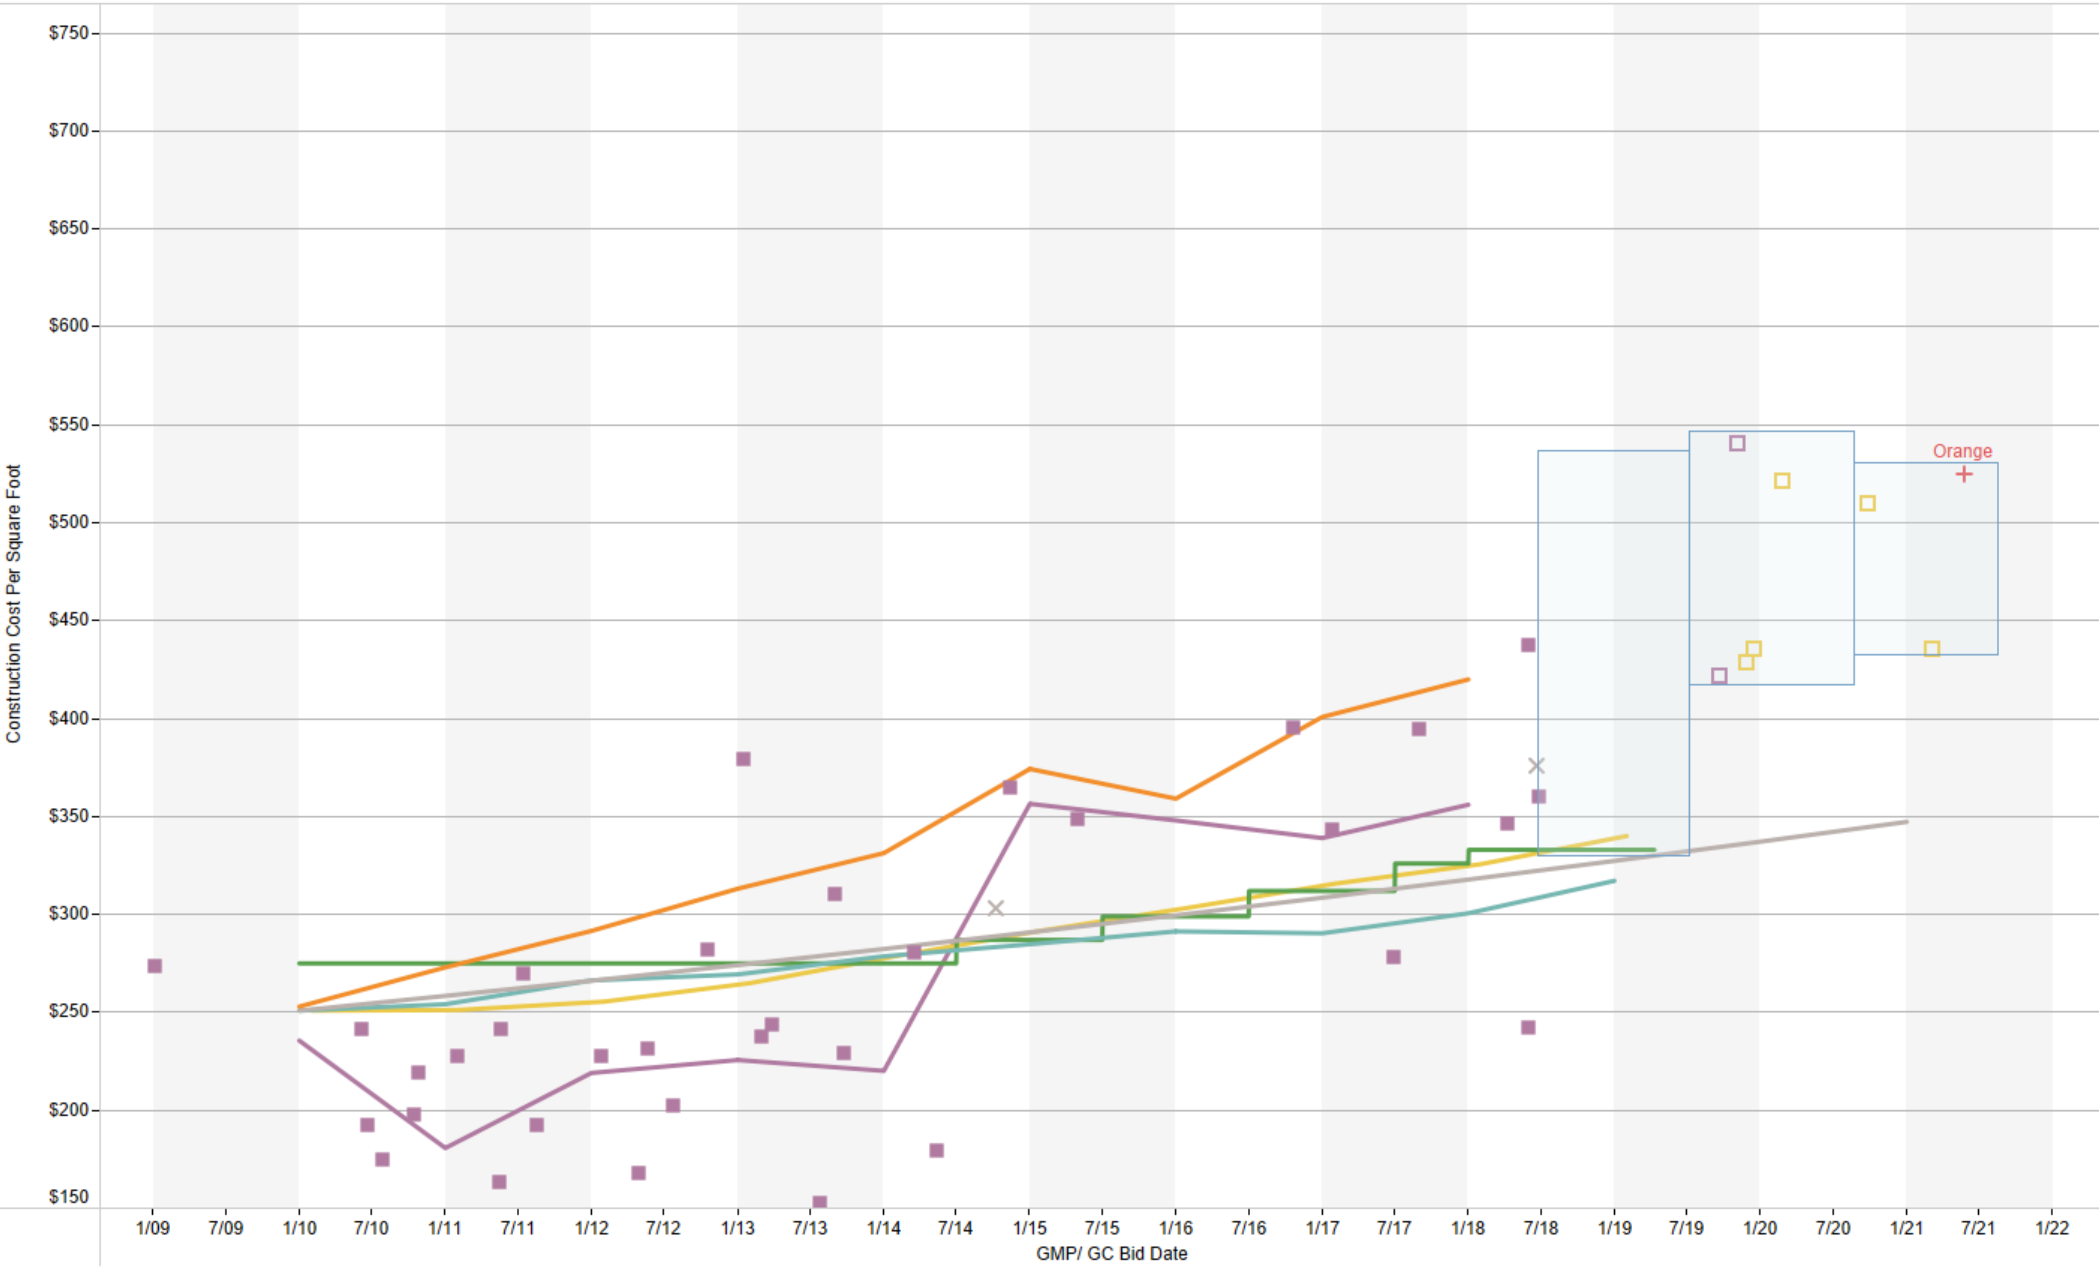

- Legend**
- Addition / Renovation PFA Amended ■
 - Addition / Renovation Bid □
 - Addition / Renovation SD □
 - Addition / Renovation Vote Failed ×
 - Addition / Renovation PSR - Board Vote +
 - 3% Escalation —
 - Average- New Construction Projects —
 - BLS PPI- New School Construction —
 - MSBA Construction Funding Limit —
 - RLB Comparative Cost- Boston —
 - Average \$/SF for Add/Reno —


An orange average line of new construction costs is included for reference.

The information and data contained in this chart is based on the MSBA's review of construction cost estimates, contracts and other documentation provided by cities, towns, and regional school districts.

This information and data is intended for informational purposes only. The data may have changed based on actual construction bids or contract amendments, for example, and the MSBA shall have no responsibility or duty to update any of the information.

Please contact the Districts for the most current information. The MSBA hereby disclaims any and all liability and responsibility that may arise in connection with the information contained in this chart. (Updated November 2019)

Projects Below \$150/ SF

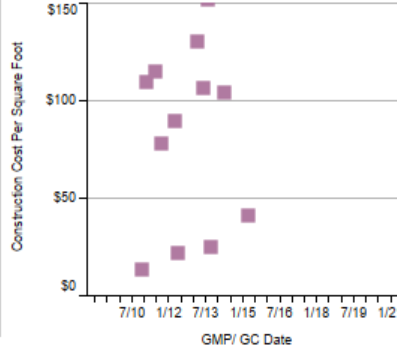

APPENDIX D
CONSTRUCTION STATUS REPORT

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of November 08, 2019**

Core Program and Waitlist Totals			\$3,127,894,333																Includes Alternates		\$1,707,647,409
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion Date *	Building Construction Complete **	Schedule Variance (days) ***	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant		
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																					
Core Program Totals			\$3,127,894,333																	\$1,707,647,409	
Bourne Peebles Elementary School	Elementary School	Brait Builders Corp.	\$30,910,366	460	Bid	73,348	\$421	\$19,234,295	\$262	Design/Bid/Build	30-Nov-17	20-May-19	30-Apr-19	20 ahead	99%	\$252,454	0.817%	Punch list items, mechanical and system controls, repairs in the kitchen, roof leak testing and repairs are all ongoing activities. Site maintenance and landscaping activities are in progress.	\$14,321,258		
Cape Cod Region Voc Tech Cape Cod Region Voc Tech	Vocational/Technical	Brait Builders Corp.	\$104,223,800	650	PFA	220,880	\$472	\$65,139,000	\$295	Design/Bid/Build	01-Dec-18	04-Feb-21		0	38%	\$559,209	0.537%	Masonry veneers are ongoing on the rear elevation of the classroom wings. Stair 1 concrete pours are ongoing. Spray fireproofing is ongoing. Steel is being prepared for intumescent paint. Metal framing is ongoing, dense-glass is ongoing and spray Air Vapor barrier is following behind. Windows are working from the top down. Metal panels are following. Roofing is ongoing, flashing is ongoing. Mechanical, Electrical and Plumbing rough-ins are ongoing. Overhead garage door installation is ongoing.	\$45,721,370		
Dedham Early Childhood Center	Elementary School	H.V. Collins Co., Inc.	\$23,213,553	200	Bid	50,988	\$455	\$13,010,627	\$255	Design/Bid/Build	16-Oct-17	25-Feb-19	07-Feb-19	18 ahead	99%	\$1,062,179	4.576%	Construction and commissioning punch list items are ongoing.	\$10,498,016		
Hanover Sylvester	Elementary School	Brait Builders Corp.	\$23,075,675	560	Bid	90,975	\$254	\$17,678,117	\$194	Design/Bid/Build	24-Jul-17	13-Aug-19	12-Dec-18	184 ahead	99%	\$1,833,787	7.947%	Open items and corrective work such as exterior window paint work, cafeteria flooring, and control issues as well as sensor faults are on going.	\$14,878,013		
Ludlow Chapin Street Elementary School	Elementary School	Fontaine Brothers, Inc.	\$45,754,614	630	PFA	106,250	\$431	\$30,234,697	\$285	Design/Bid/Build	21-May-19	15-Apr-21		0	12%	\$11,846	0.026%	Storm drainage structures are ongoing. Infiltration basin #2 is nearly complete. A wing (classroom wing) and B wing (Core spaces) slabs are ongoing. Underground drainage and sewer pipes are ongoing. B wing underground electrical is ongoing.	\$27,522,934		
Marlborough Richer	Elementary School	Fontaine Brothers, Inc.	\$47,831,946	610	Bid	111,437	\$429	\$31,031,124	\$278	Design/Bid/Build	02-Jul-18	08-Apr-20		0	65%	\$192,338	0.402%	Concrete masonry unit block walls in the stair towers and elevator shaft work are ongoing. Roof and window installation is ongoing. Interior light gauge metal framing is ongoing in Section 2 (A and B wings-classrooms). Drywall work is ongoing in Section 1 (D wing-classrooms). Painting and ceiling grid work is ongoing in Section 1 (C -classrooms, gymnasium and cafeteria and D wing-classrooms). Parking lot work is ongoing.	\$27,295,076		
Middleborough Middleborough High	High School	Fontaine Brothers, Inc.	\$83,582,398	720	PFA	166,650	\$502	\$50,541,889	\$303	Design/Bid/Build	19-Feb-19	13-Nov-20		0	32%	\$78,116	0.094%	Construction includes steel erection in the lesser developed areas of the building, along with masonry work and slab-on-grade and slab-on-deck concrete pours. Further along sections of the building include framing, roofing, and placement of stairs and doors.	\$42,541,652		
Narragansett Templeton Center	Elementary School	Fontaine Brothers, Inc.	\$36,522,000	580	Bid	92,735	\$394	\$24,888,000	\$268	Design/Bid/Build	06-Dec-17	15-May-19	18-Jun-19	34 behind	99%	\$747,861	2.048%	Site work punch list is ongoing.	\$22,250,143		
Natick J F Kennedy Middle Sch	Middle School	Brait Builders Corp.	\$87,559,890	1,000	PFA	182,195	\$481	\$58,353,861	\$320	Design/Bid/Build	19-Mar-19	07-Oct-21		0	20%	\$243,069	0.278%	Concrete slab pours are ongoing. Steel erection is targeting completion.	\$36,650,548		
Needham Hillside Elementary	Elementary School	Bacon Construction Co, Inc.	\$45,465,414	430	Bid	90,975	\$500	\$32,250,467	\$354	Design/Bid/Build	17-Oct-17	14-Jun-19	05-Jul-19	21 behind	99%	\$913,223	2.009%	Punch list work and training are ongoing. Building Management System programming is being finalized.	\$12,931,741		
North Middlesex North Middlesex Reg	High School	CTA Construction Co., Inc.	\$64,995,000	870	Bid	180,530	\$360	\$49,909,000	\$276	Design/Bid/Build	25-May-15	23-Aug-17	23-Aug-17	0	99%	\$3,883,358	5.975%	Final site work and landscaping are ongoing.	\$38,471,881		
Revere Staff Sargent James J. Hill Elementary School	Elementary School	CTA Construction Co., Inc.	\$31,975,839	690	Bid	103,650	\$308	\$27,439,789	\$265	Design/Bid/Build	25-Mar-14	17-Aug-15	17-Aug-15	0	98%	\$1,223,263	3.826%	Commissioning and punch list items are ongoing.	\$28,099,048		
Scituate Gates Intermediate School	Middle School	Bacon-Agostini Construction Joint Venture	\$52,596,801	710	Bid	164,803	\$319	\$42,947,412	\$261	Design/Bid/Build	08-Dec-15	14-Aug-17	14-Aug-17	0	99%	\$2,388,406	4.541%	Concrete deterioration at the exterior walks and plazas remains unresolved.	\$20,436,585		
Taunton Mulcahey Elementary School	Elementary School	Agostini Construction Co., Inc.	\$50,074,205	735	PFA	119,693	\$418	\$34,127,642	\$285	Design/Bid/Build	11-Feb-19	26-Jun-20		0	35%	\$133,135	0.266%	Concrete work is nearly complete. Roof installation has commenced.	\$40,454,641		
Woburn Wyman	Elementary School	CTA Construction Co., Inc.	\$27,017,841	410	Bid	70,701	\$382	\$18,251,786	\$258	Design/Bid/Build	10-Jan-17	30-Jun-18	15-Aug-18	46 behind	99%	\$207,169	0.767%	Commissioning activities are ongoing.	\$13,974,154		
Attleboro Attleboro High	High School	Consigli Construction Company, Inc.	\$223,088,312	1,725	PFA	476,425	\$468	\$134,982,665	\$283	CM-at-Risk	13-May-19	13-May-22		0	8%	\$60,685	0.027%	Site enabling work is ongoing. Concrete work is ongoing.	\$124,276,563		
Beverly Briscoe Middle	Middle School	Bacon-Agostini Construction Joint Venture	\$90,129,432	1,395	Bid	231,509	\$389	\$62,790,920	\$271	CM-at-Risk	24-Dec-15	15-Jun-18	15-Jun-18	0	99%	\$2,149,841	2.385%	Punch list work is ongoing.	\$47,562,459		
Billerica Billerica Memorial High School	High School	Shawmut Design and Construction	\$140,773,848	1,610	Bid	325,191	\$433	\$79,526,376	\$245	CM-at-Risk	13-Feb-17	29-Mar-19	06-Jun-19	0	93%	\$4,063,704	2.887%	Punch list work is ongoing in the new building. Demolition of existing school continues. Site preparation for field and stadium construction is ongoing.	\$71,262,413		
Blue Hills Voc Blue Hills Reg Voc Tech	Vocational/Technical	Consigli Construction Company, Inc.	\$70,509,857	900	Bid	292,400	\$241	\$46,789,510	\$160	CM-at-Risk	28-May-18	30-Nov-19		0	92%	\$5,232,405	7.421%	Punch list work in Administration spaces, main entrance, Cosmetology and Culinary spaces are ongoing. Commissioning activities are also ongoing throughout the building.	\$43,163,727		
Boston Boston Arts Academy	High School	Lee Kennedy Co., Inc.	\$95,976,807	500	PFA	153,476	\$625	\$64,448,394	\$420	CM-at-Risk	17-Dec-18	20-Oct-21		0	11%	\$0	0.000%	Site contaminant remediation is ongoing. Steel indicator piles are in place and remaining piles will be driven in coming weeks. Dust, noise, and vibration monitoring is ongoing.	\$47,675,093		
Braintree East Middle School	Middle School	Shawmut Design and Construction	\$67,736,699	1,180	Bid	184,425	\$367	\$44,090,239	\$239	CM-at-Risk	01-May-18	01-Jul-20		0	71%	\$1,139,357	1.682%	Work to complete phase 2A is ongoing and includes Auditorium, lobby, Guidance offices, Music rooms and Band rooms. Phase 3 and 3A has commenced and includes renovation of existing classrooms, existing gymnasium and existing Cafeteria.	\$40,346,375		
Bristol County Agr Bristol County Agr High	Vocational/Technical	Gilbane Building Company	\$83,953,900	640	PFA	196,151	\$428	\$51,232,400	\$261	CM-at-Risk	01-Aug-19	26-Nov-21		0	1%	\$0	0.000%	Early site work, concrete forms and footings are ongoing.	\$51,428,124		
Brookline Edward Devotion	Elementary School	Shawmut Design and Construction	\$92,237,854	1,010	Bid	227,087	\$406	\$57,910,095	\$255	CM-at-Risk	11-Jul-16	31-Jul-18	06-Sep-18	37 behind	92%	\$1,374,002	1.490%	Additional insulation as well as heating, ventilation and air conditioning work is ongoing in the Parking Garage and Loading Dock areas.	\$25,197,463		
Fall River B M C Durfee High	High School	Suffolk Construction Company	\$217,839,610	2,570	PFA	501,330	\$435	\$138,754,022	\$277	CM-at-Risk	14-Aug-18	05-May-21		0	18%	\$0	0.000%	Steel erection is ongoing. Renovations to existing field house are ongoing.	\$165,084,900		
Harvard Hildreth Elementary School	Elementary School	Shawmut Design and Construction	\$42,999,041	445	PFA	85,214	\$505	\$26,771,866	\$314	CM-at-Risk	16-Apr-19	12-Apr-21		0	11%	\$491,928	1.144%	Steel erection is ongoing. Crews are also working on roofing and minimal utility installations.	\$18,327,080		
Lexington Maria Hastings	Elementary School	Walsh Brothers, Inc.	\$52,973,418	645	Bid	110,000	\$482	\$22,909,213	\$208	CM-at-Risk	25-Jun-18	10-Feb-20		0	80%	\$654,794	1.236%	Window installation is ongoing. Finishes are being installed in all areas of the building.	\$16,513,723		
Millis Clyde F Brown	Elementary School	Bacon-Agostini Construction Joint Venture	\$42,591,393	515	Bid	89,852	\$474	\$26,297,583	\$293	CM-at-Risk	15-Feb-18	25-May-19	07-Jun-19	21 behind	88%	\$425,044	0.998%	Project team is working to complete the punch list, playgrounds and landscaping for the new building. The demolition and abatement of the existing building is ongoing.	\$20,951,650		
Minuteman Voc Tech Minuteman Regional High	High School	Gilbane Building Company	\$119,200,892	628	Bid	257,745	\$462	\$71,673,473	\$278	CM-at-Risk	06-Jun-17	25-Sep-19		0	94%	\$1,630,356	1.368%	Minimal work remains in the areas of the theater, greenhouses, and childcare playground. Punch list work is ongoing. Abatement and demolition of the existing school is ongoing.	\$43,902,613		
Newton Cabot	Elementary School	W. T. Rich Company Inc.	\$36,690,618	480	Bid	84,262	\$435	\$26,978,824	\$320	CM-at-Risk	11-Jul-17	30-Jun-19	09-Aug-19	40 behind	92%	\$321,403	0.887%	Punch list is ongoing. Commissioning coordination is ongoing.	\$13,636,546		
Pittsfield Taconic High	High School	Gilbane Building Company	\$97,757,373	920	Bid	246,520	\$397	\$56,984,184	\$231	CM-at-Risk	21-Mar-16	29-Jun-18	27-Jul-18	0	99%	\$3,593,568	3.676%	Completion of remaining punch list items is ongoing.	\$71,935,008		
Quincy Reay E Sterling Middle	Middle School	Bond Brothers, Inc.	\$46,550,994	430	Bid	95,732	\$486	\$29,569,323	\$309	CM-at-Risk	20-Jun-17	20-May-19	20-May-19	0	99%	\$1,448,680	3.112%	Building construction includes commissioning and final punch list work.	\$28,022,957		

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of November 08, 2019**

Core Program and Waitlist Totals			\$3,127,894,333																Includes Alternates	\$1,707,647,409
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion Date *	Building Construction Complete **	Schedule Variance (days) ***	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																				
Core Program Totals			\$3,127,894,333																\$1,707,647,409	
Saugus Saugus High	High School	Suffolk Construction Company	\$128,085,356	1,360	PFA	269,070	\$476	\$77,121,412	\$287	CM-at-Risk	25-Jun-18	01-Jul-20		0	55%	\$136,734	0.107%	Exterior facade panel installation is ongoing. Interior painting and finishes are ongoing.	\$63,798,385	
Shrewsbury Beal School	Elementary School	Fontaine Brothers, Inc.	\$74,111,830	790	PFA	141,600	\$523	\$43,382,405	\$306	CM-at-Risk	02-Sep-19	28-May-21		0	6%	\$0	0.000%	Excavation and removal of old Lake Street waterline continues and the installation of a new waterline will follow. Building A (core space) and B (classroom wing) footings and foundations are nearly complete. Building C (classroom wing) is ongoing. Underground utilities are ongoing.	\$33,222,716	
Somerville Somerville High	High School	Suffolk Construction Company	\$199,051,710	1,590	PFA	369,496	\$539	\$111,565,951	\$302	CM-at-Risk	12-Jun-17	28-May-21		0	31%	\$0	0.000%	Phase 1 envelope work is ongoing. Phase 2 structural steel erection has begun. Mechanical, electrical, and plumbing rough installation work continues.	\$119,706,988	
Springfield Brightwood	Elementary School	Daniel O'Connell's Sons, Inc.	\$66,941,200	800	PFA	150,500	\$445	\$44,037,500	\$293	CM-at-Risk	20-Aug-19	30-Jun-21		0	4%	\$0	0.000%	Under slab utilities, backfilling and slab on grade concrete pours are ongoing activities. Steel is being delivered and installation will follow.	\$49,147,673	
Stoughton Stoughton High	High School	Consigli Construction Company, Inc.	\$100,961,191	1,065	Bid	214,860	\$470	\$58,510,773	\$272	CM-at-Risk	12-Jun-17	11-Jul-19	11-Jul-19	0	82%	\$2,114,294	2.175%	Punch list work is ongoing. The demolition and abatement of the existing building is ongoing.	\$50,285,284	
Triton Pine Grove	Elementary School	W. T. Rich Company Inc.	\$30,191,749	415	Bid	87,674	\$344	\$17,111,184	\$195	CM-at-Risk	09-Apr-18	26-Aug-19	23-Aug-19	3 ahead	96%	\$1,061,033	3.514%	Punch list work is ongoing. Site work and baseball field installation has commenced.	\$16,264,155	
Westport Westport Junior/Senior High School	Middle/High School	Agostini Construction Co., Inc.	\$79,880,726	860	PFA	187,100	\$427	\$46,662,684	\$249	CM-at-Risk	15-Oct-18	31-Mar-21		0	1%	\$0	0.000%	Early site package work is ongoing.	\$37,418,778	
Worcester South High Community	High School	Fontaine Brothers, Inc.	\$172,861,181	1,420	PFA	359,994	\$480	\$105,012,370	\$292	CM-at-Risk	11-Oct-18	16-Jun-21		0	25%	\$0	0.000%	Building envelope at the classroom wing and kitchen is ongoing followed by starting Auditorium and Gymnasium. Roofing is ongoing at the classroom wing, followed by the rest of the building. Interior framing is in progress at the classroom wing. Mechanical work is in progress in the classroom wing. Site work consists of completion of storm line, final placement of conduit and duct bank with a new transformer. Slabs are in progress in Auditorium and Gymnasium.	\$112,469,676	

Substantial Completion Date *
* Contract Substantial Completion Date. Field will remain blank until a contract/GMP has been executed.

Building Construction Complete **
** Field represents actual Substantial Completion date (date of Certificate of Completion).

Variance***
*** Variance is the difference between "Building Construction Completion" date and "Substantial Completion" Date. The number zero (0) will appear in this column until actual certificate of Substantial Completion is achieved.

APPENDIX E
FY19 PROJECTS SUBSTANTIALLY COMPLETE



Pittsfield | Taconic High School

Contractor – Gilbane Building Company

OPM – Skanska USA Building, Inc.

Designer – Drummey Rosane

Anderson, Inc.

Total Project Budget:

\$120,614,674

Construction Budget:

\$97,757,373

Maximum Facilities Grant:

\$73,358,780

Substantial Completion

Baseline (PFA): 6/29/18

Substantial Completion: 7/27/18

Building Construction Complete:

7/27/18





Woburn | Wyman-Hurld ES

Contractor – CTA

OPM – Municipal Building

Consultants

Designer – DiNisco

Total Project Budget:

\$34,647,722

Construction Budget:

\$27,017,841

Maximum Facilities Grant:

\$13,974,153

Substantial Completion

Baseline (PFA): 01/02/2018

Substantial Completion:

06/30/2018

Building Construction Complete:

08/15/2018





Chelsea | Clark Ave Middle School

Contractor – W.T. Rich Company, Inc.

OPM – Pinck & Co., Inc.

Designer – HMFH Architects, Inc.

Total Project Budget:

\$57,332,407

Construction Budget:

\$46,046,367

Maximum Facilities Grant:

\$37,249,593

Substantial Completion

Baseline (PFA): 7/27/18

Substantial Completion: 9/7/18

Building Construction Complete:

9/7/18





Brookline | Edward Devotion School

Contractor – Shawmut Design and Construction

OPM – Town of Brookline

Designer – HMFH Architects, Inc.

Total Project Budget:

\$120,150,000

Construction Budget:

\$89,502,172

Maximum Facilities Grant:

\$26,163,433

Substantial Completion

Baseline (PFA): 7/26/18

Substantial Completion: 9/6/18

Building Construction Complete:

9/6/18





Hopkinton | Center Elementary School

Contractor – Colantonio Inc.

OPM – Compass Project Management, Inc.

Designer – DRA Architects

Total Project Budget:

\$47,129,373

Construction Budget:

\$37,819,615

Maximum Facilities Grant:

\$14,058,455

Substantial Completion

Baseline (PFA): 8/3/18

Substantial Completion: 7/31/18

Building Construction Complete:

5/31/18





Granby | West St. Elementary School

Contractor – Fontaine Brothers

OPM – Colliers International

Designer – JWA

Total Project Budget:

\$32,390,430

Construction Budget:

\$25,957,105

Maximum Facilities Grant:

\$17,376,626

Substantial Completion

Baseline (PFA): 8/17/18

Substantial Completion: 8/15/18

Building Construction Complete:

8/1/18





Hanover | Sylvester Elementary School

Contractor – Brait Builders

OPM – P-Three, Inc.

Designer – Mount Vernon Group

Total Project Budget:

\$31,623,075

Construction Budget:

\$26,302,013

Maximum Facilities Grant:

\$15,184,916

Substantial Completion

Baseline (PFA): August 13, 2019

Substantial Completion:

December 12, 2018

Building Construction Complete:

December 12, 2018





Mt. Greylock Regional School

Contractor – Turner Construction Company

OPM – Dore & Whittier Management Partners, Inc.

Designer – Perkins Eastman

Total Project Budget:

\$64,693,600

Construction Budget:

\$52,266,600

Maximum Facilities Grant:

\$32,282,297

Substantial Completion

Baseline (PFA): 4/25/18

Substantial Completion: 1/30/19

Building Construction Complete:
8/31/19





Dedham | Early Childhood Education Center

Contractor – H.V. Collins Co., Inc.

OPM – Construction Monitoring Services, Inc.

Designer – Knight, Bagge & Anderson, Inc.

Total Project Budget:

\$28,742,179

Construction Budget:

\$21,224,028

Maximum Facilities Grant:

\$10,758,919

Substantial Completion

Baseline (PFA): 12/21/18

Substantial Completion: 2/7/19

Building Construction Complete:

9/30/19





Quincy | R.E. Sterling Middle School

(fka/Southwest MS)

Contractor – Bond Brothers

OPM – PCA360

Designer – Ai3

Total Project Budget:

\$58,173,160

Construction Budget:

\$47,235,067

Maximum Facilities Grant:

\$28,783,720

Substantial Completion

Baseline (PFA): 03/01/2019

Substantial Completion:

05/20/2019

Building Construction Complete:

5/20/2019





Billerica Memorial High School

Contractor – Shawmut Design and Construction

OPM – Leftfield

Designer – Perkins + Will

Total Project Budget:

\$175,997,289

Construction Budget:

\$140,773,848

Maximum Facilities Grant:

\$72,812,091

Substantial Completion

Baseline (PFA): March 4, 2019

Substantial Completion: June 6, 2019

Building Construction Complete: June 6, 2019





Narragansett | Templeton Center School

Contractor – Fontaine Brothers, Inc.
OPM – Colliers Project Leaders NE, LLC
Designer – Symmes Maini & McKee Associates, Inc.

Total Project Budget:

\$45,058,033

Construction Budget:

\$32,218,500

Maximum Facilities Grant:

\$22,760,779

Substantial Completion

Baseline (PFA): 5/19/2019

Substantial Completion: 6/18/2019





Bourne | Bourne Intermediate School

(fka/Peebles ES)

Contractor – Brait Builders, Inc.

OPM – SMMA

Designer – Flansburgh Architects

Total Project Budget:

\$ 38,498,867

Construction Budget:

\$27,990,000

Maximum Facilities Grant:

\$14,321,258

Substantial Completion

Baseline (PFA): 6/27/2019

Substantial Completion:

05/20/2019

Building Construction Complete:

04/30/2019





Millis | Clyde f. Brown School

Contractor – Bacon Agostini Construction
Joint Venture

OPM – Compass

Designer – Tappe

Total Project Budget:

\$51,988,519

Construction Budget:

\$41,248,039

Maximum Facilities Grant:

\$20,968,556

Substantial Completion

Baseline (PFA): 5/21/19

Substantial Completion:

Building Construction Complete:

6/7/19



Ed Wonsek Art Works Inc.
