

Massachusetts School Building Authority

CAPITAL PLANNING PROJECT OVERVIEW REPORT

July 10, 2015


TABLE OF CONTENTS

Capital Pipeline Overview	2
Statements of Interest (SOIs)	3
Core Program	4-10
Eligibility Period	4
Consultant Selection	5
Feasibility Study	6
Schematic Design	7
Commissioning	8
Design Development	9
Summary of Bid Data.....	9
Construction	10
Accelerated Repair Program	11-13
Project Variances	14-15
<i>Appendix</i>	
(A) <i>Project Status List</i>	
(B) <i>2015 & 2016 Estimated Bid Dates</i>	
(C) <i>Construction Status Report</i>	

CAPITAL PIPELINE OVERVIEW

Current Projects Status

A total of 305 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The summary chart provides the number of projects in Eligibility Period and each phase of the Capital Pipeline. For a detailed look at the Capital Pipeline projects, please go to www.massschoolbuildings.org/building and select “Capital Pipeline Status Chart”.

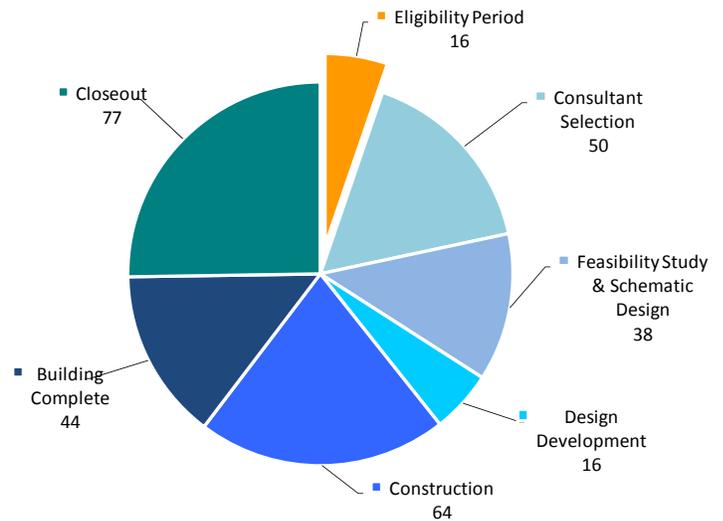

2015 Progress Report

- SOI 2015
 - 97 Core Program SOIs were received; due diligence is underway.
 - 2015 ARP SOIs were finalized with recommendations for invitation issued at the June 3, 2015 Board meeting.
- Eligibility Period
 - Collaboration with the 16 districts invited into Eligibility Period is underway. Invitations to Feasibility Study are anticipated at the upcoming August, November and January Board meetings.
- Feasibility Study/Schematic Design
 - One district received MSBA approval for selection of an OPM.
 - Three districts completed designer selection.
- Accelerated Repair Program
 - From the 2014 SOI opening, one district with two projects remains for recommendation for a Project Funding Agreement.
 - From the 2015 SOI opening, districts are underway with preliminary requirements. Consultant assignments are anticipated in August/September and Project Funding Agreement recommendations are anticipated in the fall/winter.
- Construction Costs
 - Of the 14 bids and/or execution of a GMP in 2015, eight have been reported to date.
 - Of the eight, five came in within their estimated budget, and one is awaiting GMP execution.
- Substantial Completion
 - Of the 24 districts anticipating substantial completion in 2015, seven have declared substantial completion as of this report.

STATEMENTS OF INTEREST (SOIs)

2015 SOI Process

The 2015 Statement of Interest ("SOI") process opened on Friday, January 9, 2015. The deadline to file a SOI for consideration in the Accelerated Repair Program ("ARP") was Friday, February 13, 2015. Due to inclement weather, the MSBA extended the deadline for ARP printed SOI material and related vote information to Friday, February 17, 2015. As of the deadline, the MSBA received 61 SOIs, submitted by 24 districts for consideration into the Program. Invites into the ARP were concluded at the June 3, 2015 Board of Directors meeting; and 24 districts, representing 44 projects were invited into the Program.

The deadline to file a SOI for consideration in the Core Program, which is primarily for projects beyond the scope of Accelerated Repair, including extensive repairs, renovations, additions/renovations and new school construction, was Friday, April 10, 2015. As of the deadline, the MSBA received 97 Core Program SOIs. The review process for these SOIs will last throughout the summer; with invites into Eligibility Period anticipated at the winter 2016 Board of Directors meetings.

CORE PROGRAM

Eligibility Period

There are 16 districts in Eligibility Period. Of the 16, seven districts have secured funding, while the remaining nine districts have yet to confirm their dates for action.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. All 16 districts have completed their online enrollment projection information. Of the 16 districts, three districts have received their enrollment certifications.

Based upon the schedules anticipated by the districts for completion of Eligibility Period requirements, staff anticipates recommending the districts in Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

District	School	Date of Invitation to Eligibility Period	30 days	60 days	90 days		180 days		270 days	Date of Invitation to Feasibility Study (Estimated)
			ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	
Boston	Boston Arts Academy	11/19/14	x	x	x	x	x		x	08/30/15
Attleboro	Attleboro HS	01/14/15	x	x	x	x	x	x		10/26/15
Bristol County Agricultural RSD	Bristol County Agricultural HS	01/14/15	x	x	x	x				10/26/15
Cape Cod RVTSD	Cape Code RTHS	01/14/15	x	x	x	x	x			10/26/15
Clarksburg	Clarksburg ES	01/14/15	x	x	x	x				10/26/15
Fall River	B.M.C. Durfee HS	01/14/15	x		x	x				10/26/15
Lynn	Pickering MS	01/14/15	x	x	x	x	x		x	10/26/15
Middleborough	Middleborough HS	01/14/15	x	x	x	x				10/26/15
Saugus	Saugus HS	01/14/15	x	x	x	x	x	x	x	10/26/15
Taunton	James L. Mulcahey ES	01/14/15	x	x	x	x				10/26/15
Waltham	Waltham HS	01/14/15	x	x	x	x				10/26/15
Westport	Westport MS	01/14/15	x	x	x	x	x	x	x	10/26/15
Worcester	South High Community School	01/14/15	x	x	x	x			x	10/26/15
Easthampton	Maple ES	3/25/15	x	x	x	x			x	01/04/16
Everett	George Keverian School	3/25/15	x	x	x	x			x	01/04/16
Lowell	Lowell HS	3/25/15	x	x	x	x	x			01/04/16

Consultant Selection

OPM Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner’s Project Manager (“OPM”). Since the last report, one district has completed their OPM selection as shown shaded in the table below. Currently, there are three districts in the Capital Pipeline that are in the process of procuring an OPM.

District	School	Anticipated Selection
Bourne	James F. Peebles ES	June 2015
Millis	Clyde F. Brown ES	August 2015
Ipswich	Winthrop ES	September 2015
Holyoke	Lt. Elmer J. McMahon ES	TBD

Designer Selection

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA’s Designer Selection Panel (“DSP”) for projects over \$5 million. Since the last report, three districts have completed their Designer selections as shown shaded in the table below. There are currently three districts in the Capital Pipeline that are in the process of procuring a Designer.

District	School	Anticipated Selection
Stoughton	Stoughton HS	May 2015
Quincy	Reay E. Sterling MS	May 2015
Hanover	Sylvester ES	June 2015
Amherst	Wildwood ES	July 2015
Somerville	Somerville HS	July 2015
Bourne	James F. Peebles ES	August 2015

For additional information on the selected consultant teams, see Appendix A.

Feasibility Study

Once a district has procured an OPM and Designer the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that nine districts will present their preferred schematic designs to the Board at the upcoming August, September and November Board meetings.

District	School	Anticipated PS Board Date
Billerica	Memorial HS	August 6, 2015
Granby	West Street ES	August 6, 2015
Minuteman RVTSD	Minuteman RVTHS	August 6, 2015
Narragansett RSD	Templeton Center ES	August 6, 2015
Newton	Cabot ES	August 6, 2015
Provincetown	Provincetown HS (K-8)	August 6, 2015
Dedham	Early Childhood Center	September 30, 2015
Mount Greylock RSD	Mount Greylock RHS	September 30, 2015
Quincy	Sterling MS	November 18, 2015

Schematic Design

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that seven districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming August, September and November Board meetings.

District	School	Anticipated PS&B Board Date
New Bedford	John Hannigan ES	August 6, 2015
Beverly	Briscoe MS	September 30, 2015
Hopkinton	Center School	September 30, 2015
Provincetown	Provincetown HS (K-8)	September 30, 2015
Carver	Carver ES	November 18, 2015
Narragansett RSD	Templeton Center ES	November 18, 2015
Newton	Cabot ES	November 18, 2015

Commissioning

The MSBA assigns a Commissioning Consultant once a district has secured local funding for the Board approved project. Since the last report, the MSBA has assigned no additional Commissioning Consultants to projects. To date, the MSBA has executed 324 Commissioning Consultant contracts, totaling \$23.1 million. To date, 157 contracts have been completed.

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced	Percent Complete
FY10	31	\$4,231,376	\$4,273,277	100%
FY11	95	\$6,132,890	\$6,020,429	95%
FY12	52	\$4,450,761	\$4,064,417	91%
FY13	55	\$3,364,697	\$2,498,589	74%
FY14	47	\$2,604,062	\$1,228,326	47%
FY15	44	\$2,277,711	\$251,901	11%

Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters into the Design Development phase. Currently, there are 16 projects in the Design Development phase with a total estimated construction cost of approximately \$552.9 million: eight Accelerated Repair projects and eight Core Program projects. The eight Core Program projects in Design Development have a total estimated construction cost of approximately \$537.4 million and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
	<p><u>Middle School Districts</u> Scituate Westborough</p> <p><u>Middle/High School Districts</u> Abington Boston (<i>Dearborn MS</i>)</p>	Pittsfield	Brookline (K-8) Holbrook (PK-12) Worcester (PK-6)

Summary of Bid Data

Based on the most recent data and schedules provided by the districts, the MSBA anticipates 14 projects will bid in 2015.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2015	14	10,920	\$902.2 M	\$713.7 M
2016	2	1,520	\$174.3 M	\$144.2 M
Totals	16	12,440	\$1.08 B	\$0.86 B

Note: These numbers are based on preliminary information received from the District and are subject to further review and calculation.

Anticipated Bids in 2015:

- September – Chelsea (CMR), Boston Dearborn MS (CMR)
- October – N/A
- November – Holbrook (CMR)
- December – Abington (DBB), Scituate (DBB), Westborough (DBB)

For additional information on each of these projects, see Appendix B.

Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction phase. Currently, there are 64 projects in the Construction phase with a total estimated construction cost of \$1.47 billion: 31 Accelerated Repair projects, one Waitlist project, and 32 Core Program projects. This does not include the 44 projects that have reached substantial completion and are currently in the Building Complete phase. The 32 Core Program projects have a total estimated construction cost of \$1.43 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
Athol-Royalston Regional Gloucester Milford Newton Northborough Revere South Hadley Southwick-Tolland-Granville Regional (<i>Woodland ES</i>) Westfield*	<p><u>Middle School Districts</u></p> Chelsea Chicopee Lynn Peabody Southwick-Tolland-Granville Regional (<i>Powder Mill IS</i>) Wachusett Regional Wakefield	Assabet Valley Regional Tech Ayer Shirley Regional Greater Lowell Regional Voc/Tech North Middlesex Regional Plymouth Southern Worcester County Regional Voc/Tech Southwick-Tolland-Granville Regional Winchester	Haverhill (K-8) North Adams (K-7)
	<p><u>Middle/High School Districts</u></p> Georgetown (<i>Middle/High</i>) Greenfield North Reading Lunenburg West Bridgewater Winthrop		

*Note: Westfield, Abner Gibbs Elementary School, stopped construction in December of 2012 due to a preliminary injunction based upon project site status as Article 97 "Protected Land".

For additional information on the construction status for each of these projects, see Appendix C.

ACCELERATED REPAIR PROGRAM

Currently there are a total of 83 districts, representing 168 projects, either active or completed in the Accelerated Repair Program.

Repair Program	Number of Districts	Number of Projects	Total Project Costs	Maximum Facility Grants	Number of Projects Final Audit Approved
2015 Accelerated*	24	44	-	-	0
2014 Accelerated**	33	45	\$107,466,361	\$64,722,015	0
2013 Accelerated	25	45	\$94,650,790	\$54,662,550	0
2012 Accelerated	24	36	\$63,009,653	\$38,267,952	20
Green	93	189	\$366,647,226	\$222,885,258	177

*Totals reflect projects invited into the Accelerated Repair Program as of the June 3, 2015 Board of Directors' Meeting.


**Totals reflect projects approved for Project Funding Agreements as of the June 3, 2015 Board of Directors' Meeting.

2015 Accelerated Repair Program

- Invitations – 24 districts, representing 44 projects
 - Scope includes 22 roofs, 26 windows/doors and nine boilers

2014 Accelerated Repair Program


- Invitations – 36 districts, representing 51 projects
- SOI Removal – two districts, representing four projects
- Current 2014 ARP projects – 35 districts, representing 47 projects
 - Scope includes 20 roofs, 25 windows/doors and 13 boilers
- Approved for Project Funding Agreements – 33 districts, representing 45 projects
- The remaining 2014 district, representing two projects, is anticipated for PFA Approval at the September 30, 2015 Board of Directors meeting
- Three districts, representing five projects required schedule extensions following PFA approval
- 96% of reporting projects bid within estimated budget

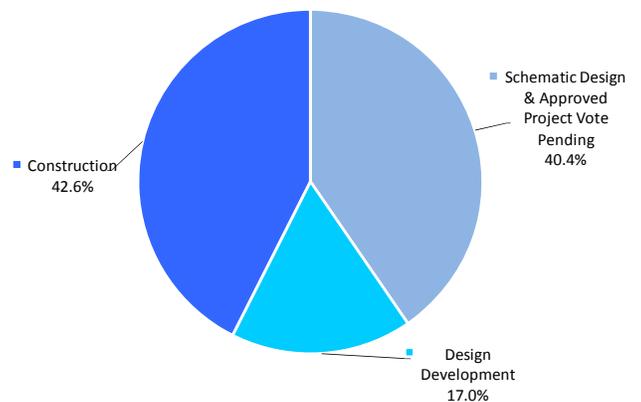

2014 ARP Status Chart

2013 Accelerated Repair Program


- Invitations – 28 districts, representing 50 projects
- SOI Removals – four districts, representing five projects
- Approved for Project Funding Agreements – 26 districts, representing 47 projects
- Active Projects – 25 districts, representing 45 projects
 - Scope includes 30 roofs, 13 windows/doors and seven boilers
- Total Project Budgets – \$94,650,790
- MSBA Total Facilities Grants – \$54,662,550
- Four districts, representing seven projects, required schedule extensions following PFA approval
- 82% of projects bid within estimated budget
- Since the last report, projects that have reached substantial completion remains at 76.6%

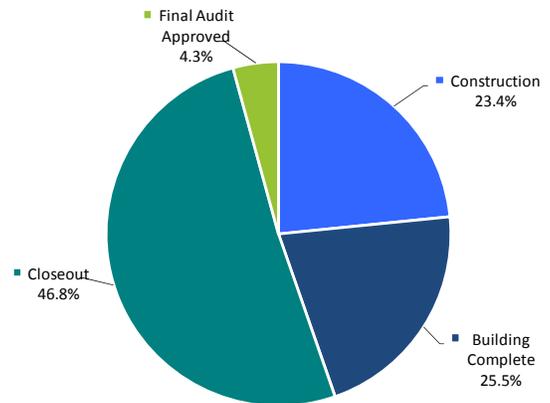

2013 ARP Status Chart

2012 Accelerated Repair Program

- Invitations – 27 districts, representing 39 projects
- SOI Removals – three districts, representing three projects
- Approved Project Funding Agreements – 24 districts, representing 36 projects
 - Scope includes 21 roofs, 11 windows/doors and seven boilers
- Total Project Budgets – \$63,009,653
- MSBA Total Facilities Grants – \$38,267,952
- Five districts, representing nine projects, required schedule extensions following PFA approval
- 86% of projects bid within estimated budget
- Since the last report, projects that have completed Final Audit have increased from 47.2% to 50.0%

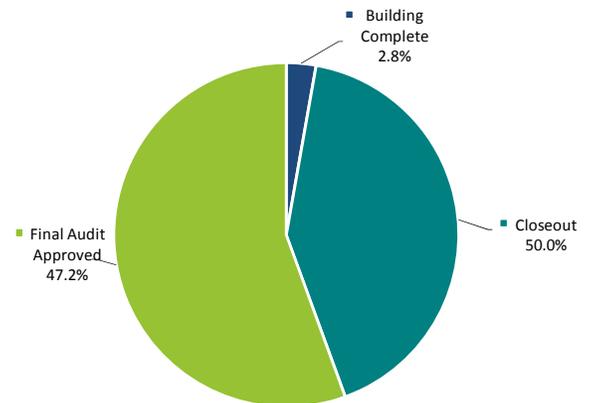

2012 ARP Status Chart

Status of Green Repair Program

The Green Repair Program resulted in PFA authorizations totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants. Of the 189 projects, 177 have been approved for final grant payments. All projects that have not been previously approved for final grant payments are substantially complete, 12 projects require Final Audit.

2014 Accelerated Repair Projects – Construction Estimate vs. 2015-2016 Bid Amount

- 96% of the 25 reported projects came within the estimated budget
- Five additional projects are scheduled to be reported prior to the September 30, 2015 Board of Directors meeting
- Of the remaining 15 projects, 13 are anticipated to be bid in 2015

				Total	\$44,870,252	\$32,159,136	\$12,711,116	-	\$7,802,357
District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
Quincy	Francis W. Parker MS	Windows/Doors	DBB	Jan-15	\$1,077,920	\$987,000	\$90,920	71.16%	\$64,699
Quincy	Lincoln-Hancock Community School	Windows/Doors	DBB	Jan-15	\$2,075,113	\$1,479,000	\$596,113	71.16%	\$424,194
Sudbury	General Nixon ES	Partial Roof/ Partial Windows / Doors	DBB	Feb-15	\$915,204	\$817,466	\$97,738	36.89%	\$36,056
Lynn	William P. Connery ES	Roof	DBB	Feb-15	\$859,532	\$604,000	\$255,532	78.95%	\$201,743
Lynn	E. J. Harrington ES	Roof	DBB	Feb-15	\$1,505,681	\$1,217,700	\$287,981	78.95%	\$227,361
Worcester	Goodard School of Science and Technology	Windows/Doors	DBB	Feb-15	\$4,634,609	\$3,053,000	\$1,581,609	78.95%	\$1,248,680
Worcester	West Tatnuck School	Windows/Doors	DBB	Feb-15	\$1,997,979	\$1,162,019	\$835,960	78.95%	\$659,990
Worcester	Clark Street Community	Windows/Doors	DBB	Feb-15	\$2,095,791	\$1,465,163	\$630,628	78.95%	\$497,881
Worcester	Union Hill School	Windows/Doors	DBB	Feb-15	\$2,096,895	\$1,618,818	\$478,077	78.95%	\$377,442
Dartmouth	George H. Potter ES	Roof	DBB	Feb-15	\$1,548,538	\$1,283,000	\$265,538	51.84%	\$137,655
Medway	John D. McGovern ES	Windows/Doors	DBB	Feb-15	\$894,675	\$561,886	\$332,789	50.16%	\$166,927
Norwood	Cornelius M. Callahan ES	Boiler	DBB	Mar-15	\$356,939	\$224,171	\$132,768	50.58%	\$67,154
Greenfield	Green River	Roof, Windows, Doors	DBB	Mar-15	\$1,739,286	\$1,005,890	\$733,396	77.47%	\$568,162
Springfield	Kensington Avenue	Windows/Doors	DBB	Mar-15	\$779,500	\$832,500	-\$53,000	80.00%	\$0
Wellesley	Wellesley MS	Windows/Doors	DBB	Mar-15	\$3,827,871	\$2,752,500	\$1,075,371	31.00%	\$333,365
Tyngsborough	Tyngsborough HS	Roof, Boiler	DBB	Mar-15	\$3,282,118	\$1,964,300	\$1,317,818	52.89%	\$696,994
Middleton	Fuller Meadow ES	Partial Roof	DBB	Apr-15	\$1,257,849	\$906,800	\$351,049	46.37%	\$162,781
Northampton	Leeds ES	Partial Roof	DBB	Apr-15	\$540,900	\$401,550	\$139,350	56.26%	\$78,398
Northampton	R. K. Finn Ryan Road School	Partial Roof	DBB	Apr-15	\$851,639	\$501,520	\$350,119	56.26%	\$196,977
North Attleborough	Roosevelt Avenue ES	Boiler	DBB	Apr-15	\$303,623	\$265,667	\$37,956	53.53%	\$20,318
Southern Berkshire RSD	Mount Everett RHS	Roof, Boiler	DBB	Apr-15	\$6,376,974	\$4,806,662	\$1,570,312	39.21%	\$615,719
Leominster	Northwest ES	Roof	DBB	May-15	\$2,693,028	\$1,805,000	\$888,028	71.96%	\$639,025
Tri-County Regional	Tri-County RVTHS	Boiler	DBB	Jun-15	\$729,259	\$494,131	\$235,128	51.42%	\$120,903
Auburn	Auburn MS	Roof, Partial Boiler	DBB	Jun-15	\$1,757,394	\$1,371,393	\$386,001	54.16%	\$209,058
Auburn	Bryn Mawr ES	Roof	DBB	Jun-15	\$671,935	\$578,000	\$93,935	54.16%	\$50,875

*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

**The construction estimate and bid amount do not include pre-construction services and alternatives.

PROJECT VARIANCES

Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Staff have reported on budget increases for the ten projects shaded below at previous Board meetings. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

As of this report, staff notes that one project has increased its Total Project Budget (still pending an executed PFA) due to the delay in completing its City Council vote for its appropriation and incurred additional costs.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment / Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Andover	Bancroft ES	New	\$44,659,837	\$16,773,753	\$50,374,837	\$16,575,965	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Burlington	Marshall Simonds MS	Add/Reno	\$32,865,272	\$17,143,365	\$34,221,929	\$15,362,127	The District appropriated at its May 2012 annual town meeting through Articles 18: 19, additional funds for the costs associated with the construction of the new field complex and field lighting replacement.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical High School	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical High School	New	\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Lexington	Estabrook ES	New	\$40,792,248	\$12,250,739	\$43,392,248	\$12,148,491	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
North Reading	North Reading MS/HS	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Revere	Staff Sergeant James J. Hill ES	New	\$45,402,396	\$29,551,048	TBD*	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge HS	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.
Norfolk County Agricultural	Norfolk County Agricultural HS	Add/Reno	\$28,552,385	\$15,369,712	TBD*	TBD*	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Sutton	Sutton MS	Add/Reno	\$59,945,474	\$29,843,511	TBD*	TBD*	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Woburn**	Wyman-Hurld ES	New	\$33,705,396	\$14,387,427	TBD*	TBD*	The District had completed a project review with its Conservation Commission and an Order of conditions was issued on June 12, 2015. A neighborhood group has appealed this Order and it is now under review by DEP. The District has experienced delays in completing its City Council vote for its appropriation and incurred additional costs.

*PFA Bid Amendment has not been developed to calculate a revised Total Facilities Grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but, upon review, may decrease.

**Pending an executed Project Funding Agreement.

Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their Project Funding Agreements pending compliance with the following stipulations:

- The district needed to submit a detailed, revised construction timeline showing how the work will be completed at each school; and
- Any costs that may result from the district’s requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for windows, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

Seven of the 45 2013 Accelerated Repair Projects did not meet their anticipated construction completion dates in 2014. These projects have revised construction schedules and are scheduled to be completed by the beginning of the 2015-2016 school year.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Hamilton-Wenham RSD	Winthrop ES	Windows	9/15/2014	8/13/2015	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2015.
Pathfinder RVTSD	Pathfinder RVTHS	Roof	9/22/2014	8/28/2015	The District fell behind schedule due to local funding issues.
Quincy	Merrymount ES	Windows	9/22/2014	8/28/2015	The District and its consultants have elected to re-bid the project and complete construction in 2015.
Quincy	North Quincy HS	Windows	9/22/2014	8/28/2015	The District and its consultants have elected to re-bid the project and complete construction in 2015.
Quincy	Wollaston ES	Windows	9/22/2014	8/28/2015	The District and its consultants have elected to re-bid the project and complete construction in 2015.
Dighton-Rehoboth RSD	Dighton ES	Roof	8/29/2014	7/31/2015	The District requested that spray-foam insulation be applied during Summer 2015. The spray-foam created an odor that was disruptive to students and staff.
Dighton-Rehoboth RSD	Dighton MS	Roof	8/29/2014	7/31/2015	The District requested that spray-foam insulation be applied during Summer 2015. The spray-foam created an odor that was disruptive to students and staff.

Five of the 45 2014 Accelerated Repair Projects approved for a PFA will not meet their anticipated construction completion dates in 2015. These projects have revised construction schedules and are scheduled to be completed by the beginning of the 2015-2016 school year.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Orleans	Orleans ES	Partial Window/Door	8/25/2015	8/29/2016	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.
Springfield	John F. Kennedy MS	Window/Door	12/22/2015	10/28/2016	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.
Brockton	Ashfield MS	Roof/Boiler	8/31/2015	7/11/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facilities.
Brockton	Brookfield School	Roof	8/25/2015	7/11/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facilities.
Brockton	Gilmore School	Roof/Boiler	8/31/2015	7/11/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facilities.

APPENDIX A
PROJECT STATUS LIST

Date of Report: 7/10/2015

Total Projects: 305

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
200800010405	Abington	Frolio Middle School	Design Development	Core Program	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	-	Horizon Engineering Associates, LLP
201300080050	Amherst	Wildwood Elementary	Feasibility Study	Core Program			Joslin, Lesser + Associates Inc.	-	-	-
200800090003	Andover	Bancroft Elementary School	Closeout	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Skanska USA Building, Inc.	Sebesta Blomberg & Associates, Inc.
201300140405	Ashland	Ashland Middle	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Raymond Design Associates, Inc.	Gibson Roofs, Inc.	Gale Associates, Inc.
201300140010	Ashland	Henry E Warren Elem	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Raymond Design Associates, Inc.	MDM Engineering	Gale Associates, Inc.
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Construction	Core Program	Repair	DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
200906150020	Athol-Royalston	Riverbend School	Construction	Core Program	New Construction	DBB	Symmes Maini & McKee Associates	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Strategic Building Solutions, LLC
201400160505	Attleboro	Attleboro High	Eligibility Period	Core Program			-	-	-	-
200800170305	Auburn	Auburn Middle	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	WSP USA
201400170305	Auburn	Auburn Middle	Approved Project Vote Pending	Accelerated Repair	Roof, Boiler		Skanska USA Building, Inc	Dietz & Company Architects, Inc.	-	Horizon Engineering Associates, LLP Thompson & Lichtner Co., Inc.
201400170010	Auburn	Bryn Mawr	Approved Project Vote Pending	Accelerated Repair	Roof		Skanska USA Building, Inc	Dietz & Company Architects, Inc.	-	Thompson & Lichtner Co., Inc.
200806160505	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Construction	Core Program	Addition / Renovation	CM@R	Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	WSP USA
201300200010	Barnstable	Barnstable United Elementary School	Closeout	Accelerated Repair	Roof	DBB	expERTcon, Inc.	Gale Associates, Inc.	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.
201100200005G	Barnstable	West Barnstable Elem	Closeout	Green Repair	Windows / Doors	DBB	PMA Construction Services - Atlantic Construction and Management, Inc.	-	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201400250020	Bellingham	South Elem	Design Development	Accelerated Repair	Roof		-	-	-	Building Enclosure Associates, LLC
200800260035	Belmont	Roger Wellington Elementary School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Skanska USA Building, Inc.	Strategic Building Solutions, LLC
200806200505	Berlin-Boylston	Tahanto Regional High School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	CTA Construction Co., Inc.	Strategic Building Solutions, LLC
200800300505	Beverly	Beverly High School	Closeout	Core Program	Addition / Renovation	DBB	HEERY	-	CTA Ventures	-
201300300305	Beverly	Briscoe Middle	Schematic Design	Core Program	New Construction		HEERY	Ai3 Architects LLC	-	-
201300310505	Billerica	Billerica Memorial High School	Feasibility Study	Core Program			KV Associates, Inc.	Perkins+Will	-	-
201508050605	Blackstone Valley Reg	Blackstone Valley	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201206220505	Blackstone-Millville	Blackstone Millville RHS	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	-	Gale Associates, Inc.
201306220010	Blackstone-Millville	Millville Elem	Building Complete	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	CBI Consulting Inc.	MDM Engineering	Simpson Gumpertz & Heger Inc.
201500350651	Boston	Dorchester Academy	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201300350546	Boston	Boston Arts Academy	Eligibility Period	Core Program			-	-	-	-
201500350052	Boston	Charles Sumner	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201500350020	Boston	Curley K-8 School	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201500350072	Boston	David A Ellis	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201500350080	Boston	Donald Mckay	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201500350415	Boston	Grover Cleveland	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
201000350074	Boston	Henry Dearborn Middle School	Design Development	Core Program	New Construction	CM@R	Daedalus Projects Inc	Jonathan Levi Architects LLC	Gilbane Building Company	Symmes, Maini & McKee Associates
201000350565	Boston	Quincy Upper School	Feasibility Study	Core Program			Skanska USA Building, Inc	HMFH Architects, Inc.	-	-
201500350380	Boston	Young Achievers	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201400360010	Bourne	James F Peebles Elem	Designer Selection	Core Program			Symmes Maini & McKee Associates, Inc.	-	-	-
201300400305	Braintree	East Middle School	Feasibility Study	Core Program			Hill International Company	Miller Dyer Spears Inc.	-	-
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	-	-	CBI Consulting Inc.
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201206250020	Bridgewater-Raynham	Merrill Elementary School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201409100705	Bristol County Agr	Bristol County Agr High	Eligibility Period	Core Program			-	-	-	-
201400440421	Brockton	Ashfield Middle School	Approved Project Vote Pending	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C. Simpson Gumpertz & Heger Inc.
201400440080	Brockton	Barrett Russell School	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Simpson Gumpertz & Heger Inc.
201400440010	Brockton	Brookfield	Approved Project Vote Pending	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Simpson Gumpertz & Heger Inc.
201400440035	Brockton	Gilmore	Approved Project Vote Pending	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C. Simpson Gumpertz & Heger Inc.
201100460015	Brookline	Edward Devotion	Design Development	Core Program	Addition / Renovation		Anthony Guigli Town Employee	HMFH Architects, Inc.	-	-
201500490090	Cambridge	Fletcher/Maynard Academy	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
201500490040	Cambridge	Kennedy-Longfellow	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201200500012	Canton	Lt Peter M Hansen	Closeout	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201200500305	Canton	Wm H Galvin Middle	Building Complete	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201408150605	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Eligibility Period	Core Program			-	-	-	-
201300520015	Carver	Carver Elementary School	Schematic Design	Core Program			PMA Construction Services	HMFH Architects, Inc.	-	-
200800570050	Chelsea	Clark Avenue School	Construction	Core Program	New Construction		Pinck & Co., Inc.	HMFH Architects, Inc.	-	Cannon Design
201500610010	Chicopee	Belcher	OPM Selection	Accelerated Repair	Roof		-	-	-	-
200900610021	Chicopee	Chicopee Academy	Construction	Core Program	Renovation	DBB	Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Symmes, Maini & McKee Associates
201500610310	Chicopee	Fairview Middle	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201400630010	Clarksburg	Clarksburg Elementary	Eligibility Period	Core Program			-	-	-	-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Building Complete	Core Program	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Turner Construction Company	Strategic Building Solutions, LLC
200800710505	Danvers	Danvers High School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Bacon Construction Co, Inc.	Turner Facilities Management Solutions
201400720030	Dartmouth	George H Potter	Construction	Accelerated Repair	Roof		Pinck & Co., Inc.	Russo Barr Associates, Inc.	-	Gale Associates, Inc.
201200730005	Dedham	Early Childhood Center	Feasibility Study	Core Program			Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	-	-
201500740015	Deerfield	Deerfield Elem	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201306500005	Dighton-Rehoboth	Dighton Elementary	Construction	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	MDM Engineering	Gale Associates, Inc.
201306500305	Dighton-Rehoboth	Dighton Middle School	Construction	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	MDM Engineering	Gale Associates, Inc.
201306500310	Dighton-Rehoboth	Dorothy L Beckwith	Building Complete	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	Greenwood Industries, Inc.	Gale Associates, Inc.

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
200800770010	Douglas	Douglas Elementary	Building Complete	Core Program	New Construction - Model School	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800770100G	Douglas	Douglas Intermediate Elementary School	Building Complete	Green Repair	Roof, Windows / Doors, Boiler	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800790505	Dracut	Dracut Senior High School	Building Complete	Core Program	Addition / Renovation	DBB	Hill International Company	Architects, Inc.	CTA Construction Co., Inc.	RDK Engineers
201000820505	Duxbury	Duxbury High School	Building Complete	Core Program	New Construction - Model School	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	Dimeo Construction Company	WSP USA
200900830505	East Bridgewater	East Bridgewater High School	Building Complete	Core Program	New Construction - Model School	DBB	Hill International Company	Ai3 Architects LLC	Fontaine Brothers, Inc.	Foreman Building Commissioning, LP
201400860010	Easthampton	Maple	Eligibility Period	Core Program			-	-	-	-
201300880020	Easton	Moreau Hall	Building Complete	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	Capeway Roofing Systems, Inc.	Gale Associates, Inc.
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Building Complete	Core Program	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Gilbane Building Company	Turner Facilities Management Solutions
201400930028	Everett	George Keverian School	Eligibility Period	Core Program			-	-	-	-
201500940305	Fairhaven	Hastings Middle	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201400950505	Fall River	B M C Durfee High	Eligibility Period	Core Program			-	-	-	-
200900950315	Fall River	James Madison Morton Middle School	Closeout	Core Program	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	J & J Contractors, Inc.	Sebesta Blomberg & Associates, Inc.
201400960405	Falmouth	Lawrence	Design Development	Accelerated Repair	Windows / Doors		PMA Construction Services	Civitects PC	-	Gale Associates, Inc.
200901010505	Franklin	Franklin High School	Building Complete	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Consulting Engineering Services, LLC
201408180605	Franklin County	Franklin County Tech	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Strategic Building Solutions, LLC	-	-	CBI Consulting Inc. Fitzemeyer & Tocci Associates, Inc. Thompson & Lichtner Co., Inc.
201401030001	Gardner	Elm Street School	Construction	Accelerated Repair	Windows / Doors, Boiler		Hill International Company	ICON architecture, inc.	-	Fitzemeyer & Tocci Associates, Inc.
201201030505	Gardner	Gardner High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Five Star Building Corp.	Fitzemeyer & Tocci Associates, Inc.
201201030405	Gardner	Gardner Middle School	Closeout	Accelerated Repair	Boiler		Lefffield, LLC	Richard D. Kimball Company, Inc.	Royal Steam Heater Co.	Fitzemeyer & Tocci Associates, Inc.
200801050505	Georgetown	Georgetown Middle/High School	Construction	Core Program	Renovation	DBB	Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	L.D. Russo, Inc.	WSP USA
200901050010	Georgetown	Penn Brook Elementary School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
201406740050	Gill-Montague	Sheffield Elementary	Approved Project Vote Pending	Accelerated Repair	Windows / Doors, Boiler		NETCO Construction Project Managers, Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
200901070050	Gloucester	West Parish Elementary School	Construction	Core Program	New Construction	CM@R	Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.	W. T. Rich Company Inc.	Fitzemeyer & Tocci Associates, Inc.
201201110010	Granby	West St	Feasibility Study	Core Program			Strategic Building Solutions, LLC	Jones Whitsett Architects, Inc.	-	-
201108230605	Greater Lawrence RVT	Gr Lawrence Reg Voc Tech	Building Complete	Core Program	Repair	DBB	Vertex Construction Services	Richard D. Kimball Company, Inc.	E. Amanti & Sons, Inc.	WSP USA
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Construction	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High School	Building Complete	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Drumme Rosane Anderson, Inc.	Agostini Construction Co., Inc.	Symmes, Maini & McKee Associates
201501140010	Greenfield	Federal	OPM Selection	Accelerated Repair	Roof, Windows / Doors, Boiler		-	-	-	-
201401140030	Greenfield	Green River	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler		Arcadis U.S., Inc.	Baker/Wohl Architects, Inc.	RAC Builders, Inc.	CBI Consulting Inc.
200901140505	Greenfield	Greenfield High School	Construction	Core Program	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Shawmut Design and Construction	BVH Integrated Services, P.C.
201306750007	Hamilton-Wenham	Bessie Buker Elementary	Closeout	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Multitemp Mechanical Corporation	Strategic Building Solutions, LLC

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
201306750015	Hamilton-Wenham	Winthrop School	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	CBI Consulting Inc. Strategic Building Solutions, LLC
201301220015	Hanover	Sylvester	Feasibility Study	Core Program			P3 Inc.	Mount Vernon Group Architects, Inc.	-	-
201301270505	Hatfield	Smith Academy	Building Complete	Accelerated Repair	Roof, Windows / Doors	DBB	Hill International Company Joslin, Lesser + Associates Inc.	Civitects PC	Silktown Roofing	Building Enclosure Associates, LLC Strategic Building Solutions, LLC
201201280035	Haverhill	Caleb Dustin Hunking	Construction	Core Program	New Construction			JCJ Architecture, PC	-	
201101280100G	Haverhill	Consentino	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	RDK Engineers Russo Barr Associates, Inc.
201101280085G	Haverhill	John G Whittier	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	Russo Barr Associates, Inc.
201101280075G	Haverhill	Tilton	Closeout	Green Repair	Roof	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	Russo Barr Associates, Inc.
201101280080G	Haverhill	Walnut Square	Closeout	Green Repair	Roof, Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	RDK Engineers Russo Barr Associates, Inc.
201001310410	Hingham	Hingham Middle School	Building Complete	Core Program	New Construction - Model School	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Foreman Building Commissioning, LP
200801330505	Holbrook	Holbrook Junior-Senior High School	Design Development	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201401370045	Holyoke	E N White Elem	Schematic Design	Accelerated Repair	Boiler		-	-	-	-
201201370015	Holyoke	Lt Elmer J McMahon Elem	OPM Selection	Core Program			-	-	-	-
201401370025	Holyoke	Morgan Elem	Schematic Design	Accelerated Repair	Boiler		-	-	-	-
201201370605	Holyoke	Wm J Dean Voc Tech High	Building Complete	Science Lab Initiative	Addition / Renovation	DBB	Skanska USA Building, Inc Atlantic Construction and Management, Inc.	Kaestle Boos Associates, Inc.	RAC Builders, Inc.	BVH Integrated Services, P.C. Simpson Gumpertz & Heger Inc.
201301380010	Hopedale	Memorial	Closeout	Accelerated Repair	Roof	DBB	Compass Project Management, Inc.	Civitects PC	MDM Engineering	
201301390005	Hopkinton	Center	Schematic Design	Core Program	New Construction			Drumney Rosane Anderson, Inc.	-	-
200801410410	Hudson	John F. Kennedy Middle School	Closeout	Core Program	New Construction	DBB	PMA Construction Services Atlantic Construction and Management, Inc.	OMR Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP USA
201401410007	Hudson	Mulready Elementary	Construction	Accelerated Repair	Roof			-	-	CBI Consulting Inc.
201401440015	Ipswich	Winthrop	OPM Selection	Core Program			-	-	-	-
201501510505	Leicester	Leicester High	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201501530025	Leominster	Johnny Appleseed	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-	-	-	-
201401530030	Leominster	Northwest	Construction	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201101540005G	Leverett	Leverett Elementary	Closeout	Green Repair	Roof, Windows / Doors	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	-	Russo Barr Associates, Inc.
201101550010E	Lexington	Joseph Estabrook	Closeout	Core Program	New Construction	CM@R	Hill International Company Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	Shawmut Design and Construction	BVH Integrated Services, P.C. Foreman Building Commissioning, LP
200801590505	Longmeadow	Longmeadow High School	Closeout	Core Program	New Construction	CM@R		OMR Architects, Inc.	Gilbane Building Company	
201401600505	Lowell	Lowell High	Eligibility Period	Core Program			-	-	-	-
201501610010	Ludlow	East Street Elementary School	OPM Selection	Accelerated Repair	Roof, Boiler		-	-	-	-
201001620505	Lunenburg	Lunenburg High School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	Cannon Design
201201630405	Lynn	Breed Middle School	Closeout	Accelerated Repair	Windows / Doors	DBB	Diversified Project Management	Kaestle Boos Associates, Inc.	GVW, Inc.	CBI Consulting Inc.
201401630045	Lynn	E J Harrington	Construction	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Capeway Roofing Systems, Inc.	CBI Consulting Inc.
201201630605	Lynn	Lynn Voc Tech Institute	Closeout	Accelerated Repair	Roof	DBB	Diversified Project Management	Kaestle Boos Associates, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
201401630420	Lynn	Pickering Middle	Eligibility Period	Core Program			-	-	-	-
200901630305	Lynn	Thurgood Marshall Middle School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Walsh Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
201401630040	Lynn	Wm P Connery	Construction	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
200801680020	Marblehead	Glover School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	G & R Construction, Inc.	RDK Engineers
201101710505	Marshfield	Marshfield High	Building Complete	Core Program	New Construction - Model School	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Ventures	Sebesta Blomberg & Associates, Inc.
200801740505	Maynard	Maynard High School	Closeout	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	CTA Construction Co., Inc.	WSP USA
201401750007	Medfield	Ralph Wheelock School	Design Development	Accelerated Repair	Boiler		-	-	-	RDK Engineers
201201760505	Medford	Medford High	Building Complete	Science Lab Initiative	Addition / Renovation	DBB	Leftfield, LLC	DiNisco Design Partnership, Limited	G & R Construction, Inc.	Cannon Design
201301760505	Medford	Medford High	Building Complete	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	Dietz & Company Architects, Inc.	NB Kenney Company, Inc	Symmes, Maini & McKee Associates
201401770013	Medway	John D Mc Govern Elem	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CBI Consulting Inc.	-	Russo Barr Associates, Inc.
201401780017	Melrose	Herbert Clark Hoover	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Strategic Building Solutions, LLC	ICON architecture, inc.	-	Simpson Gumpertz & Heger Inc.
201201780505	Melrose	Melrose High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Hill International Company	Ai3 Architects LLC	G & R Construction, Inc.	WSP USA
200801810505	Methuen	Methuen High School	Closeout	Core Program	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
201501820011	Middleborough	Memorial Early Childhood Center	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201401820505	Middleborough	Middleborough High	Eligibility Period	Core Program			-	-	-	-
201401840003	Middleton	Fuller Meadow	Approved Project Vote Pending	Accelerated Repair	Roof		Hill International Company	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201101850090	Milford	Woodland	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
201401870005	Millis	Clyde F Brown	OPM Selection	Core Program			-	-	-	-
200908300605	Minuteman Voc Tech	Minuteman Regional High School	Feasibility Study	Core Program			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-	-
201107129999	Monomoy	Monomoy Regional High School	Building Complete	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Sebesta Blomberg & Associates, Inc.
201307150505	Mount Greylock	Mt Greylock Reg High	Feasibility Study	Core Program			Dore & Whittier Management Partners, Inc.	Design Partnership of Cambridge, Inc.	-	-
200807200020	Narragansett	Templeton Center School	Feasibility Study	Core Program			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
200807250015	Nashoba	Pompositticut Elementary School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	P.J. Stella Construction Corp.	Strategic Building Solutions, LLC
201308520605	Nashoba Valley Tech	Nashoba Valley Tech H S	Building Complete	Accelerated Repair	Roof	DBB	STV Incorporated	CGKV Architects, Inc.	Stanley Roofing Company, Inc.	CBI Consulting Inc.
201306600305	Nauset	Nauset Reg Middle	Closeout	Accelerated Repair	Roof	DBB	Strategic Building Solutions, LLC	ICON architecture, inc.	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.
201301990035	Needham	Hillside Elementary	Feasibility Study	Core Program			Steven H. Popper Town Employee	Dore & Whittier Architects, Inc.	-	-
201502010063	New Bedford	Alfred J Gomes	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201502010123	New Bedford	Casmir Pulaski	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-
201502010078	New Bedford	Hayden/McFadden	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-
201502010115	New Bedford	John Avery Parker	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-
200902010070	New Bedford	John Hannigan	Schematic Design	Core Program	New Construction		Daedalus Projects Inc	Turowski2 Architecture, Inc.	-	-
W201002010505P2	New Bedford	New Bedford High	Construction	Waitlist	Repair		Architectural Consulting Group, LLC	Mount Vernon Group Architects, Inc.	Sparks Company, Inc.	-
201502010045	New Bedford	Sgt Wm H Carney Acad	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
201102040005	Newburyport	Francis T Bresnahan Elem	Building Complete	Core Program	New Construction - Model School	DBB	HEERY	HMFH Architects, Inc.	CTA Construction Co., Inc.	Fitzemeyer & Tocci Associates, Inc.
201002040305	Newburyport	Rupert A. Nock Middle School	Building Complete	Core Program	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Gilbane Building Company	Fitzemeyer & Tocci Associates, Inc.
201102070005	Newton	A E Angier	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	W. T. Rich Company Inc.	Fitzemeyer & Tocci Associates, Inc.
201302070025	Newton	Cabot	Feasibility Study	Core Program			Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	-	-
200802080005	Norfolk	Freeman-Kennedy Elementary School	Closeout	Core Program	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	Fontaine Brothers, Inc.	WSP USA
200909150705	Norfolk County Agriculture	Norfolk County Agr	Closeout	Core Program	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
200802090305	North Adams	Silvio O Conte Middle School	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Jones Whitsett Architects, Inc.	PDS Engineering and Construction, Inc.	Rist-Frost-Shumway Engineering, P.C.
201402120015	North Attleborough	Roosevelt Avenue	Construction	Accelerated Repair	Boiler		Pinck & Co., Inc.	Consulting Engineering Services, LLC	-	Bard, Rao + Athanas Consulting Engineers, LLC
201107350505	North Middlesex	North Middlesex Reg	Construction	Core Program	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	-	Horizon Engineering Associates, LLP
201502170003	North Reading	E Ethel Little School	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201002170505	North Reading	North Reading High School	Construction	Core Program	Addition / Renovation	CM@R	PMA Construction Services Inc.	Dore & Whittier Architects, Inc.	Gilbane Building Company	Cannon Design
201402100025	Northampton	Leeds	Construction	Accelerated Repair	Roof		STV Incorporated	Raymond Design Associates, Inc.	-	Russo Barr Associates, Inc.
201402100029	Northampton	R. K. Finn Ryan Road	Construction	Accelerated Repair	Roof		STV Incorporated	Raymond Design Associates, Inc.	-	Russo Barr Associates, Inc.
201102130003	Northborough	Lincoln Street	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Lamoureux Pagano & Associates, Inc.	-	Fitzemeyer & Tocci Associates, Inc.
200902180505	Norton	Norton High School	Building Complete	Core Program	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	Rist-Frost-Shumway Engineering, P.C.
201402200010	Norwood	Cornelius M Callahan	Construction	Accelerated Repair	Boiler		PMA Construction Services	Consulting Engineering Services, LLC	George T. Wilkinson, Inc.	Symmes, Maini & McKee Associates
201402240005	Orleans	Orleans Elementary	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Gale Associates, Inc.
200802260405	Oxford	Oxford Middle School	Closeout	Core Program	Repair	DBB	Diversified Project Management	CGKV Architects, Inc.	J.J. Cardosi, Inc.	Cannon Design
201308600605	Pathfinder Voc Tech	Pathfinder Voc Tech	Construction	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Baker/Wohl Architects, Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
200802290305	Peabody	Higgins Middle School	Construction	Core Program	New Construction	DBB	Daedalus Projects Inc	DiNisco Design Partnership, Limited	Bacon-Agostini Construction Joint Venture	BVH Integrated Services, P.C.
201102290007G	Peabody	John E Burke	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201402290016	Peabody	John E. McCarthy	Approved Project Vote Pending	Accelerated Repair	Roof, Windows / Doors		Hill International Company	Civitects PC	-	Thompson & Lichtner Co., Inc.
201502290510	Peabody	Peabody Veterans Memorial High	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201102290027G	Peabody	William A Welch Sr	Closeout	Green Repair	Roof	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201302310010	Pembroke	Hobomock Elementary	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Greenwood Industries, Inc.	CBI Consulting Inc.
201302310015	Pembroke	North Pembroke Elem	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310305	Pembroke	Pembroke Community Middle School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310505	Pembroke	Pembroke High School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Greenwood Industries, Inc.	CBI Consulting Inc.
201307450405	Pentucket	Pentucket Reg Middle	Closeout	Accelerated Repair	Roof, Boiler	DBB	Arcadis U.S., Inc.	CGKV Architects, Inc.	Ambient Temperature Corporation	CBI Consulting Inc. Strategic Building Solutions, LLC
201002360510	Pittsfield	Taconic High School	Design Development	Core Program	New Construction		Skanska USA Building, Inc	Drumme Rosane Anderson, Inc.	-	-
201202390515	Plymouth	Plymouth South High	Construction	Core Program	New Construction		Ted Gentry Associates, Inc	Ai3 Architects LLC	-	Rist-Frost-Shumway Engineering, P.C.

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
201302420505	Provincetown	Provincetown High	Feasibility Study	Core Program			Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	-	-
201502430020	Quincy	Beechwood Knoll Elem	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-	-	-	-
200802430315	Quincy	Central Middle School	Closeout	Core Program	New Construction - Model School	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	H.V. Collins Co., Inc.	Sebesta Blomberg & Associates, Inc.
201402430075	Quincy	Francis W Parker	Construction	Accelerated Repair	Windows / Doors		PMA Construction Services	-	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201402430035	Quincy	Lincoln-Hancock Comm Sch	Construction	Accelerated Repair	Windows / Doors		PMA Construction Services	-	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201302430060	Quincy	Merrymount	Construction	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	Alpha Contracting Associates, Inc.	Simpson Gumpertz & Heger Inc.
201502430060	Quincy	Merrymount	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201302430510	Quincy	North Quincy High	Construction	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	GVW, Inc.	Simpson Gumpertz & Heger Inc.
201302430320	Quincy	Reay E Sterling Middle	Feasibility Study	Core Program			Joslin, Lesser + Associates Inc.	Ai3 Architects LLC	-	-
201302430110	Quincy	Wollaston School	Construction	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	Northeast Energy Control Systems	Simpson Gumpertz & Heger Inc.
201402440018	Randolph	J F Kennedy Elem	Design Development	Accelerated Repair	Windows / Doors		-	-	-	Gale Associates, Inc.
201302440410	Randolph	Randolph Community Middle	Closeout	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	AAlanco Service Corporation	Consulting Engineering Services, LLC
201302440505	Randolph	Randolph High	Closeout	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	John F. Shea Company, Inc.	Gale Associates, Inc.
201402440505	Randolph	Randolph High	Design Development	Accelerated Repair	Windows / Doors		-	-	-	Gale Associates, Inc.
201502480056	Revere	Garfield Elementary School	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201002480035	Revere	Staff Sergeant James J. Hill School	Construction	Core Program	New Construction	DBB	Hill International Company	Drumme Rosane Anderson, Inc.	CTA Construction Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
200802510305	Rockland	John W. Rogers Middle School	Closeout	Core Program	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
200902580305G	Salem	Collins Middle School	Building Complete	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002580050G	Salem	Saltonstall School	Closeout	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002620305	Saugus	Belmonte Middle School	Closeout	Core Program	Repair	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201402620505	Saugus	Saugus High	Eligibility Period	Core Program			-	-	-	-
201202640305	Scituate	Gates Intermediate School	Design Development	Core Program	New Construction		Daedalus Projects Inc	Dore & Whittier Architects, Inc.	-	WSP USA
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Accelerated Repair	Boiler	DBB	Diversified Project Management	Shekar & Associates, Inc.	NB Kenney Company, Inc	Fitzemeyer & Tocci Associates, Inc.
200802710305	Shrewsbury	Sherwood Middle School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	Gilbane Building Company	RDK Engineers
201308290605	So Middlesex Voc Tech Reg	Joseph P Keefe Tech HS	Closeout	Accelerated Repair	Roof	DBB	PMA Construction Services	Raymond Design Associates, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
20081119999	Somerset-Berkley	Somerset-Berkley High	Building Complete	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Horizon Engineering Associates, LLP
200902740111E	Somerville	East Somerville Community School at Cummings	Closeout	Core Program	Renovation	CM@R	PMA Construction Services	Maguire Group Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201302740505	Somerville	Somerville High	Designer Selection	Core Program			PMA Construction Services	-	-	-
200902780015	South Hadley	Plains School	Construction	Core Program	New Construction	DBB	Arcadis U.S., Inc.	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Strategic Building Solutions, LLC

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
201408730605	South Shore Reg Voc Tech	So Shore Voc Tech High	Approved Project Vote Pending	Accelerated Repair	Boiler		exPERTcon, Inc.	Richard D. Kimball Company, Inc.	-	Consulting Engineering Services, LLC
201407650505	Southern Berkshire	Mt Everett Regional	Construction	Accelerated Repair	Roof, Boiler		NETCO Construction Project Managers, Inc.	Dietz & Company Architects, Inc.	Titan Roofing, Inc.	Strategic Building Solutions, LLC
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Construction	Core Program	Addition / Renovation	CM@R	HEERY	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
201107660305	Southwick-Tolland	Powder Mill	Construction	Core Program	Repair	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201107660505	Southwick-Tolland	Southwick-Tolland Regional High	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	Fontaine Brothers, Inc.	BVH Integrated Services, P.C.
200807660010	Southwick-Tolland	Woodland Elementary School	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201502810350	Springfield	STEM Middle Academy	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201302810310	Springfield	Chestnut Accelerated Middle School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
201502810035	Springfield	Daniel B Brunton	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201102810125E	Springfield	Dryden Memorial	Closeout	Core Program	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Drumme Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
201102810030E	Springfield	Elias Brookings	Building Complete	Core Program	New Construction	CM@R	Arcadis U.S., Inc.	Drumme Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
W20014137	Springfield	Forest Park Middle School	Closeout	Waitlist	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Perkins Eastman	Consigli Construction Company, Inc.	Foreman Building Commissioning, LP
201302810530	Springfield	High School/Science-Tech	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Kronenberger & Sons Restoration, Inc.	Building Enclosure Associates, LLC
201402810328	Springfield	John F Kennedy Middle	Design Development	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201402810110	Springfield	Kensington Avenue	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201302810060	Springfield	Margaret C Ells	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
201502810155	Springfield	Mary M Walsh	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201302810355	Springfield	South End Middle School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Titan Roofing, Inc.	Building Enclosure Associates, LLC
201202810500	Springfield	Springfield Central High	Building Complete	Science Lab Initiative	Addition / Renovation	CM@R	Leftfield, LLC	DiNisco Design Partnership, Limited	Morganti/Aquadro & Cerruti	Horizon Engineering Associates, LLP
201302810550	Springfield	Springfield Public Day High School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201502810550	Springfield	Springfield Public Day High School	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
200902840405	Stoneham	Stoneham Middle School	Building Complete	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	RDK Engineers
201302850010	Stoughton	Helen Hansen Elementary	Construction	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	Lockheed Window Corporations	Building Enclosure Associates, LLC
201402850025	Stoughton	Joseph H Gibbons	Construction	Accelerated Repair	Roof, Windows / Doors		Atlantic Construction and Management, Inc.	CGKV Architects, Inc.	-	Building Enclosure Associates, LLC
201302850014	Stoughton	Joseph R Dawe Jr Elem	Construction	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	Lockheed Window Corporations	Building Enclosure Associates, LLC
201302850505	Stoughton	Stoughton High	Feasibility Study	Core Program			Compass Project Management, Inc.	Drumme Rosane Anderson, Inc.	-	-
201302850020	Stoughton	West Elementary	Closeout	Accelerated Repair	Roof	DBB	Hill International Company	Russo Barr Associates, Inc.	Titan Roofing, Inc.	Building Enclosure Associates, LLC
201502850020	Stoughton	West Elementary	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
200802870005	Sturbridge	Burgess Elementary School	Closeout	Core Program	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201402880025	Sudbury	General John Nixon Elem	Construction	Accelerated Repair	Roof, Windows / Doors		Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	Silktown Roofing	Building Enclosure Associates, LLC
200802900305	Sutton	Sutton Middle School	Building Complete	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	Brait Builders Corp.	RDK Engineers
201102910010	Swampscott	Hadley	Closeout	Core Program	New Construction	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	-	-
201502930007	Taunton	Edmund Hatch Bennett	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-	-	-	-

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
201502930042	Taunton	Joseph H Martin	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-	-	-	-
201402930015	Taunton	Mulcahey Elementary School	Eligibility Period	Core Program			-	-	-	-
200802950505	Tewksbury	Tewksbury Memorial High School	Closeout	Core Program	New Construction - Model School	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Ventures	Sebesta Blomberg & Associates, Inc.
201408780605	Tri County	Tri County Reg Voc Tech	Design Development	Accelerated Repair	Boiler		Strategic Building Solutions, LLC	Shekar & Associates, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
201403010505	Tyngsborough	Tyngsborough High School	Construction	Accelerated Repair	Roof, Boiler		Municipal Building Consultants, Inc.	CSS Architects Incorporated	-	Strategic Building Solutions, LLC
200803040505	Uxbridge	Uxbridge High	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Shawmut Design and Construction	Turner Facilities Management Solutions
200907750305	Wachusett	Mountview Middle School	Construction	Core Program	New Construction	DBB	Gary Kaczmarek Town Employee	Lamoureux Pagano & Associates, Inc.	CTA Construction Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
201003050310	Wakefield	Galvin Middle School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Bond Brothers, Inc.	B2Q Associates, Inc.
201303070015	Walpole	Fisher	Closeout	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Rockwell Roofing, Inc.	Gale Associates, Inc.
201403080505	Waltham	Waltham High School	Eligibility Period	Core Program			-	-	-	-
201503100003	Wareham	John W. Decas Elementary School	OPM Selection	Accelerated Repair	Roof, Boiler		-	-	-	-
201303100505	Wareham	Wareham Senior High	Closeout	Accelerated Repair	Roof	DBB	Hill International Company	Tighe & Bond, Inc.	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.
201503140305	Watertown	Watertown Middle	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201403150005	Wayland	Claypit Hill School	Design Development	Accelerated Repair	Windows / Doors		Pinck & Co., Inc.	CGKV Architects, Inc.	-	Russo Barr Associates, Inc.
200903160015	Webster	Park Avenue Elementary School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Dore & Whittier Architects, Inc.	CTA Construction Co., Inc.	Cannon Design
201403170305	Wellesley	Wellesley Middle	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	Paul J. Rogan Co., Inc.	Gale Associates, Inc.
200803170505	Wellesley	Wellesley Senior School	Closeout	Core Program	New Construction	CM@R	-	Symmes Maini & McKee Associates, Inc.	-	Rist-Frost-Shurway Engineering, P.C.
201303180005	Wellfleet	Wellfleet Elementary	Closeout	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	CSS Architects Incorporated	DDC Construction Inc.	Russo Barr Associates, Inc.
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Green Repair	Windows / Doors	DBB	URS Corporation	Reinhardt Associates, Inc.	-	Cannon Design
201503230005	West Bridgewater	Spring Street School	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Construction	Core Program	New Construction	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	CTA Construction Co., Inc.	Cannon Design
200903320505	West Springfield	West Springfield High School	Building Complete	Core Program	New Construction - Model School	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Fontaine Brothers, Inc.	Turner Facilities Management Solutions
200903210305	Westborough	Gibbons Middle School	Design Development	Core Program	Repair		HEERY	Habeeb & Associates Architects, Inc.	-	BVH Integrated Services, P.C.
200903250020	Westfield	Abner Gibbs Elementary School	Construction	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201303260025	Westford	Col John Robinson	Construction	Accelerated Repair	Windows / Doors	DBB	Strategic Building Solutions, LLC	Gale Associates, Inc.	GTC Construction Management	CBI Consulting Inc.
201303260007	Westford	Day Elementary	Construction	Accelerated Repair	Windows / Doors	DBB	Strategic Building Solutions, LLC	Gale Associates, Inc.	J.J. Cardosi, Inc.	CBI Consulting Inc.
201303270005	Westhampton	Westhampton Elem School	Closeout	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Independent Roofing Co. Inc.	Building Enclosure Associates, LLC
200903300012	Weston	Field Elementary School	Building Complete	Core Program	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Colantonio, Inc.	Foreman Building Commissioning, LP
201403310305	Westport	Westport Middle	Eligibility Period	Core Program			-	-	-	-
200803400005	Williamsburg	Anne T. Dunphy School	Building Complete	Core Program	Addition / Renovation	DBB	Arcadis U.S., Inc.	Drumme Rosane Anderson, Inc.	Enfield Builders, Inc.	B2Q Associates, Inc.
201203420060	Wilmington	North Intermediate	Closeout	Accelerated Repair	Windows / Doors	DBB	Diversified Project Management	-	-	CBI Consulting Inc.
200903420505	Wilmington	Wilmington High School	Building Complete	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
201003440505	Winchester	Winchester High School	Construction	Core Program	Addition / Renovation	CM@R	Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CMGC	Commissioning Consultant
200803460505	Winthrop	Winthrop High School	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	HMFH Architects, Inc.	Gilbane Building Company	WSP USA
201203470060	Woburn	Wyman	Approved Project Vote Pending	Core Program	New Construction		Municipal Building Consultants, Inc.	DiNisco Design Partnership, Limited	-	-
201203480052	Worcester	Chandler Magnet	Closeout	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201403480055	Worcester	Clark St Community	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480060	Worcester	Columbus Park	Building Complete	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers Russo Barr Associates, Inc.
201203488099	Worcester	Dr. James Caradonio Center	Closeout	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers Russo Barr Associates, Inc.
201503480090	Worcester	Flagg Street	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201503480177	Worcester	Francis J McGrath Elem	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201403480100	Worcester	Goddard Sch/Science Tech	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	Lambrian Construction Corp.	Russo Barr Associates, Inc.
201503480115	Worcester	Grafton Street	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-
201203480140	Worcester	Jacob Hiatt Magnet	Closeout	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers
201503480140	Worcester	Jacob Hiatt Magnet	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201203480145	Worcester	Lake View	Closeout	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480175	Worcester	May Street	Closeout	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480200	Worcester	Nelson Place	Design Development	Core Program	New Construction	CM@R	Tishman Construction Corporation of MA	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
201403480520	Worcester	South High Community	Eligibility Period	Core Program			-	-	-	-
201303480230	Worcester	Tatnuck	Building Complete	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
201403480240	Worcester	Union Hill School	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201403480260	Worcester	West Tatnuck	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480225	Worcester	Worcester Arts Magnet Sch	Building Complete	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
201303480420	Worcester	Worcester East Middle	Building Complete	Accelerated Repair	Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers
201503500003	Wrentham	Delaney	OPM Selection	Accelerated Repair	Roof		-	-	-	-

APPENDIX B
2015 & 2016 ESTIMATED BID DATES

2015 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.


Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Constructio Budget	Notes	Oct '14	Nov '14	Dec '14	Jan '15	Feb '15	Mar '15	Apr '15	May '15	Jun '15	Jul '15	Aug '15	Sep '15	Oct '15	Nov '15	Dec '15	Jan '16					
							Gantt Chart Data																				
Gloucester	355	\$ 39.6	Mon 10/20/14	Thu 1/8/15	\$ 30.0	GMP issued: January	10/20  1/8																				
Milford	985	\$ 60.9	Mon 11/3/14	Tue 1/20/15	\$ 48.4	GMP issued: January	11/3  1/20																				
Winthrop	970	\$ 80.2	Wed 2/4/15	Thu 4/16/15	\$ 61.9	GMP issued: April	2/4  4/16																				
Northborough	270	\$ 25.5	Mon 2/9/15	Fri 5/1/15	\$ 18.2	NTP targeted: April	2/9  5/1																				
Georgetown	720	\$ 7.8	Mon 2/9/15	Thu 3/12/15	\$ 5.9	NTP issued: March	2/9  3/12																				
North Middlesex RSD	870	\$ 89.0	Wed 4/8/15	Thu 5/21/15	\$ 68.8	NTP targeted: June	4/8  5/21																				
Haverhill	1005	\$ 61.5	Tue 4/14/15	Mon 5/18/15	\$ 50.0	GMP targeted: May	4/14  5/18																				
Plymouth	1005	\$ 107.8	Thu 5/21/15	Wed 7/1/15	\$ 83.8	NTP targeted: July	5/21  7/1																				
Chelsea	670	\$ 57.3	Wed 7/22/15	Tue 10/6/15	\$ 46.0	GMP targeted: September	7/22  10/6																				
Boston	600	\$ 73.5	Mon 8/3/15	Thu 9/17/15	\$ 60.2	GMP targeted: September	8/3  9/17																				
Holbrook	1095	\$ 103.0	Tue 9/29/15	Mon 11/23/15	\$ 79.8	GMP targeted: November	9/29  11/23																				
Abington	1115	\$ 96.4	Wed 10/14/15	Fri 12/11/15	\$ 77.2	NTP targeted: December	10/14  12/11																				
Scituate	710	\$ 72.9	Wed 10/21/15	Fri 12/18/15	\$ 61.9	NTP targeted: December	10/21  12/18																				
Westborough	550	\$ 26.8	Mon 11/2/15	Thu 12/17/15	\$ 21.6	NTP targeted: December	11/2  12/17																				
Total	10920	\$ 902.2			\$ 713.7																						

Note: Budget values are in millions.

The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

07/10/2015




2016 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Constructio Budget	Notes	Nov '15	Dec '15	Jan '16	Feb '16	Mar '16	Apr '16	May '16	Jun '16	Jul '16	Aug '16	Sep '16	Oct '16	Nov '16	Dec '16		
							Worcester	600	\$ 58.2	Wed 12/16/15	Tue 4/5/16	\$ 46.5	GMP targeted: April 2016		12/16	Worcester - Nelson Place School			4/5			
Pittsfield	920	\$ 116.1	Thu 6/16/16	Fri 7/29/16	\$ 97.7	GMP targeted: August 2016								Pittsfield - Taconic High School			6/16	7/22	7/29			
Total	1520	\$ 174.3			\$ 144.2																	

Note: Budget values are in millions.
The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.



APPENDIX C
CONSTRUCTION STATUS REPORT

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of July 10, 2015**

Core Program and Waitlist Totals			\$2,781,781,636														*Includes Alternates	\$1,714,468,572
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
Core Program Totals			\$2,779,805,553															\$1,708,982,133
Assabet Valley Assabet Valley Voc H S	Vocational / Technical	CTA Construction Co., Inc.	\$46,764,740	1,000	Bid	367,565	\$127	\$41,523,764	\$113	Design/Bid/Build	01-Apr-13	23-Aug-15	0	80%	\$2,808,400	6.005%	This project is a 10-phase major renovation. Scope includes multiple building systems, site and ADA upgrades. The project is currently in Phase 10 which is scheduled to be completed August 23, 2015, which is the project's Substantial Completion Date. Punch list work for Phases 1-5 is complete and punch list for Phase 6 is ongoing. Punch lists for Phases 7 through 9 are about to begin.	\$28,790,301
Athol-Royalston Riverbend	Elementary School	Fontaine Brothers, Inc.	\$35,191,363	545	PFA	95,726	\$368	\$21,101,359	\$220	Design/Bid/Build	08-Dec-14	14-Jun-16	0	11%	\$62,826	0.179%	Temporary fencing installed. Grading, blasting, and foundations continue.	\$26,011,620
Berlin-Boylston Tahanto Reg High	Junior High School	CTA Construction Co., Inc.	\$32,162,000	560	Bid	126,100	\$255	\$24,629,999	\$195	Design/Bid/Build	10-May-11	01-Jul-13	0	99%	\$1,026,723	3.282%	The new school building is in service. The District is working to resolve issues associated with final change orders and rain screen repairs.	\$18,733,021
Chicopee Chicopee Academy	Middle School	Fontaine Brothers, Inc.	\$30,776,990	825	Bid	176,425	\$174	\$21,508,080	\$122	Design/Bid/Build	01-Jul-14	11-Aug-15	0	92%	\$1,536,273	4.992%	Drywall, ceiling tiles, painting and MEP installations continue throughout the building. Window installation is complete and tested. Granite curbing and sidewalk installations have begun.	\$28,813,458
Douglas Douglas Elementary	Elementary School	CTA Construction Co., Inc.	\$24,275,111	552	Bid	83,100	\$292	\$19,026,763	\$229	Design/Bid/Build	02-Mar-12	26-Aug-13	0	100%	\$627,104	2.629%	The new school building is in service. Site work is complete and final acceptance of landscaping work is scheduled for completion during the Summer of 2015.	\$16,456,925
Dracut Dracut Senior High	High School	CTA Construction Co., Inc.	\$45,900,000	1,160	Bid	226,844	\$202	\$38,377,028	\$169	Design/Bid/Build	27-Aug-12	29-Aug-14	0	98%	\$1,959,525	4.269%	All spaces have been turned over to the District except the main courtyard. Punch list work is ongoing throughout the building for all phases.	\$34,137,202
East Bridgewater East Bridgewater High	High School	Fontaine Brothers, Inc.	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	25-Jun-13	0	99%	\$2,398,294	3.928%	HVAC long-standing issues are being addressed and are scheduled to be completed over the summer months.	\$40,164,584
Franklin Franklin High	High School	Bacon-Agostini Construction Joint Venture	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$239	Design/Bid/Build	16-Oct-12	25-Jul-14	0	98%	\$1,075,558	1.239%	The new building and parking areas are complete. Landscaping is ongoing for the new athletic fields. Installation of the sport light poles is to take place in July. Construction of the synthetic field is ongoing with completion expected in August. Expect all work to be completed by August 15.	\$54,558,408
Georgetown Georgetown Middle/High	Junior High School	L.D. Russo, Inc.	\$5,861,090	720	PFA	128,670	\$46	\$3,543,961	\$28	Design/Bid/Build	15-Apr-15	21-Dec-15	0	5%	\$60,646	1.035%	Demolition of the Gym continues. Roofing is underway.	\$3,686,039
Georgetown Penn Brook	Elementary School	Brait Builders Corp.	\$32,875,975	770	Bid	98,000	\$335	\$26,976,145	\$275	Design/Bid/Build	26-Sep-13	20-May-15	0	95%	\$3,595,693	10.937%	Site work contractor has remobilized. Temporary power has been removed from the site and exterior lighting is progressing. Final painting, flooring, and acoustical wall panels are continuing. Start-up and commissioning of all mechanical equipment is ongoing.	\$18,864,538
Greater Lawrence RVT Gr Lawrence Reg Voc Tech	Vocational / Technical	E. Amanti & Sons, Inc.	\$4,361,641	1,400	Bid	360,000	\$12	\$3,551,593	\$10	Design/Bid/Build	04-Jun-14	12-Dec-14	0	99%	\$260,493	5.972%	Project includes the replacement of cooling towers, chiller plant, HVAC pumps, HVAC controls, domestic hot water heaters, roof top mechanical units, and ventilation throughout the shop areas. The only work remaining is the chiller and cooling tower start up, commissioning, training and closeout. The team is currently investigating a noise level issue with the above ceiling unit heaters. This will be resolved as part of the final commissioning process.	\$2,627,875
Greater New Bedford Gr New Bedford Voc Tech	Vocational / Technical	Agostini Construction Co., Inc.	\$12,181,500	2,060	Bid	487,530	\$25	\$10,757,696	\$22	Design/Bid/Build	13-Sep-13	19-Dec-14	0	100%	\$1,141,471	9.371%	The building is complete and in service. Replacement of the cooling tower has been completed and is operational. Cooling tower pump replacement and miscellaneous punch list work to be completed during the summer months.	\$11,573,133
Hingham Hingham Middle School	Middle School	Brait Builders Corp.	\$48,436,000	1,020	Bid	176,385	\$275	\$41,227,552	\$234	Design/Bid/Build	07-Jun-12	01-May-14	0	99%	\$714,526	1.492%	Demolition of the existing building is complete. Landscaping and field installation has resumed. Commissioning of the building is ongoing.	\$23,653,420
Marblehead Glover	Elementary School	G & R Construction, Inc.	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/Build	25-Jun-12	20-Dec-13	0	100%	\$791,625	3.794%	The new school building is complete and in service. Site work is complete and final acceptance inspection of the landscaping work is planned for the Fall of 2015.	\$9,316,827
Marshfield Marshfield High	High School	Brait Builders Ventures	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/Build	16-Aug-12	01-Jun-14	0	98%	\$2,144,062	2.694%	Remaining work consists of punch list items, system checkouts, and technology interfacing. Demolition of the existing high school building continues which will be followed by final site restoration.	\$46,550,599
Monomoy Monomoy Regional High School	High School	Fontaine Brothers, Inc.	\$49,374,000	700	Bid	168,000	\$294	\$41,433,695	\$247	Design/Bid/Build	11-Feb-13	02-Sep-14	0	99%	\$921,683	1.920%	Work continues with the irrigation and landscaping around the building. Work has commenced on the concession stand foundations. Punch list work and roof top unit maintenance is ongoing.	\$27,654,507
Newburyport Francis T Bresnahan Elem	Elementary School	CTA Construction Co., Inc.	\$28,190,000	660	PFA	112,517	\$251	\$20,841,757	\$185	Design/Bid/Build	14-Mar-13	19-Aug-14	0	99%	\$1,086,168	3.963%	Punch list work is remaining as well as final commissioning of the major mechanical equipment.	\$15,676,427
North Adams Silvio O Conte Middle	Middle School	PDS Engineering and Construction, Inc.	\$21,877,496	310	Bid	78,119	\$280	\$17,831,491	\$228	Design/Bid/Build	28-Apr-14	22-Jul-15	86 behind	82%	\$879,038	4.018%	Progress on finishes has focused on the 3rd floor with ceiling grid installations, light fixtures, HVAC units, and painting underway. Most new window installations have been completed throughout the building. Plastering continues on the lower floors and quarry tile installation began in the kitchen areas. Stripping of the old roof began on the low roof, and installation of the base and membrane is proceeding. Concrete foundation placements began for the playground equipment. The structural engineer issued a report for a section of failed exterior veneer at the Gym south wall. Some additional work will be requested at this wall for structural integrity.	\$20,508,670
North Middlesex North Middlesex Reg	High School	CTA Construction Co., Inc.	\$68,829,726	870	PFA	180,530	\$381	\$44,223,062	\$245	Design/Bid/Build	25-May-15	14-Jul-17	0	0%	\$0	0.000%	Contractor has mobilized.	\$39,373,276
Northborough Lincoln Street	Elementary School	Brait Builders Ventures	\$18,285,000	270	PFA	52,920	\$346	\$10,744,900	\$203	Design/Bid/Build	27-Apr-15	01-Sep-16	0	5%	\$0	0.000%	Construction fencing and the office trailers have been setup. Demolition of the old septic system and connection of the building to the sewer system is complete. The retaining wall along the north property line has been completed. Foundation work at the Gym addition and at the west canopy structure is complete.	\$9,925,570
Peabody J Henry Higgins Middle	Middle School	Bacon-Agostini Construction Joint Venture	\$76,735,661	1,340	Bid	227,314	\$338	\$47,562,204	\$209	Design/Bid/Build	10-Mar-14	01-Jul-16	0	30%	(\$709,977)	-0.946%	Structural steel is nearly complete. Concrete slabs are 70% complete. Light gauge metal framing and exterior sheathing are complete on the 2nd and 3rd floor of Academic West with the 1st floor to follow. Brick veneer is 75% complete on Academic West. Masonry is 3 weeks ahead of schedule. Roofing is about 70% complete. Window and glazed block installations have started. Exterior porcelain panel fabrication is in progress. Mechanical, electrical, and plumbing installation continues on the 3rd floor. Overhead HVAC ducts, piping and storm drains are complete on the 3rd floor and in progress on the 2nd and 1st floors. In-wall electrical has started. Drywall installation has not begun yet.	\$38,652,137
Plymouth Plymouth South High	High School	Bacon-Agostini Construction Joint Venture	\$88,163,542	1,005	PFA	248,081	\$355	\$60,612,309	\$244	Design/Bid/Build	06-Jul-15	05-May-17	0	0%	\$0	0.000%	GC bids were received on July 1, 2015. Bacon-Agostini is the current low-bidder.	\$46,241,232
Revere Staff Sergeant James J. Hill School	Elementary School	CTA Construction Co., Inc.	\$33,897,336	690	Bid	103,650	\$327	\$24,309,968	\$235	Design/Bid/Build	25-Mar-14	16-Jun-15	49 behind	80%	\$1,050,055	3.098%	Substantial Completion for the project is currently forecast for August 3, 2015. Teachers are scheduled to be in the building on August 10, 2015 with the students to follow on August 19, 2015. The Building is weather tight with permanent power. Building C (classrooms) requires the completion of punch list work including cable rework. MEP and architectural finishes as well as cable rework are required in both Building A (classrooms) and Building B (common areas). Site work is ongoing and includes soil removal, completion of detention ponds, and paving.	\$28,099,048
Somerset-Berkley Somerset-Berkley High	High School	Bacon-Agostini Construction Joint Venture	\$69,407,000	1,000	Bid	222,826	\$311	\$52,553,676	\$236	Design/Bid/Build	16-Jul-12	20-Jun-14	0	98%	\$827,990	1.258%	Exterior work continues with development of the softball fields, including fencing and seeding. Abatement of the existing high school continues in preparation for demolition.	\$46,722,150
South Hadley Plains Elementary	Elementary School	Fontaine Brothers, Inc.	\$21,391,144	270	Bid	63,377	\$338	\$17,380,907	\$274	Design/Bid/Build	08-May-14	04-Sep-15	0	76%	\$782,766	3.659%	Roofing, doors and windows are nearly complete. Ceiling and fixture installations as well as painting and interior finishes are ongoing. Site work continues; The building is scheduled to be open on September 8, 2015.	\$13,676,432
Southwick-Tolland Powder Mill	Middle School	PDS Engineering and Construction, Inc.	\$13,556,194	545	Bid	95,775	\$142	\$11,289,029	\$118	Design/Bid/Build	07-Jun-13	14-Aug-15	0	95%	\$762,222	5.623%	The project is currently in Phase 4 of a 5-phase project. Finishes in the 2nd floor of the West Wing (Phase 4) are complete. Finishes for the 1st floor of the West Wing (Phase 4) remain on schedule with the contractor completing the installation of VCT flooring, ceiling grids, and casework. Contractor's laydown area has been demobilized.	\$8,437,002
Southwick-Tolland Southwick-Tolland Regional High	High School	Fontaine Brothers, Inc.	\$25,307,990	790	Bid	165,995	\$152	\$19,838,420	\$120	Design/Bid/Build	05-Aug-13	18-Sep-15	0	86%	\$2,025,231	8.171%	This is a 5-phase project. Phase 4A (Alternate Gym) is progressing with masonry, roofing, and MEP rough work nearing completion. The Band Room and Locker Rooms (Phases 5B & 5C) have been abated and demolition is proceeding. The new sewer pipe installation to the connection at the Woodland Elementary School entrance is complete.	\$19,572,669
Southwick-Tolland Woodland Elementary	Elementary School	PDS Engineering and Construction, Inc.	\$7,172,052	400	Bid	67,800	\$106	\$6,077,790	\$90	Design/Bid/Build	07-Jun-13	14-Aug-15	0	98%	\$682,601	9.518%	Phase 4 (East Wing) is substantially complete. Phase 4 was the final renovation phase. Remaining work includes removal of the classroom modulars which will occur during the Summer of 2015.	\$4,620,410

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of July 10, 2015**

Core Program and Waitlist Totals			\$2,781,781,636														*Includes Alternates	\$1,714,468,572
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
Core Program Totals			\$2,779,805,553															\$1,708,982,133
Sutton Sutton Middle School	Junior High School	Brait Builders Corp.	\$41,230,800	840	PFA	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	01-Jul-11	30-Jun-15	0	99%	\$1,691,778	4.211%	Remaining site work is being completed at the baseball field and the previous location of the modular building site.	\$26,120,512
Wachusett Mountview Middle	Middle School	CTA Construction Co., Inc.	\$43,122,257	800	Bid	126,200	\$342	\$28,959,805	\$229	Design/Bid/Build	21-May-14	19-Apr-16	0	42%	\$58,725	0.136%	Masonry is complete in the academic building and windows are nearing completion. Insulated metal panel installation is complete in the academic wing and at 90% complete overall. Roofing system is nearing completion, with metal edge installation remaining. Roof top HVAC units are set except for an additional unit for a dehumidification system. Drywall installation is nearly complete on the 3rd floor and painting is underway. Mechanical/electrical installation is nearing completion with ceiling grid installation about to start. Metal stud installation is complete on the 1st floor. In the Cafeteria/Gym area, installation of slab on grade concrete has been completed. Site utility work continues with gas piping and electric ductbank. The Maintenance Building and diesel generator slab on grade foundations are underway.	\$24,279,591
Webster Park Avenue Elementary	Elementary School	CTA Construction Co., Inc.	\$32,370,001	720	Bid	109,597	\$295	\$24,190,915	\$221	Design/Bid/Build	08-Jul-13	06-Feb-15	0	95%	\$684,633	2.163%	Miscellaneous punch list items remain outstanding for the building and site. Site drainage system, playgrounds, bus loop, parking areas, site utilities, site lighting and front plaza retaining wall installations are ongoing.	\$28,102,666
West Bridgewater West Bridgewater Jr-Sr	Junior High School	CTA Construction Co., Inc.	\$46,267,000	625	Bid	141,250	\$328	\$34,404,274	\$244	Design/Bid/Build	01-Oct-13	15-Jun-15	22 behind	74%	\$307,797	0.678%	Interior finishes are being completed and final cleaning has started. Work continues on the punch list as well as completion of sound, security and fire alarm systems.	\$26,385,058
West Springfield West Springfield High	High School	Fontaine Brothers, Inc.	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	22-Nov-11	31-Dec-13	0	99%	\$2,932,683	4.162%	Punch list and field maintenance work continues. Site warranty issues are being addressed. The commissioning report is complete.	\$60,722,795
Westfield Abner Gibbs	Elementary School	Fontaine Brothers, Inc.	\$25,578,000	600	Bid	95,573	\$268	\$21,444,000	\$224	Design/Bid/Build	24-Aug-12	01-Jun-16	0	7%	\$0	0.000%	Work stoppage due to preliminary injunction based upon project site status as Article 97 "Protected Land". Preliminary Injunction vacated but city awaiting National Park Service approval for use of site. The General Contractor has demobilized from the site. The project team is working on closing out the General Contractor's contract.	\$21,281,639
Weston Field Elem School	Elementary School	Colantonio, Inc.	\$24,537,966	355	Bid	65,390	\$375	\$19,872,289	\$304	Design/Bid/Build	21-Dec-12	04-Aug-14	0	99%	\$2,107,241	8.588%	Final change order scope requires installation of a drywell in the paved area to address ponding issues. Remaining punch list items consist of mostly site work.	\$8,004,886
Williamsburg Anne T Dunphy	Elementary School	Enfield Builders, Inc.	\$8,990,457	170	Bid	37,859	\$237	\$7,625,327	\$201	Design/Bid/Build	05-Apr-13	29-Aug-14	0	100%	\$683,518	7.603%	Miscellaneous punch list work and warranty items continue to be addressed.	\$6,808,088
Auburn Auburn Middle	Middle School	Fontaine Brothers, Inc.	\$36,412,806	560	Bid	100,395	\$363	\$23,350,958	\$233	CM-at-Risk	27-Feb-14	07-Jul-15	0	93%	\$139,506	0.393%	Finishes are nearing completion. Major activity remaining is punch list work. Classroom wing is signed off and the Kitchen and Gym will be completed shortly. Final paving overlay and striping was completed at the end of June. Landscaping has been completed. Load bank test for the emergency generator was completed in June. Final elevator inspection/approval will be scheduled once telephone service is installed and verified. Locker installation is in progress.	\$19,761,870
Ayer-Shirley Ayer-Shirley Regional Middle/High School	High School	Consigli Construction Company, Inc.	\$44,516,576	495	Bid	144,072	\$309	\$32,082,505	\$223	CM-at-Risk	19-Feb-13	26-Aug-15	0	81%	\$806,953	1.819%	This is a 6-phase Addition/Renovation project. Phases 1a, 1b, 2a, 2b and 3a are complete and punch list work is ongoing. Phase 3b is underway and includes a new cafeteria and new front entry. Phase 3b was scheduled to be complete on June 17, 2015 but is currently behind schedule. However, the substantial completion date for this project is still on schedule.	\$34,704,031
Chelsea Clark Avenue School	Middle School	W.T. Rich Company Inc.	\$46,046,367	670	PFA	115,235	\$400	\$29,311,076	\$254	CM-at-Risk	23-Feb-15	29-Jun-18	0	0%	\$0	0.000%	Interior abatement work has begun on the building (Phase 1).	\$36,093,628
Concord-Carlisle Concord Carlisle High	High School	Turner Construction Company	\$76,143,704	1,225	Bid	219,871	\$346	\$53,607,000	\$244	CM-at-Risk	20-Feb-13	13-Feb-15	0	91%	\$2,059,669	2.705%	All building systems have been successfully started up and commissioned. Demolition, site work and close out are ongoing. Although some time was lost due to unforeseen abatement scope, the project remains on schedule.	\$26,795,748
Duxbury Duxbury High	Junior High School	Dimeo Construction Company	\$105,475,520	1,735	Bid	322,105	\$327	\$73,368,123	\$228	CM-at-Risk	12-Sep-12	09-Jun-14	0	95%	\$5,946,667	5.972%	Demolition work is complete. Site work at the former Middle School is ongoing with partial road placement, detention basins and other related site improvement installations. Site work is ongoing at the former High School with fill material work substantially complete and site drainage work underway.	\$48,141,830
Essex Agr Tech Essex Agr and Tech Inst	Vocational / Technical	Gilbane Building Company	\$110,217,451	1,440	Bid	337,000	\$327	\$79,334,889	\$235	CM-at-Risk	07-May-12	27-Aug-14	0	99%	\$3,018,720	2.739%	Punch list work is nearly complete. The HVAC System has outstanding control issues to be addressed. Sod has been placed at the Danvers field. Structural repairs to the Fish Barn continue.	\$72,471,233
Gloucester West Parish	Elementary School	W. T. Rich Company Inc.	\$29,995,466	355	PFA	65,679	\$457	\$18,591,872	\$283	CM-at-Risk	07-Jul-14	12-May-16	0	40%	\$69,627	0.232%	Building exterior work is ongoing including installation of brick veneer, precast concrete and roof blocking. Interior framing is ongoing on the third floor and the mechanical, electrical and plumbing trades are continuing to hang pipe and ductwork. All concrete slabs in the Academic wing are in place. Site utility work is progressing with water and sanitary work complete and underground electrical duct bank is also complete. Fabrication of windows and boilers is complete.	\$14,732,645
Greater Lowell Voc Tec Gr Lowell Reg Voc Tech	Vocational / Technical	Consigli Construction Company, Inc.	\$52,472,010	1,990	Bid	505,766	\$104	\$38,997,643	\$77	CM-at-Risk	04-Nov-13	31-Aug-15	0	79%	\$2,233,471	4.257%	This is a 3-phase Addition/Renovation project currently in Phase 1. Phase 1 is the addition of a new Café and Kitchen. The addition of the new Cafeteria is complete and was turned over to the District on February 23, 2015. The new kitchen has also been turned over. The 3rd floor Commons being converted to Science Labs: work is progressing, cabinetry and finishes are currently being installed. Expected turnover date is June 1, 2015. The new classrooms that occupy the old Testing space and the swing space adjacent to the Discipline Office have been completed and turned over for use to the school. The 2nd floor science labs being renovated: CM took over the spaces during the April school vacation for demolition and abatement. Work is ongoing in these areas.	\$45,839,013
Greenfield Greenfield High	High School	Shawmut Design and Construction	\$53,507,787	585	Bid	160,650	\$333	\$37,812,150	\$235	CM-at-Risk	27-Mar-13	15-Dec-15	0	84%	\$769,522	1.438%	The main school building is complete and in service. The remaining building work consisting of a new 2-story science lab wing, new Gym, new Locker Rooms, new Band Room, and renovated Auditorium is on schedule for completing by the end of August 2015. Athletic fields are scheduled for completion in the Fall of 2015.	\$42,146,257
Haverhill Caleb Dustin Hunking	Middle School	Shawmut Design and Construction	\$58,998,100	1,005	PFA	147,996	\$399	\$34,446,742	\$233	CM-at-Risk	20-Apr-15	30-Dec-16	0	1%	\$0	0.000%	Tree removal is complete. Footing and foundation work are ongoing. Structural steel deliveries commenced in July.	\$39,639,497
Lunenburg Lunenburg High	Junior High School	Shawmut Design and Construction	\$59,570,728	820	PFA	169,018	\$352	\$39,057,924	\$231	CM-at-Risk	15-Aug-14	25-Mar-16	0	32%	\$51,378	0.086%	Slab on grade installation is nearing completion. Air vapor barrier and spray fireproofing installations are underway throughout the building. Gym, Auditorium and Locker Room area masonry installations are underway. Rough mechanical electrical and plumbing work is also underway. Flat roof installation is nearing completion.	\$34,075,598
Lynn Thurgood Marshall Mid	Middle School	Walsh Brothers, Inc.	\$67,725,244	1,100	PFA	181,847	\$372	\$49,913,764	\$274	CM-at-Risk	27-Jun-14	06-Jun-16	0	49%	\$0	0.000%	MEP and architectural finishes are being completed in Building A. Envelope, interior framing, and MEP rough-ins are ongoing in Building B. Exterior framing and fireproofing are being completed in Building C. Site work includes soil removal, utility preparation and pole relocation.	\$49,690,902
Milford Woodland	Elementary School	Shawmut Design and Construction	\$48,381,844	985	PFA	132,539	\$365	\$31,853,445	\$240	CM-at-Risk	01-Apr-15	28-Jul-16	0	10%	\$0	0.000%	Building excavation, foundations, and frost walls are complete. Structural steel is complete in Building C and ongoing in Buildings B & A. Roofing is complete in Building C and ongoing in Building B. Exterior framing, sheathing, and air vapor barrier installations have begun in Building C.	\$27,564,734
Newburyport Rupert A Nock Middle	Middle School	Gilbane Building Company	\$20,877,414	845	PFA	161,500	\$129	\$14,924,391	\$92	CM-at-Risk	18-Mar-13	10-Oct-14	0	99%	\$2,036,392	9.754%	Miscellaneous punch list items are remaining to be completed.	\$12,785,667
Newton A E Angier	Elementary School	W. T. Rich Company Inc.	\$30,179,957	465	PFA	74,960	\$403	\$16,758,548	\$224	CM-at-Risk	22-Aug-14	18-Dec-15	0	33%	(\$10,570)	-0.040%	Framing, utility work and MEP rough-ins are in progress. All trades are working on Saturdays and electricians are working additional hours.	\$10,839,093
North Reading North Reading High	Junior High School	Gilbane Building Company	\$101,328,353	1,370	Bid	267,939	\$378	\$66,726,592	\$249	CM-at-Risk	01-May-12	31-Aug-15	0	92%	\$2,754,052	2.718%	Middle school roof installation is nearing completion with edge flashing remaining. Academic area is most advanced towards completion with painting touch ups required followed by cleanup. Casework deliveries and assembly are underway. Lavatory partitions and electrical finishes are progressing. The Superintendent's addition is less complete with drywall completion and floor installation required. Exterior work progresses in the tennis courts with the base material set for paving. Curbing has been installed along with loam and planting of trees. Abatement and demolition of the old high school is scheduled to begin in July.	\$47,071,882
Norton Norton High	High School	W. T. Rich Company Inc.	\$27,023,541	700	Bid	162,000	\$167	\$20,590,559	\$127	CM-at-Risk	12-Mar-12	31-Jan-14	0	100%	\$1,366,532	5.131%	Roof top unit punch list issue is ongoing. The closeout process including the final change orders are pending resolution of a roof top unit noise and vibration issue.	\$20,634,829

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of July 10, 2015**

Core Program and Waitlist Totals			\$2,781,781,636															*Includes Alternates	\$1,714,468,572
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																			
Core Program Totals			\$2,779,805,553																\$1,708,982,133
Southern Worcester Cty VT Bay Path Reg Voc Tech H S	Vocational / Technical	Consigli Construction Company, Inc.	\$57,024,455	1,110	Bid	249,521	\$229	\$41,468,049	\$166	CM-at-Risk	02-Aug-13	01-Sep-15	0	82%	\$2,179,782	3.848%	Project is currently in Phase 9 of a 10-phase project. Phase 1 and 2 includes a new addition that houses the vocational shops, Science Rooms, Admin Space and a Restaurant/Kitchen. Phases 1-8 are complete other than punch list work. Phase 9 began on June 23, 2015. Phase 10 is scheduled to begin in August, 2015.	\$44,420,530	
Springfield Elias Brookings	Elementary School	Morganti/Aquadro & Cerruti	\$22,733,394	320	Bid	64,800	\$351	\$18,337,328	\$283	CM-at-Risk	01-Jul-13	20-Jan-15	0	100%	\$183,205	0.806%	Punch list and warranty items are being addressed.	\$25,563,992	
Stoneham Stoneham Middle School	Middle School	Shawmut Design and Construction	\$33,086,864	775	Bid	136,410	\$243	\$23,430,771	\$172	CM-at-Risk	01-Nov-12	08-Aug-14	0	99%	\$933,834	2.822%	Miscellaneous punch list work is remaining to be completed.	\$21,346,937	
Wakefield Galvin Middle School	Middle School	Bond Brothers, Inc.	\$59,756,584	1,070	Bid	187,773	\$318	\$44,899,853	\$239	CM-at-Risk	18-Mar-13	30-Jun-15	0	89%	\$3,156,802	5.283%	The main school building and Auditorium have been completed and are in service. The remaining building work including a new Gym, Locker Rooms, and Music Room are progressing on schedule for completion along with final site work in the Summer of 2015.	\$32,519,108	
Wilmington Wilmington High	High School	Gilbane Building Company	\$67,558,835	960	Bid	192,443	\$351	\$48,060,314	\$250	CM-at-Risk	30-Apr-13	12-Feb-15	0	86%	\$1,901,566	2.943%	Existing high school building has been demolished and removed. Site work has begun. Punch list items are to be completed over the summer in the New High School.	\$35,674,893	
Winchester Winchester High School	High School	Consigli Construction Company, Inc.	\$101,118,622	1,370	PFA	278,925	\$363	\$60,656,324	\$217	CM-at-Risk	23-Apr-14	31-Aug-17	0	36%	\$869,481	0.861%	Phase 1 construction of a new main entrance, administration offices, music wing, kitchen, cafeteria, and media center is progressing on schedule for completion and occupancy in September 2015. As a result of the extreme past winter conditions and unforeseen existing conditions, the completion of renovations to the Auditorium have been delayed from September 1, 2015 to October 23, 2015 which has no adverse impact on school operations. Phase 2 and 3 construction are scheduled for completion in August 2016 and August 2017, respectively.	\$42,106,263	
Winthrop Winthrop Sr High	Junior High School	Gilbane Building Company	\$63,542,179	970	PFA	187,917	\$338	\$42,616,843	\$227	CM-at-Risk	01-Jul-14	19-Jul-16	0	30%	\$0	0.000%	Structural work has been completed in most of the building. Roofing, framing, fireproofing and electrical work are in progress. Installation of exterior brick has started.	\$39,559,238	
Waitlist Totals			\$1,976,083				\$4		\$4										
New Bedford New Bedford High	High School	Sparks Company, Inc.	\$1,976,083	4,000	PFA	454,028	\$4	\$1,669,516	\$4	Design/Bid/Build	27-Aug-14	15-May-15	61 behind	94%	\$0	0.000%	Change Order work for door replacement and bus canopy remain to be completed. Work on miscellaneous punch list items continues.	\$5,486,439	
